

Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Eternity Lane Channel

Activity: Routine/Preventive Maintenance

Duration: 03/03/2022 - 04/13/2022

Narrative Description of Project:

Project improved 935 L.F. of drainage system. Grubbed and cleared 1,050 L.F. of workshelf by sub-contractor. Reconstructed and cleaned out 935 L.F. of channel ditch. Installed (2) access pipes, (2) bleeder pipes, rip rap and hydroseeded for erosion control.

2022-550 / Eternity Lane Channel	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
APINS / Access pipe - installed	72.00	\$1,885.92	\$555.70	\$729.80	\$0.00	\$1,320.80	\$4,492.22
AUDIT / Audit Project	5.00	\$163.70	\$0.00	\$0.00	\$0.00	\$101.05	\$264.75
BKFILL / Back Fill	24.00	\$739.72	\$146.61	\$138.03	\$0.00	\$490.20	\$1,514.56
BPINST / Bleeder pipe - Installed	24.00	\$790.40	\$316.61	\$238.05	\$0.00	\$512.48	\$1,857.54
CCO / Channel - cleaned out	88.00	\$2,689.04	\$1,233.82	\$364.38	\$0.00	\$1,403.20	\$5,690.44
DEBRIS / Debris Removal	68.00	\$1,579.12	\$601.53	\$318.72	\$0.00	\$1,186.12	\$3,685.49
GRDNRD / Grading - non-roads	24.00	\$695.04	\$290.20	\$137.10	\$0.00	\$471.84	\$1,594.18
HAUL / Hauling	201.00	\$6,151.08	\$3,678.58	\$5,487.70	\$0.00	\$3,363.34	\$18,680.70
HEQ / Haul equipment	28.00	\$782.88	\$398.60	\$268.80	\$0.00	\$382.32	\$1,832.60
HYDR / Hydroseeding	16.00	\$479.44	\$75.62	\$1,005.56	\$0.00	\$321.44	\$1,882.06
LM / Loading Materials	16.00	\$520.56	\$371.76	\$96.84	\$0.00	\$337.52	\$1,326.68

Continued on the next page


2022-550 / Eternity Lane Channel cont'd	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
NONPRO / Non-Professional Services	0.00	\$0.00	\$0.00	\$0.00	\$49,200.00	\$0.00	\$49,200.00
RMTRW / Remove trees - Workshelf	16.00	\$438.32	\$34.80	\$46.76	\$0.00	\$305.36	\$825.24
RRI / Rip Rap - Installed	16.00	\$438.32	\$34.80	\$26.72	\$0.00	\$272.40	\$772.24
SG / Shoot Grade	16.00	\$438.32	\$34.80	\$30.06	\$0.00	\$272.40	\$775.58
WSDR / Workshelf - Dressed	32.00	\$876.64	\$69.60	\$94.40	\$0.00	\$577.76	\$1,618.40
WSGRB / Workshelf - Grubbed	16.00	\$520.56	\$371.76	\$179.32	\$0.00	\$337.52	\$1,409.16
WSL / Workshelf - Level	56.00	\$1,414.40	\$762.97	\$211.54	\$0.00	\$692.32	\$3,081.23
Grand Total	718.00	\$20,603.46	\$8,977.76	\$9,373.77	\$49,200.00	\$12,348.07	\$100,503.06

Before During After







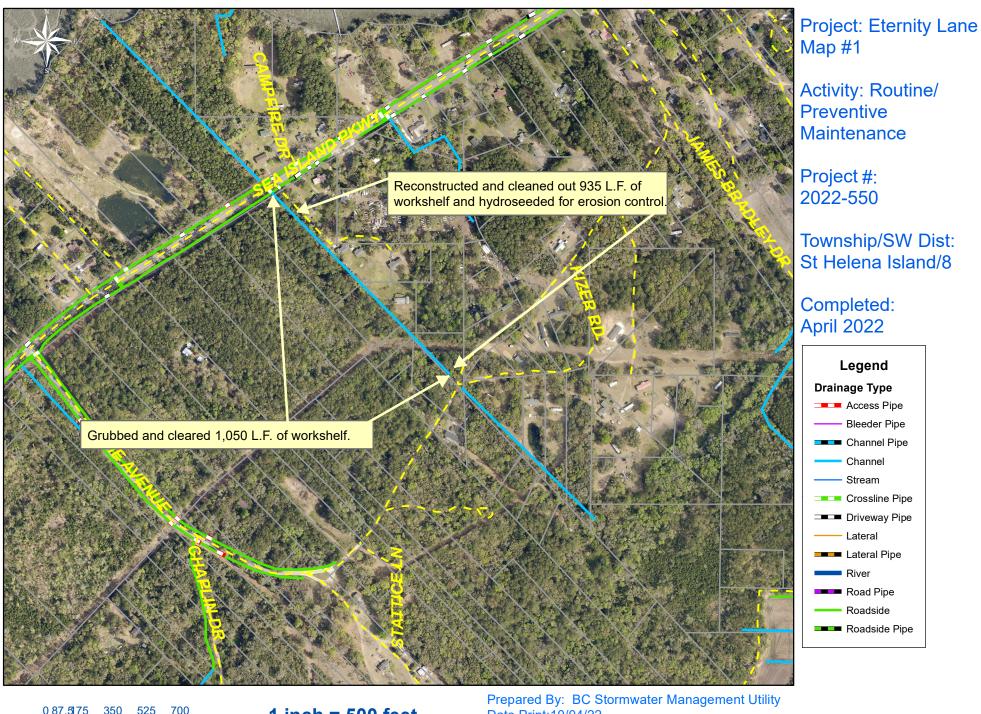


0 87.5175 350

1 inch = 500 feet

Date Print: 10/04/22

File:C:\project summaries map/Eternite Ln Map#1 2022-550

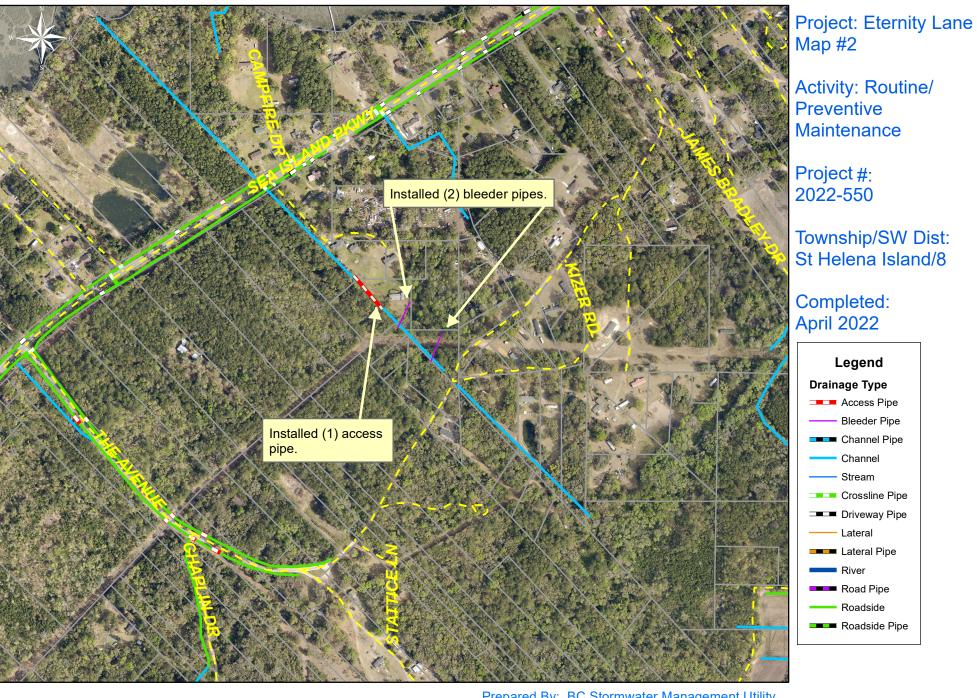

Prepared By: BC Stormwater Management Utility Date Print: 10/04/22

File:C:\project summaries map/Eternite Ln Map#2_2022-550

Legend **Drainage Type** Access Pipe Bleeder Pipe

Channel Pipe Channel Stream Crossline Pipe ■ Driveway Pipe Lateral Lateral Pipe River Road Pipe Roadside Roadside Pipe



Project: Eternity Lane Map #3

Activity: Routine/ Preventive Maintenance

Project #: 2022-550

Township/SW Dist: St Helena Island/8

Completed: April 2022

Legend Drainage Type Access Pipe Bleeder Pipe Channel Pipe Channel Stream Crossline Pipe Lateral Lateral Pipe River Roadside Roadside Pipe

1 inch = 500 feet

0 87.5175 350

Prepared By: BC Stormwater Management Utility Date Print:10/04/22

File:C:\project summaries map/Eternite Ln Map#3_2022-550
