

Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: LH Nelson Drive Subdivision - LH Nelson Drive, Hale Drive,

Jefferson Drive and Grant Street **Duration:** 12/22/20 - 03/09/21

Narrative Description of Project:

Project improved 8,738 L.F. of drainage system. Road swept 8,738 L.F. Removed blockage from flowline. Cleaned out 4,700 L.F. of roadside ditch. Jetted (2) catch basins, (3) access pipes, (6) crossline pipes and (38) driveway pipes.


2021-526 / LH Nelson Drive	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
CBCO / Catch basin - clean out	24.0	\$512.40	\$341.36	\$72.08	\$0.00	\$229.44	\$1,155.28
CLPJT / Crossline Pipe - Jetted	24.0	\$530.28	\$306.56	\$86.30	\$0.00	\$197.64	\$1,120.78
RDSW / Street/Road Sweep	48.0	\$1,025.92	\$366.88	\$83.08	\$0.00	\$211.68	\$1,687.56
DEBREM / Debris Removal - Jobsite	8.0	\$164.40	\$74.57	\$4.40	\$0.00	\$50.88	\$294.25
DPJT / Driveway Pipe - Jetted	92.0	\$2,045.18	\$1,365.28	\$347.34	\$0.00	\$934.80	\$4,692.60
HAUL / Hauling	78.0	\$1,714.02	\$1,486.68	\$332.20	\$0.00	\$432.60	\$3,965.50
RSDCL / Roadside Ditch - Cleanout	182.0	\$3,895.16	\$947.10	\$271.67	\$0.00	\$820.26	\$5,934.19
UTLOC / Utility locates	1.0	\$24.70	\$0.00	\$0.00	\$0.00	\$13.23	\$37.93
2021-526 / LH Nelson Drive Project Sub Total	458.5	\$9,944.74	\$4,888.43	\$1,197.07	\$0.00	\$2,890.53	\$18,920.77
Grand Total	458.5	\$9,944.74	\$4,888.43	\$1,197.07	\$0.00	\$2,890.53	\$18,920.77
Before		During			I	Ending	







Activity: Routine/Preventive Maintenance

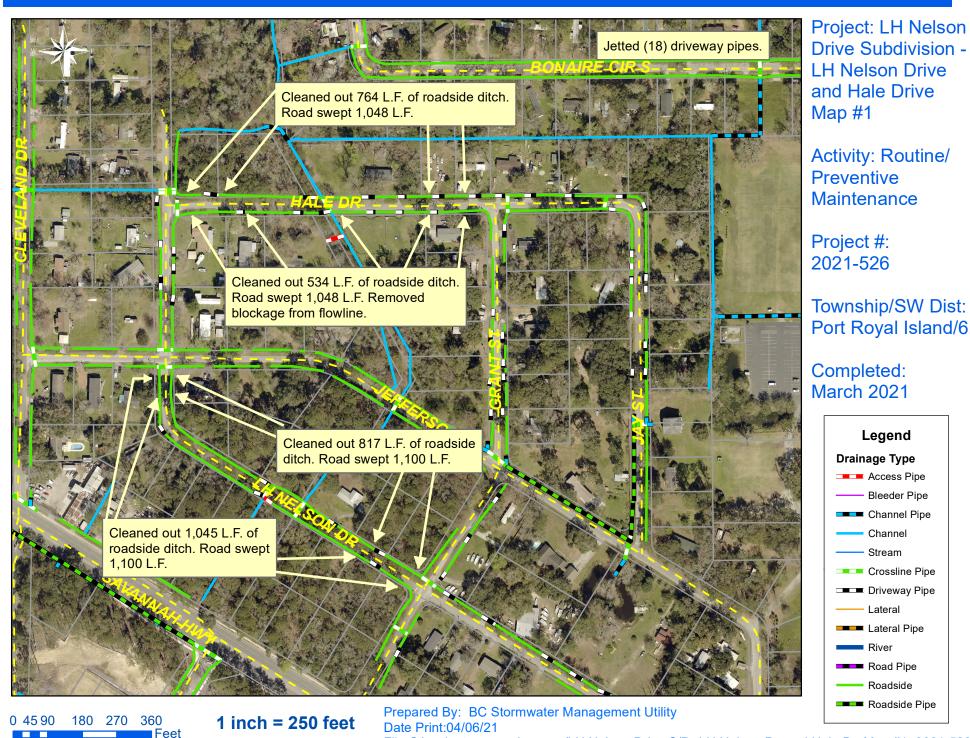

File:C:\project summaries map/LH Nelson Drive S/D- LH Nelson Dr. and Hale Dr. Map #1_2021-526

Legend

Channel

Stream

Crossline Pipe □■□■ Driveway Pipe Lateral Lateral Pipe River Road Pipe Roadside Roadside Pipe

Drainage Type Access Pipe Bleeder Pipe Channel Pipe

