



# Beaufort County Public Works

## Stormwater Infrastructure

### Project Summary

**Project Summary:** Colonial Heights - Pulaski Drive Phase V

**Narrative Description of Project:**

**Completion:** Apr-11

Project improved 1,719 L.F. of drainage system. Grubbed, cleared and cleaned out 825 L.F. of outfall ditch and 437 L.F. of lateral ditch. Repaired washout. Installed 377 L.F. of lateral pipe, 80 L.F. of outfall pipe, (3) bleeder pipes, rip rap and hydroseeded for erosion control.

2011-047D / Colonial Heights-Pulaski Drive Phase V	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	3.0	\$61.44	\$0.00	\$0.00	\$0.00	\$0.00	\$61.44
BKFILL / Back Fill	48.0	\$983.04	\$848.76	\$237.00	\$0.00	\$0.00	\$2,068.80
BPINST / Bleeder pipe - Installed	71.0	\$1,598.03	\$235.53	\$813.20	\$0.00	\$0.00	\$2,646.76
COMP / Compile Project	4.5	\$92.16	\$0.00	\$0.00	\$0.00	\$0.00	\$92.16
EDO / Equipment Drop Off	7.0	\$154.02	\$42.88	\$37.47	\$0.00	\$0.00	\$234.37
HAUL / Hauling	198.5	\$4,258.94	\$2,820.19	\$6,896.15	\$0.00	\$0.00	\$13,975.27
HYDR / Hydroseeding	34.0	\$696.32	\$216.24	\$878.39	\$0.00	\$0.00	\$1,790.95
LM / Loading Materials	7.0	\$149.94	\$223.04	\$48.58	\$0.00	\$0.00	\$421.56
ODCO / Outfall ditch - cleaned out	50.0	\$1,069.34	\$206.69	\$60.58	\$0.00	\$0.00	\$1,336.61
ODGRB / Outfall ditch - grubbed	53.0	\$1,138.45	\$416.28	\$260.86	\$0.00	\$0.00	\$1,815.59
OFPI / Outfall Pipe - Installation	104.0	\$2,306.49	\$413.38	\$4,455.43	\$0.00	\$0.00	\$7,175.30
RMTRW / Remove trees - Workshelf	24.0	\$514.72	\$127.31	\$77.03	\$0.00	\$0.00	\$719.06
TR / Trash Removal	45.0	\$1,001.24	\$321.50	\$139.14	\$0.00	\$0.00	\$1,461.88
TRCT / Tree cutting	45.0	\$1,014.43	\$180.87	\$64.65	\$4,600.00	\$0.00	\$5,859.95
WSGRB / Workshelf - Grubbed	234.0	\$5,146.77	\$1,497.94	\$581.97	\$0.00	\$0.00	\$7,226.68
WSL / Workshelf - Level	48.0	\$983.04	\$811.28	\$257.13	\$0.00	\$0.00	\$2,051.45
Indirect Labor, Services and Supplies	0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$14,193.92	\$14,193.92
<b>2011-047D / Colonial Heights-Pulaski Drive Phase V</b>	<b>976.0</b>	<b>\$21,168.37</b>	<b>\$8,361.88</b>	<b>\$14,807.57</b>	<b>\$4,600.00</b>	<b>\$14,193.92</b>	<b>\$63,131.74</b>
<b>Sub Total</b>							
<b>Grand Total</b>	<b>976.0</b>	<b>\$21,168.37</b>	<b>\$8,361.88</b>	<b>\$14,807.57</b>	<b>\$4,600.00</b>	<b>\$14,193.92</b>	<b>\$63,131.74</b>

Before



During



After




Project: Colonial Heights - Pulaski Drive Phase V

Activity: Drainage Maintenance

Project #: 2011-047D

Township: Port Royal Island

Completed: April 2011

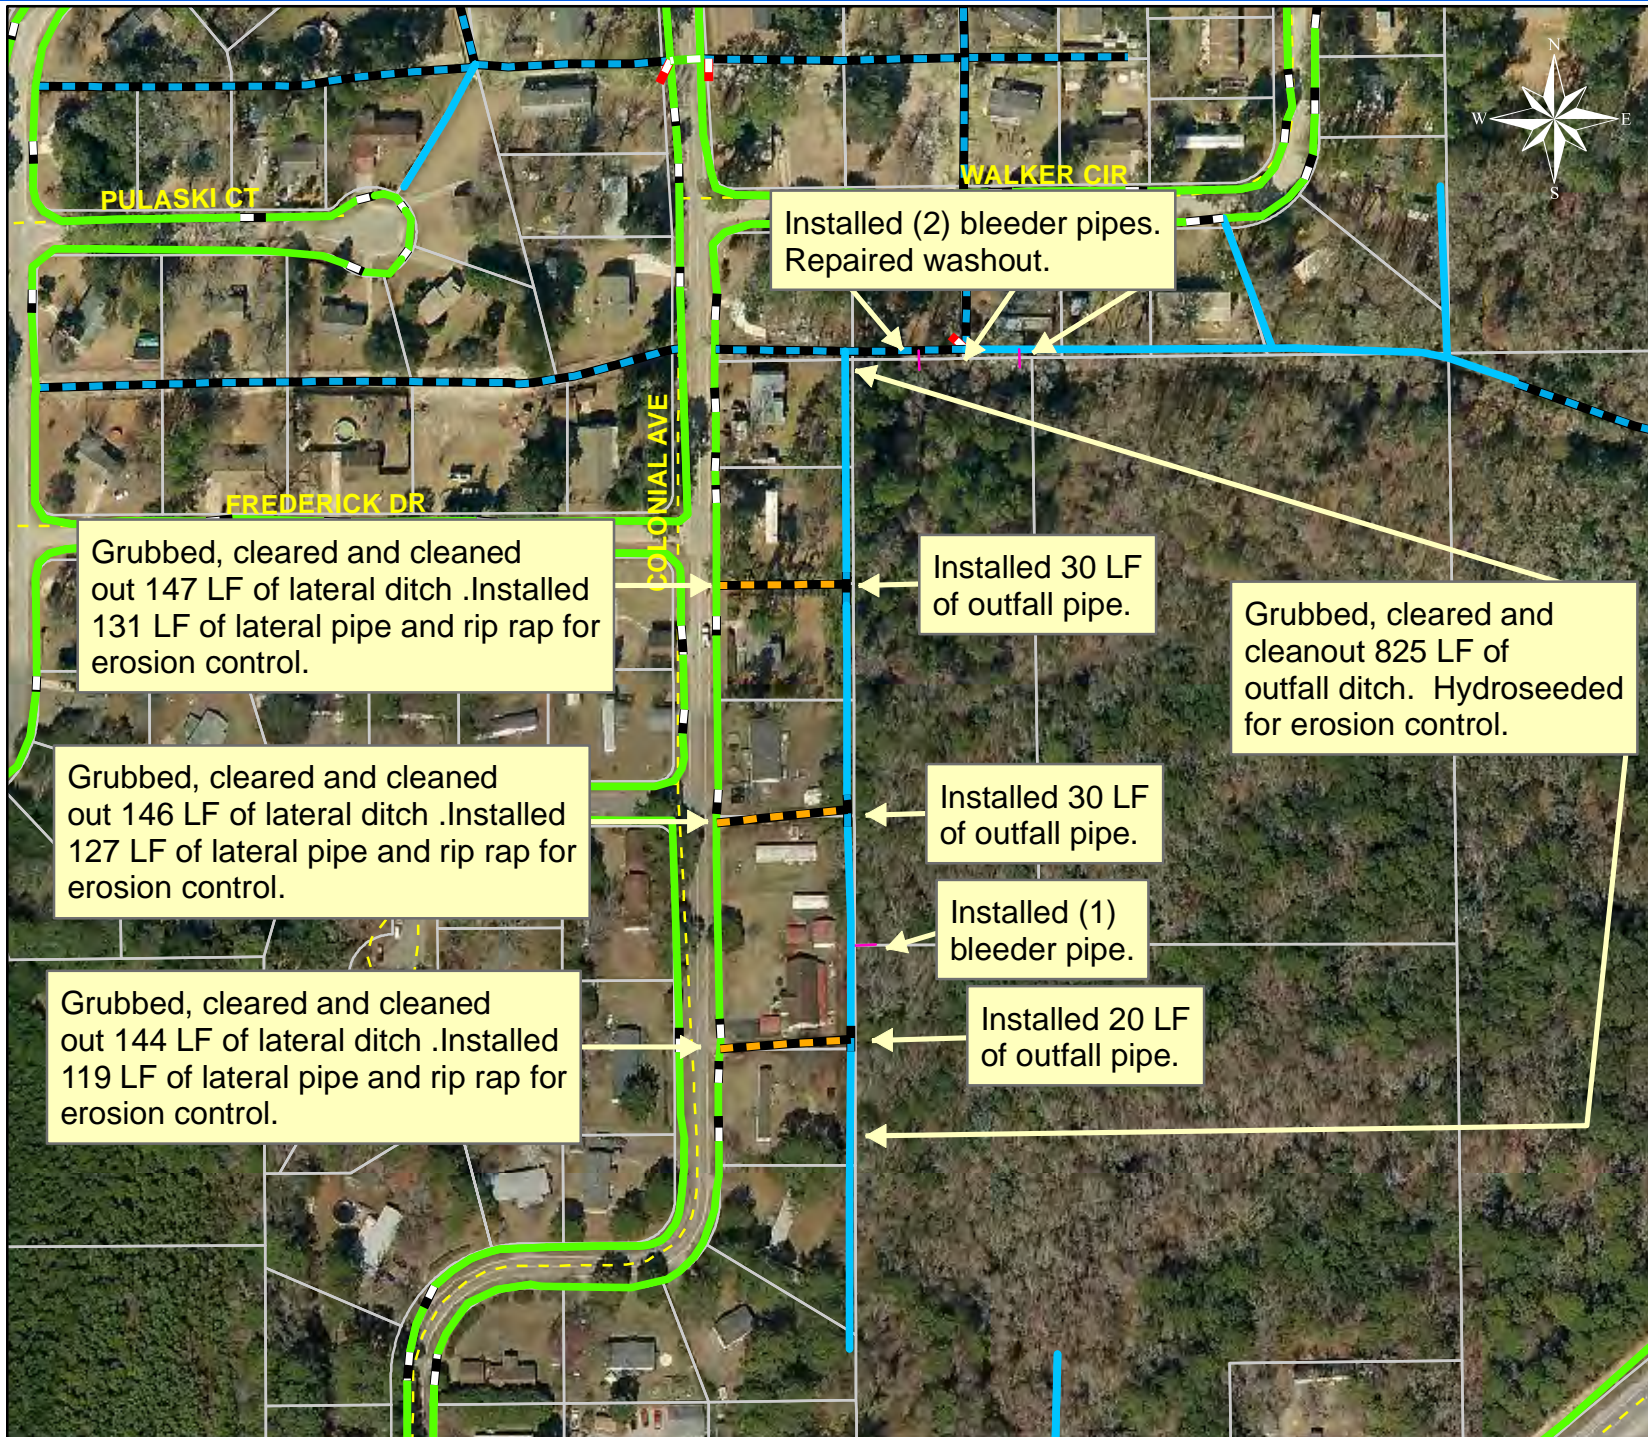

Legend	
Drainage Type	
	River
	Stream
	Outfall
	Lateral
	Lateral Pipe
	Roadside
	Roadside Pipe
	Road Pipe
	Crossline
	D/W
	Access
	Piped
	Bleeder
	Parcels



1 inch = 215 feet
