



Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: Westwood Circle

Narrative Description of Project:

Completion: Nov-12

Project improved 1,779 L.F. of drainage system. Cleaned out 100 L.F. of outfall ditch, 1,647 L.F. of roadside ditch and (1) catch basin. Jetted (2) crossline pipes, (15) driveway pipes and 32 L.F. of roadside pipe. Hydroseeded for erosion control.

2013-564 / Westwood Circle	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	1.0	\$20.89	\$0.00	\$0.00	\$0.00	\$13.23	\$34.12
CLPJT / Crossline Pipe - Jetted	10.0	\$237.50	\$221.60	\$65.60	\$0.00	\$164.70	\$689.40
DPJT / Driveway Pipe - Jetted	40.0	\$873.80	\$443.20	\$129.37	\$0.00	\$329.40	\$1,775.77
HAUL / Hauling	88.0	\$1,922.80	\$877.40	\$326.61	\$0.00	\$1,211.50	\$4,338.31
ODCO / Outfall ditch - cleaned out	30.0	\$664.80	\$162.44	\$31.58	\$0.00	\$317.40	\$1,176.22
RSDCL / Roadside Ditch - Cleanout	137.0	\$3,079.83	\$883.34	\$281.45	\$0.00	\$1,575.01	\$5,819.63
UTLOC / Utility locates	0.5	\$10.45	\$0.00	\$0.00	\$0.00	\$6.62	\$17.06
2013-564 / Westwood Circle Sub Total	306.5	\$6,810.07	\$2,587.98	\$834.61	\$0.00	\$3,617.86	\$13,850.51
Grand Total	306.5	\$6,810.07	\$2,587.98	\$834.61	\$0.00	\$3,617.86	\$13,850.51

Before



During



After



Project: Westwood Circle Map 1

Activity: Drainage Maintenance














Project #: 2013-564


Township: Port Royal Island

Completed: November 2012

Legend

Drainage Type

-  River
-  Stream
-  Outfall
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Crossline
-  D/W
-  Access
-  Piped
-  Bleeder
-  Parcels

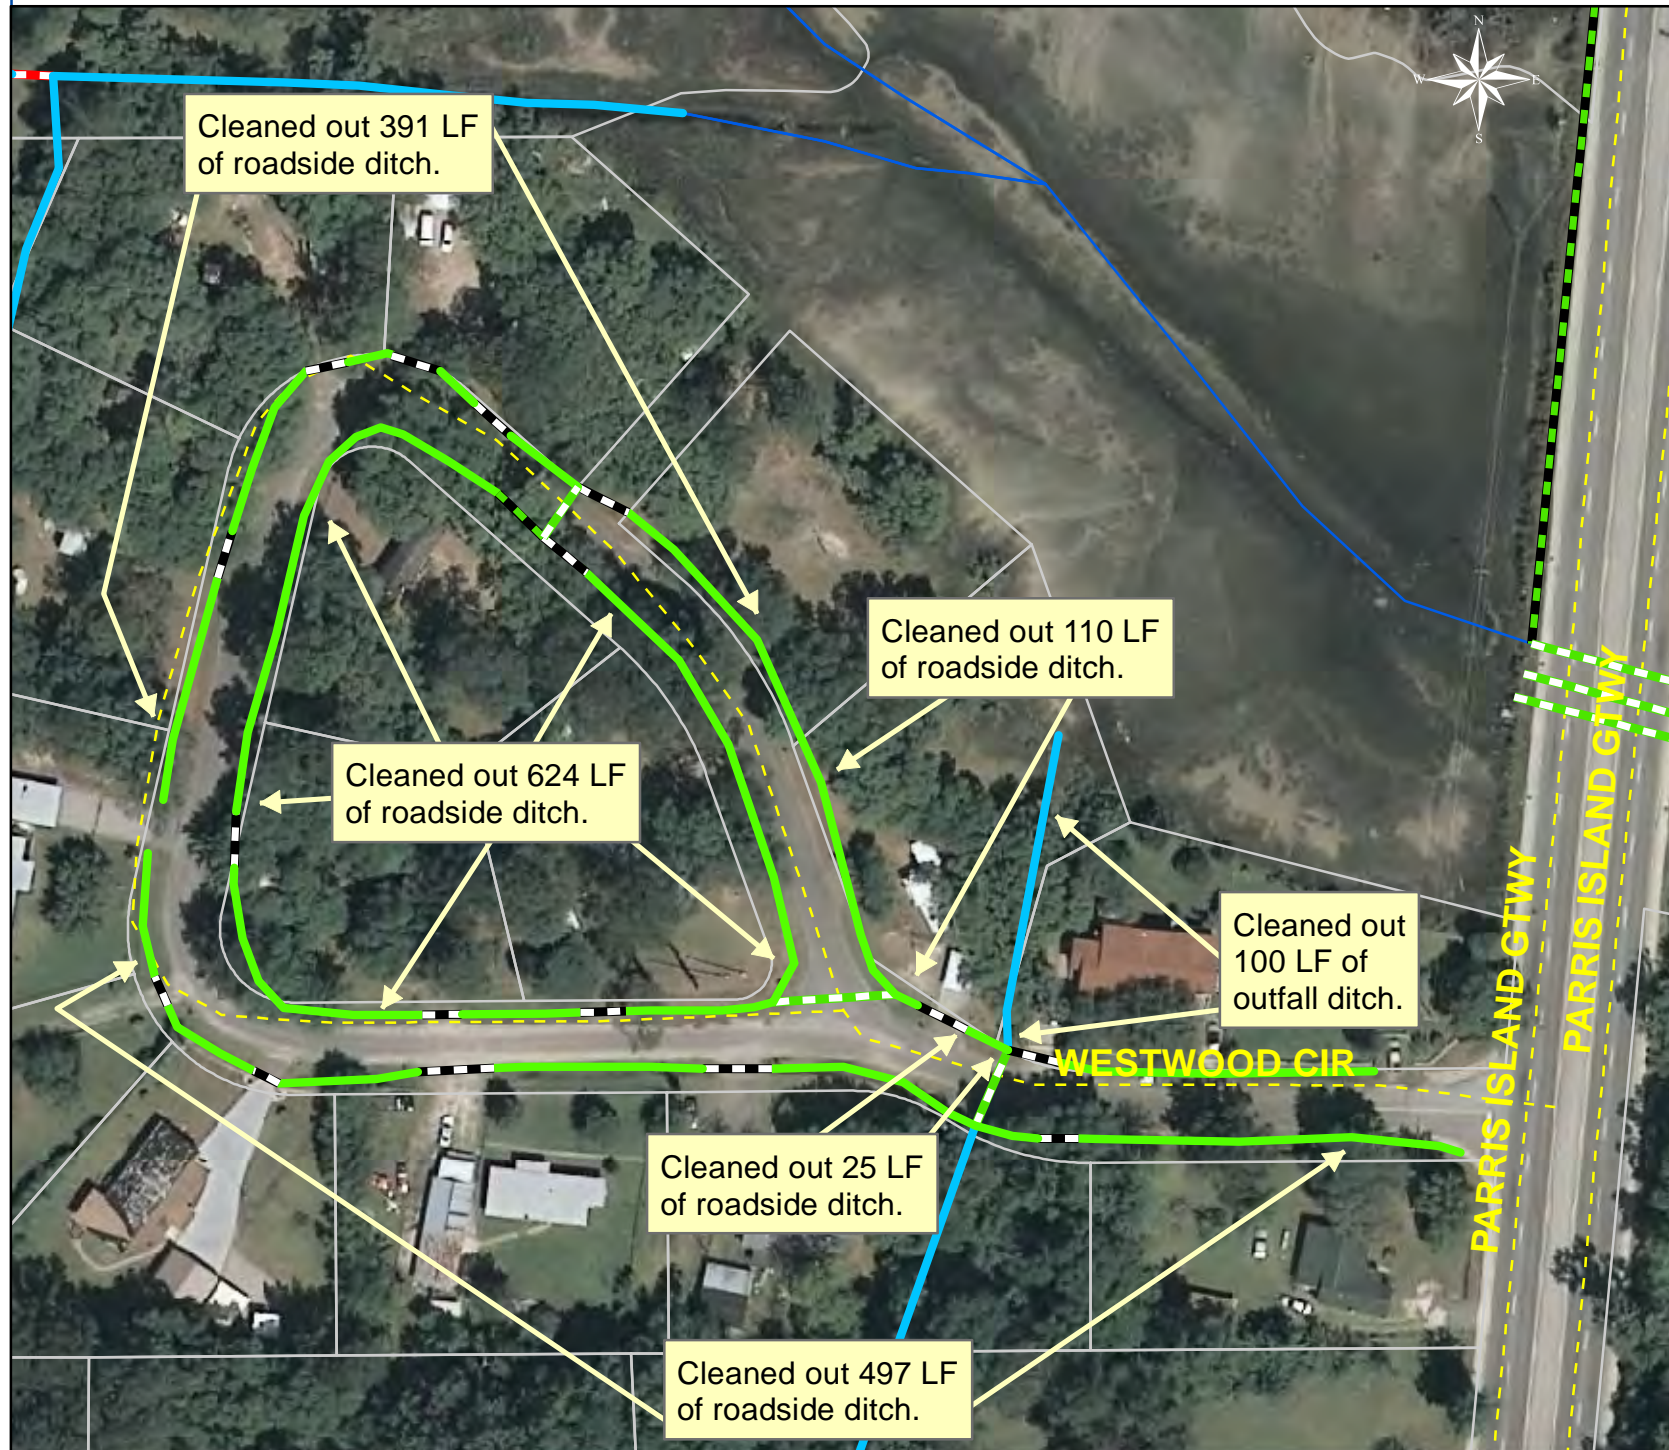

Cleaned out 391 LF of roadside ditch.

Cleaned out 110 LF of roadside ditch.

Cleaned out 624 LF of roadside ditch.

Cleaned out 100 LF of outfall ditch.

Cleaned out 25 LF of roadside ditch.

Cleaned out 497 LF of roadside ditch.



1 inch = 104 feet

Project: Westwood Circle Map 2

Activity: Vacuum Truck

Project #: 2013-564

Township: Port Royal Island

Completed: November 2012














Jetted (15) driveway pipes.

Jetted (2) crossline pipes.

Cleaned out (1) catch basin and 32 LF of roadside pipe.

Legend

Drainage Type

-  River
-  Stream
-  Outfall
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Crossline
-  D/W
-  Access
-  Piped
-  Bleeder
-  Parcels



1 inch = 104 feet
