



Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: Pinckney Colony Road Channel #1

Activity: Routine/Preventive Maintenance

Narrative Description of Project:

Project improved 5,205 L.F. of drainage system. Bush hogged 3,530 L.F. of channel. Cleaned out 5,205 L.F. of channel. Installed (7) access pipes and rip rap for erosion control. Jetted (2) crossline pipes and (7) access pipes.


Completion: Jul-14

2014-631 / Pinckney Colony Rd Channel #1	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
APINS / Access pipe - installed	59.5	\$1,313.11	\$390.48	\$1,045.78	\$0.00	\$873.84	\$3,623.21
APJT / Access pipe - jetted	10.0	\$223.38	\$110.80	\$47.70	\$0.00	\$149.55	\$531.43
AUDIT / Audit Project	1.0	\$20.46	\$0.00	\$0.00	\$0.00	\$13.23	\$33.69
DLO / Ditch Layout	15.0	\$331.62	\$18.10	\$27.21	\$0.00	\$220.80	\$597.73
HAUL / Hauling	63.0	\$1,344.78	\$642.00	\$1,025.91	\$0.00	\$875.88	\$3,888.57
LM / Loading Materials	30.0	\$687.90	\$363.82	\$174.95	\$0.00	\$463.95	\$1,690.62
ODBH / Outfall ditch - bushhogged	58.0	\$1,289.73	\$526.18	\$313.92	\$0.00	\$860.76	\$2,990.59
ODCO / Outfall ditch - cleaned out	219.0	\$4,873.13	\$1,942.04	\$991.34	\$0.00	\$3,252.51	\$11,059.01
ONJV / Onsite Job Visit	19.5	\$635.12	\$61.54	\$67.20	\$0.00	\$452.58	\$1,216.44
PP / Project Preparation	3.0	\$132.81	\$10.86	\$12.80	\$0.00	\$101.88	\$258.35
PROFS / Professional Services	0.0	\$0.00	\$0.00	\$0.00	\$109.35	\$0.00	\$109.35
RRI / Rip Rap - Installed	20.0	\$458.60	\$195.24	\$123.15	\$0.00	\$309.30	\$1,086.29
STAGING / Staging Materials	6.0	\$137.58	\$10.86	\$26.16	\$0.00	\$92.79	\$267.39
STBY / Stand By	2.0	\$43.26	\$21.40	\$29.43	\$0.00	\$28.84	\$122.93
TRAIN / Training	2.0	\$38.56	\$0.00	\$0.00	\$0.00	\$24.42	\$62.98
WSGRB / Workshelf - Grubbed	18.0	\$397.92	\$61.48	\$27.70	\$0.00	\$264.96	\$752.06
2014-631 / Pinckney Colony Rd Channel #1 Sub Total	526.0	\$11,927.96	\$4,354.80	\$3,913.23	\$109.35	\$7,985.29	\$28,290.63
Grand Total	526.0	\$11,927.96	\$4,354.80	\$3,913.23	\$109.35	\$7,985.29	\$28,290.63

Before



During

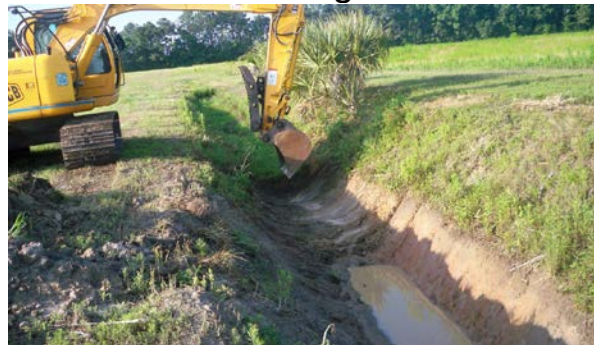

After




Project: Pinckney Colony Road Map 1

Activity: Routine/
Preventive
Maintenance

Project #:
2014-631





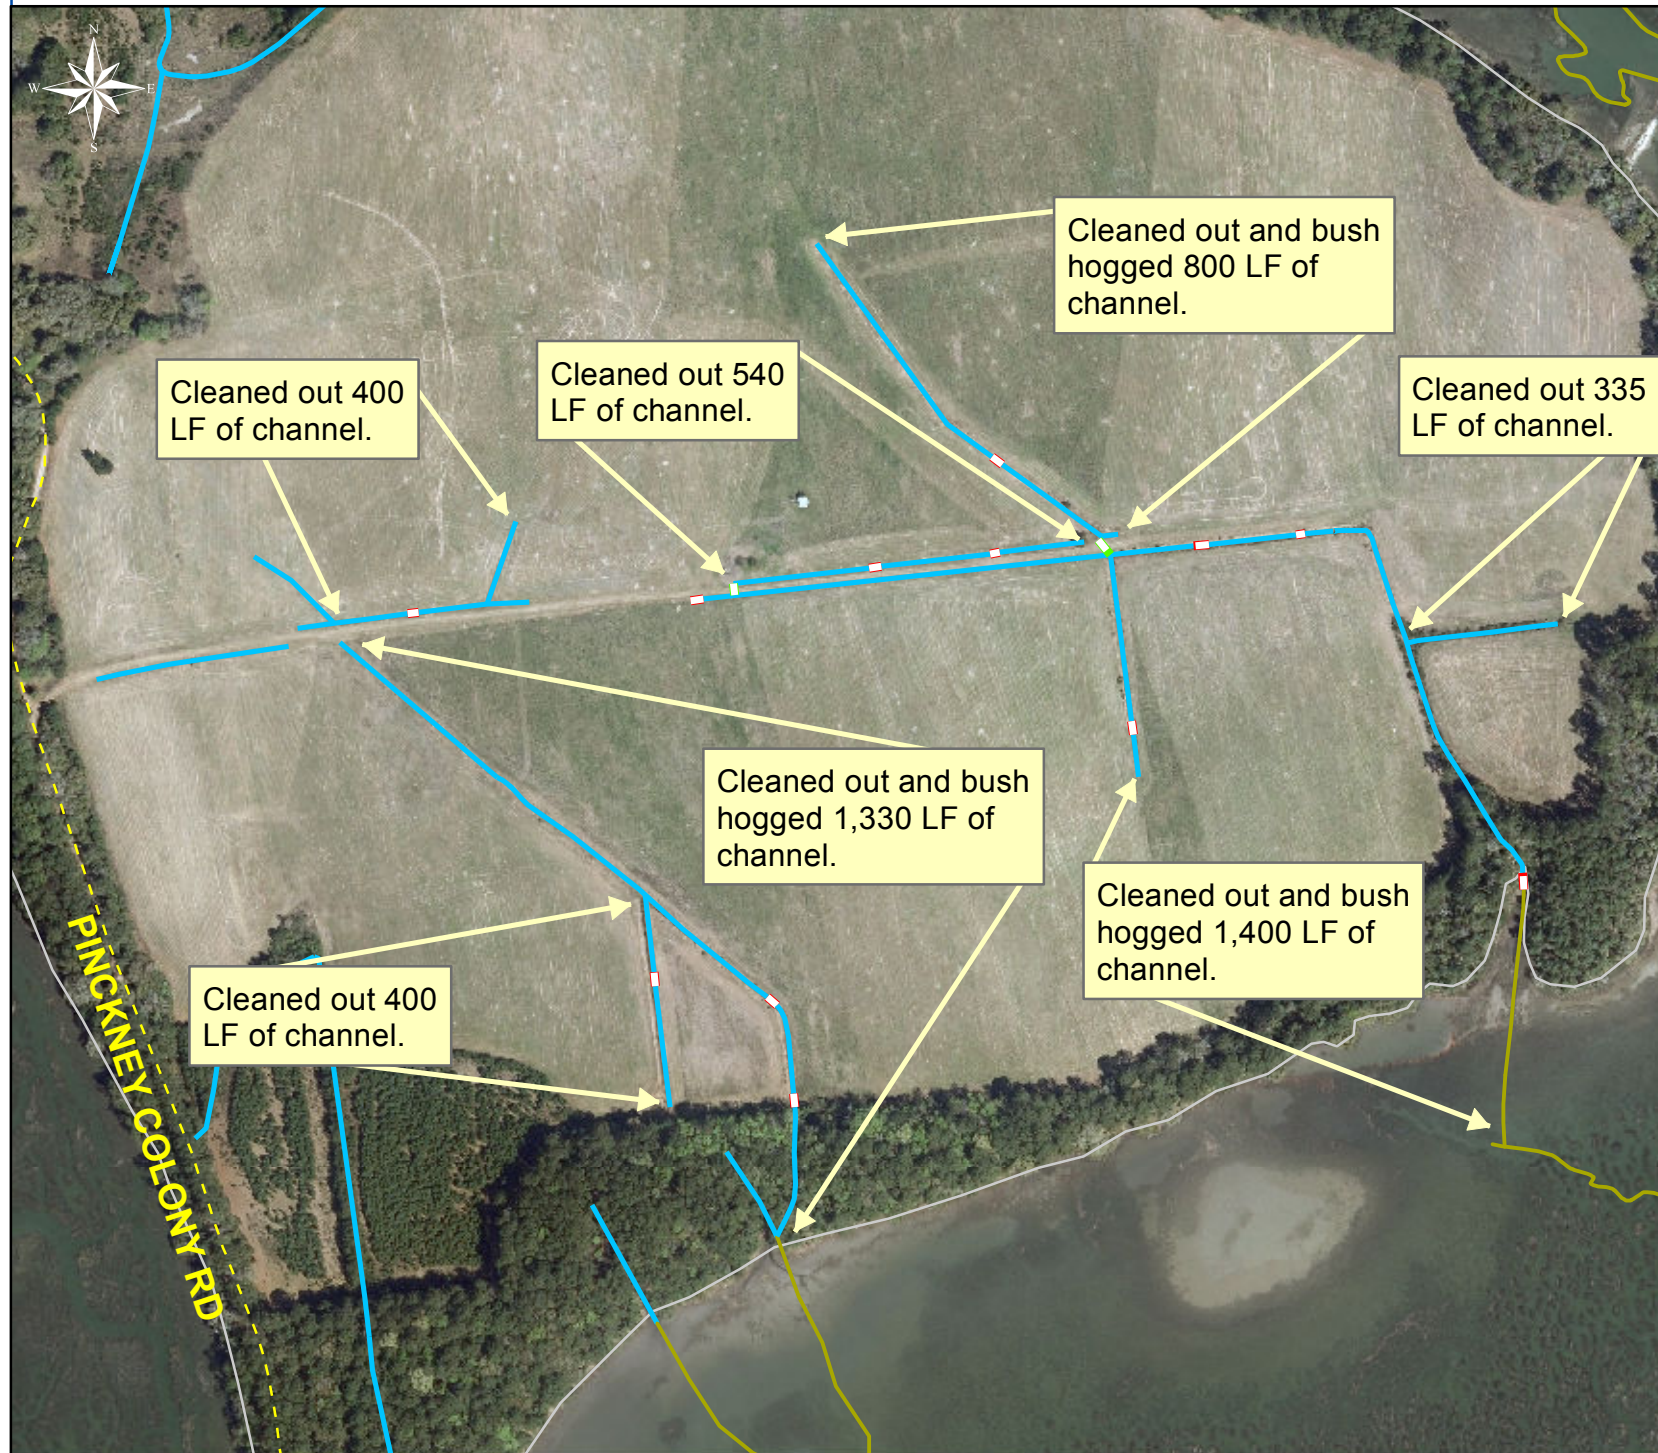









Township:
Bluffton

Completed:
July 2014



Legend

TYPE

-  River
-  Creek/Stream
-  River/Creek/Marsh BANK
-  Channel (fka Outfall)
-  Channel Pipe
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Road Pipe
-  Crossline Pipe
-  Driveway Pipe
-  Access Pipe
-  Bleeder Pipe



1 inch = 383 feet

Prepared By: BC Stormwater Management Utility

Date Print: 8/25/14

File: C:/sethdata/projects/projectmaps/Pinckney 2014-631 Map1

**Project: Pinckney
Colony Road Map 2**

**Activity: Vacuum
Truck**

**Project #:
2014-631**

**Township:
Bluffton**

**Completed:
July 2014**















Jetted (3) access pipes
and (1) crossline pipe.

Jetted (1) crossline pipe.

Jetted (3)
access pipes.

Legend

TYPE

-  River
-  Creek/Stream
-  River/Creek/Marsh BANK
-  Channel (fka Outfall)
-  Channel Pipe
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Road Pipe
-  Crossline Pipe
-  Driveway Pipe
-  Access Pipe
-  Bleeder Pipe



1 inch = 319 feet

Prepared By: BC Stormwater Management Utility

Date Print: 8/13/14

File:C:/sethdata/projects/projectmaps//Vac/Pinckneyt 2014-631 Map2

**Project: Pinckney
Colony Road Map 3**

**Activity: Routine/
Preventive
Maintenance**

**Project #:
2014-631**

**Township:
Bluffton**

**Completed:
July 2014**



Installed (1)
access pipe.

Installed (1) access pipe.

Installed (1)
access pipe.

Installed (1)
access pipe.

Installed (3)
access pipes.

Legend	
TYPE	
	River
	Creek/Stream
	River/Creek/Marsh BANK
	Channel (fka Outfall)
	Channel Pipe
	Lateral
	Lateral Pipe
	Roadside
	Roadside Pipe
	Road Pipe
	Crossline Pipe
	Driveway Pipe
	Access Pipe
	Bleeder Pipe



1 inch = 319 feet
