Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: Godwin Road

Activity: Routine/Preventive Maintenance


Narrative Description of Project:

Completion: Jul-15

Project improved 1,694 L.F. of drainage system. Cleaned out 560 L.F. of roadside ditch and 1,560 L.F. of valley drain. Jetted (4) driveway pipes and 134 L.F. of roadside pipe.

2015-619 / Godwin Road	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	0.5	\$11.75	\$0.00	\$0.00	\$0.00	\$6.62	\$18.36
COVD / Cleaned Out Valley Drains	14.0	\$312.90	\$67.18	\$10.60	\$0.00	\$209.37	\$600.05
DPJT / Driveway Pipe - Jetted	8.0	\$183.06	\$34.72	\$29.84	\$0.00	\$118.80	\$366.42
DPREM / Driveway Pipe - Removed	6.0	\$134.10	\$10.62	\$6.36	\$0.00	\$89.73	\$240.81
HAUL / Hauling	22.0	\$515.90	\$175.78	\$197.18	\$0.00	\$317.24	\$1,206.10
ONJV / Onsite Job Visit	10.0	\$338.28	\$35.56	\$21.60	\$0.00	\$232.48	\$627.92
PRRECON / Project Reconnaissance	2.0	\$74.11	\$7.16	\$6.48	\$0.00	\$52.19	\$139.94
RPWO / Repaired Washout	12.0	\$264.48	\$21.24	\$10.60	\$0.00	\$169.11	\$465.43
RSDCL / Roadside Ditch - Cleanout	55.0	\$1,235.45	\$205.15	\$51.94	\$0.00	\$789.60	\$2,282.14
STBY / Stand By	20.0	\$432.65	\$17.70	\$8.64	\$0.00	\$285.90	\$744.89
2015-619 / Godwin Road Sub Total	149.5	\$3,502.68	\$575.11	\$343.24	\$0.00	\$2,271.03	\$6,692.07
Grand Total	149.5	\$3,502.68	\$575.11	\$343.24	\$0.00	\$2,271.03	\$6,692.07



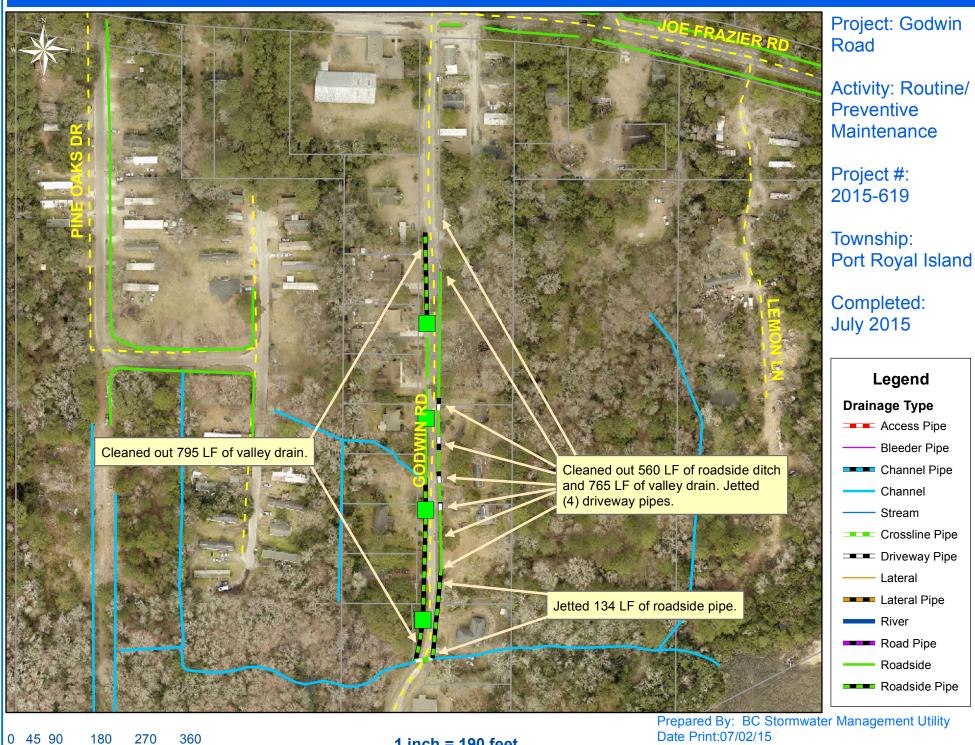

Feet

1 inch = 190 feet

File:C:\project summaries map/Godwin Road 2015-619
