



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Orange Grove Road Channel #1

Activity: Routine/Preventive Maintenance

Duration: 04/24/18-05/08/18

Narrative Description of Project:

Project improved 2,650 L.F. of drainage system. Bush hogged 1,250 L.F. of workshelf and 800 L.F. of roadside ditch. Cleaned out 600 L.F. of channel.

2018-602 / Orange Grove Road Channel #1	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	0.5	\$10.90	\$0.00	\$0.00	\$0.00	\$0.00	\$10.90
CBH / Channel- bushhogged	20.0	\$466.10	\$78.96	\$19.09	\$0.00	\$271.60	\$835.75
CCO / Channel - cleaned out	40.0	\$932.20	\$147.70	\$61.84	\$0.00	\$543.20	\$1,684.94
HAUL / Hauling	5.0	\$111.35	\$47.10	\$38.72	\$0.00	\$72.10	\$269.27
UTLOC / Utility locates	0.5	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
2018-602 / Orange Grove Road Channel #1 Sub Total	66.0	\$1,532.90	\$273.76	\$119.65	\$0.00	\$893.51	\$2,819.82
Grand Total	66.0	\$1,532.90	\$273.76	\$119.65	\$0.00	\$893.51	\$2,819.82

Before




During



After



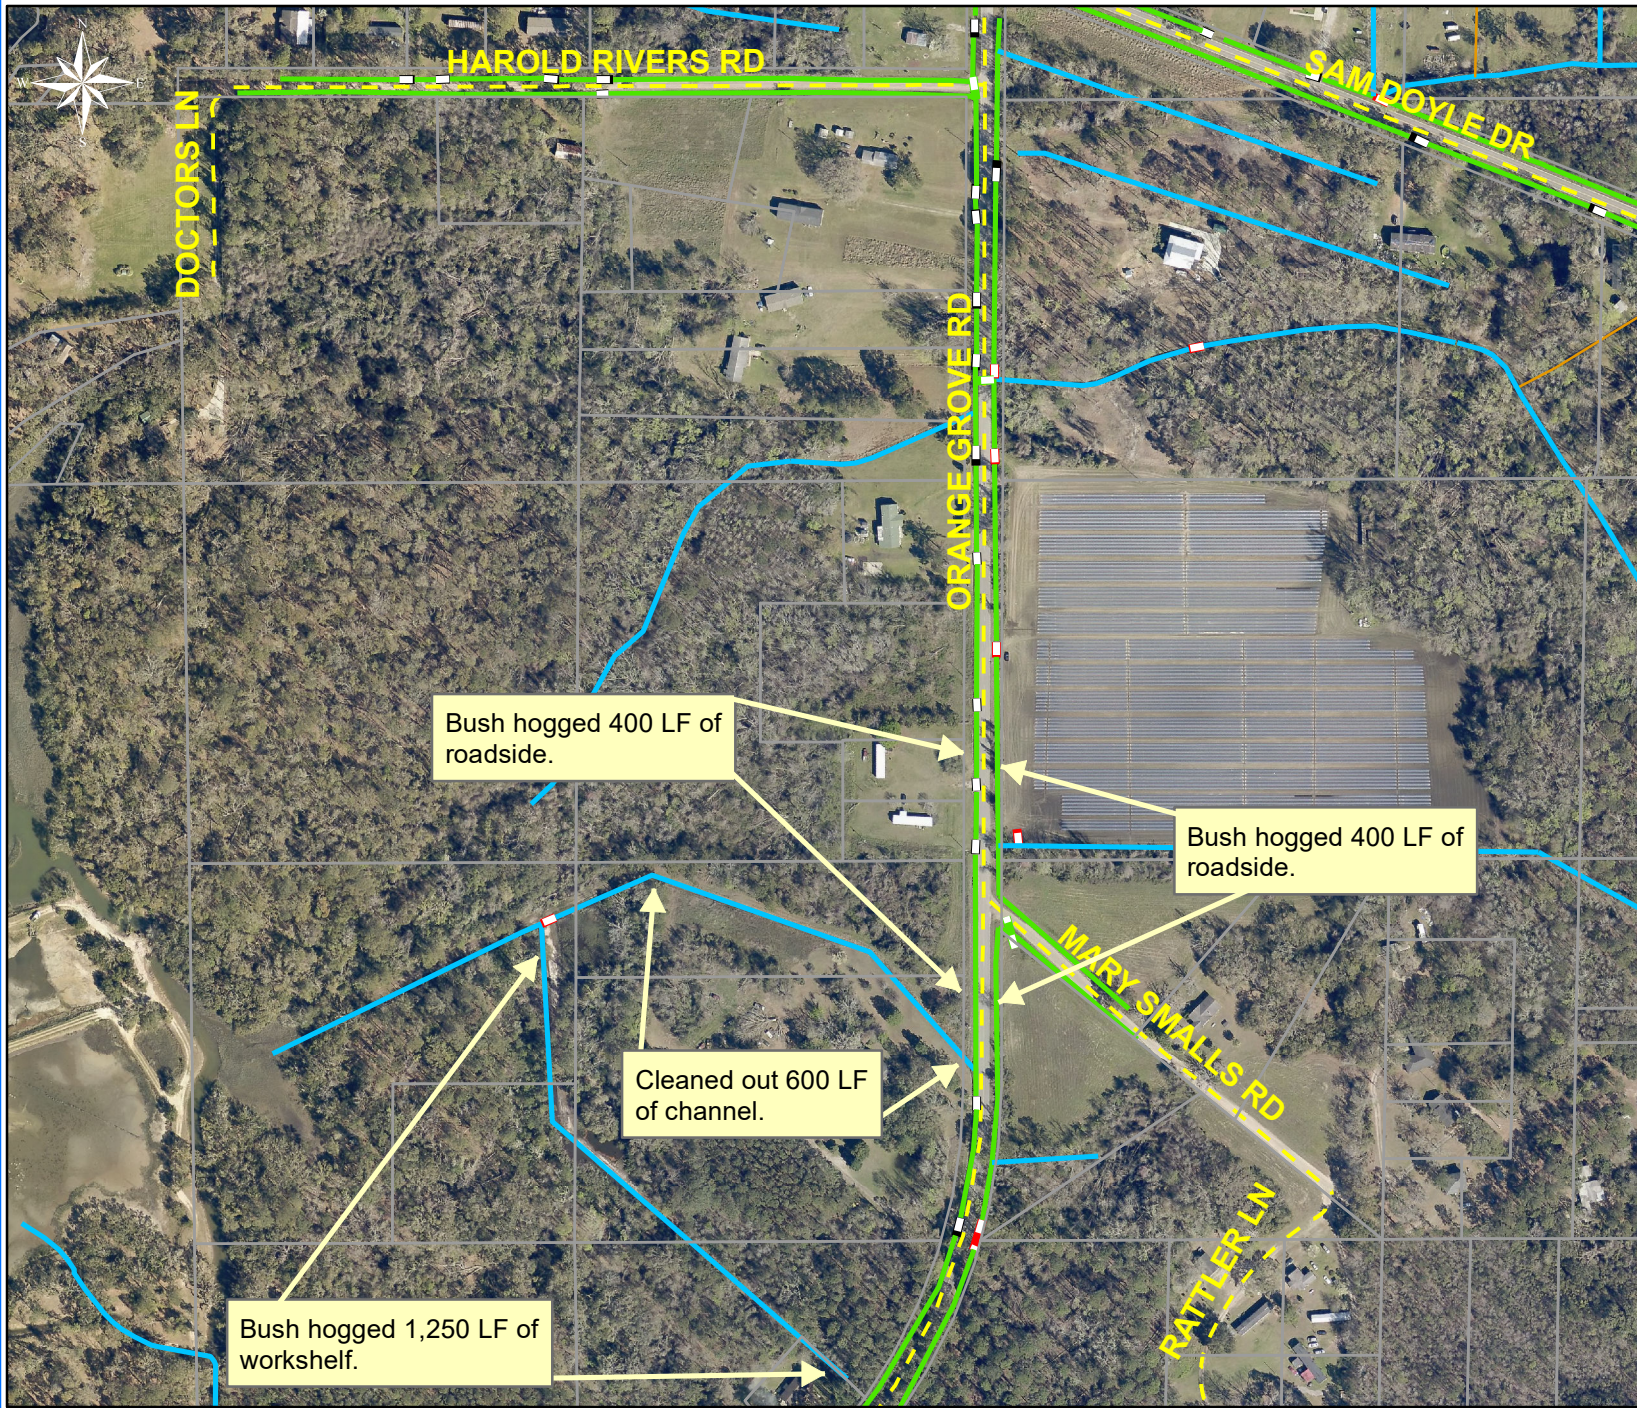

Project: Orange Grove Road Channel #1

Activity: Routine/ Preventive Maintenance

Project #: 2018-602

Township/SW Dist: St. Helena Island/8

Completed: May 2018

Legend	
Drainage Type	
	Access Pipe
	Bleeder Pipe
	Channel Pipe
	Channel
	Stream
	Crossline Pipe
	Driveway Pipe
	Lateral
	Lateral Pipe
	River
	Road Pipe
	Roadside
	Roadside Pipe



1 inch = 330 feet

Prepared By: BC Stormwater Management Utility
 Date Print: 11/27/18
 File: C:\project summaries map\Orange Grove Road Channel#1 2018-602
