



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Laurel Court Channel #1

Activity: Drainage Improvement

Duration: 10/24/17-12/14/17

Narrative Description of Project:

Project improved 270 L.F. of drainage system. Installed 270 L.F. of channel pipe, rip rap and hydroseeded for erosion control.

2018-003 / Laurel Court Channel #1	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	1.5	32.69	0.00	0.00	0.00	0.00	32.69
CPI / Channel Pipe - Installation	170.0	3,814.70	1,610.94	5,663.09	0.00	1,906.10	12,994.83
DEBREM / Debris Removal - Jobsite	10.0	240.90	88.03	19.50	0.00	138.25	486.68
HAUL / Hauling	138.0	3,132.59	1,208.56	3,218.91	0.00	1,327.61	8,887.67
HYDR / Hydroseeding	28.0	616.52	88.32	1,245.95	0.00	394.86	2,345.65
RRI / Rip Rap - Installed	52.0	1,181.50	283.74	185.78	0.00	549.15	2,200.17
STAGING / Staging Materials/Equipment	20.0	457.70	36.00	33.60	0.00	297.00	824.30
UTLOC / Utility locates	3.0	74.10	0.00	0.00	0.00	39.69	113.79
WSDR / Workshelf - Dressed	6.0	133.68	10.80	8.58	0.00	86.04	239.10
2018-003 / Laurel Court Channel #1 Sub Total	428.5	9,684.38	3,326.39	10,375.40	0.00	4,738.70	28,124.87
Grand Total	428.5	9,684.38	3,326.39	10,375.40	0.00	4,738.70	28,124.87

Before




During



After



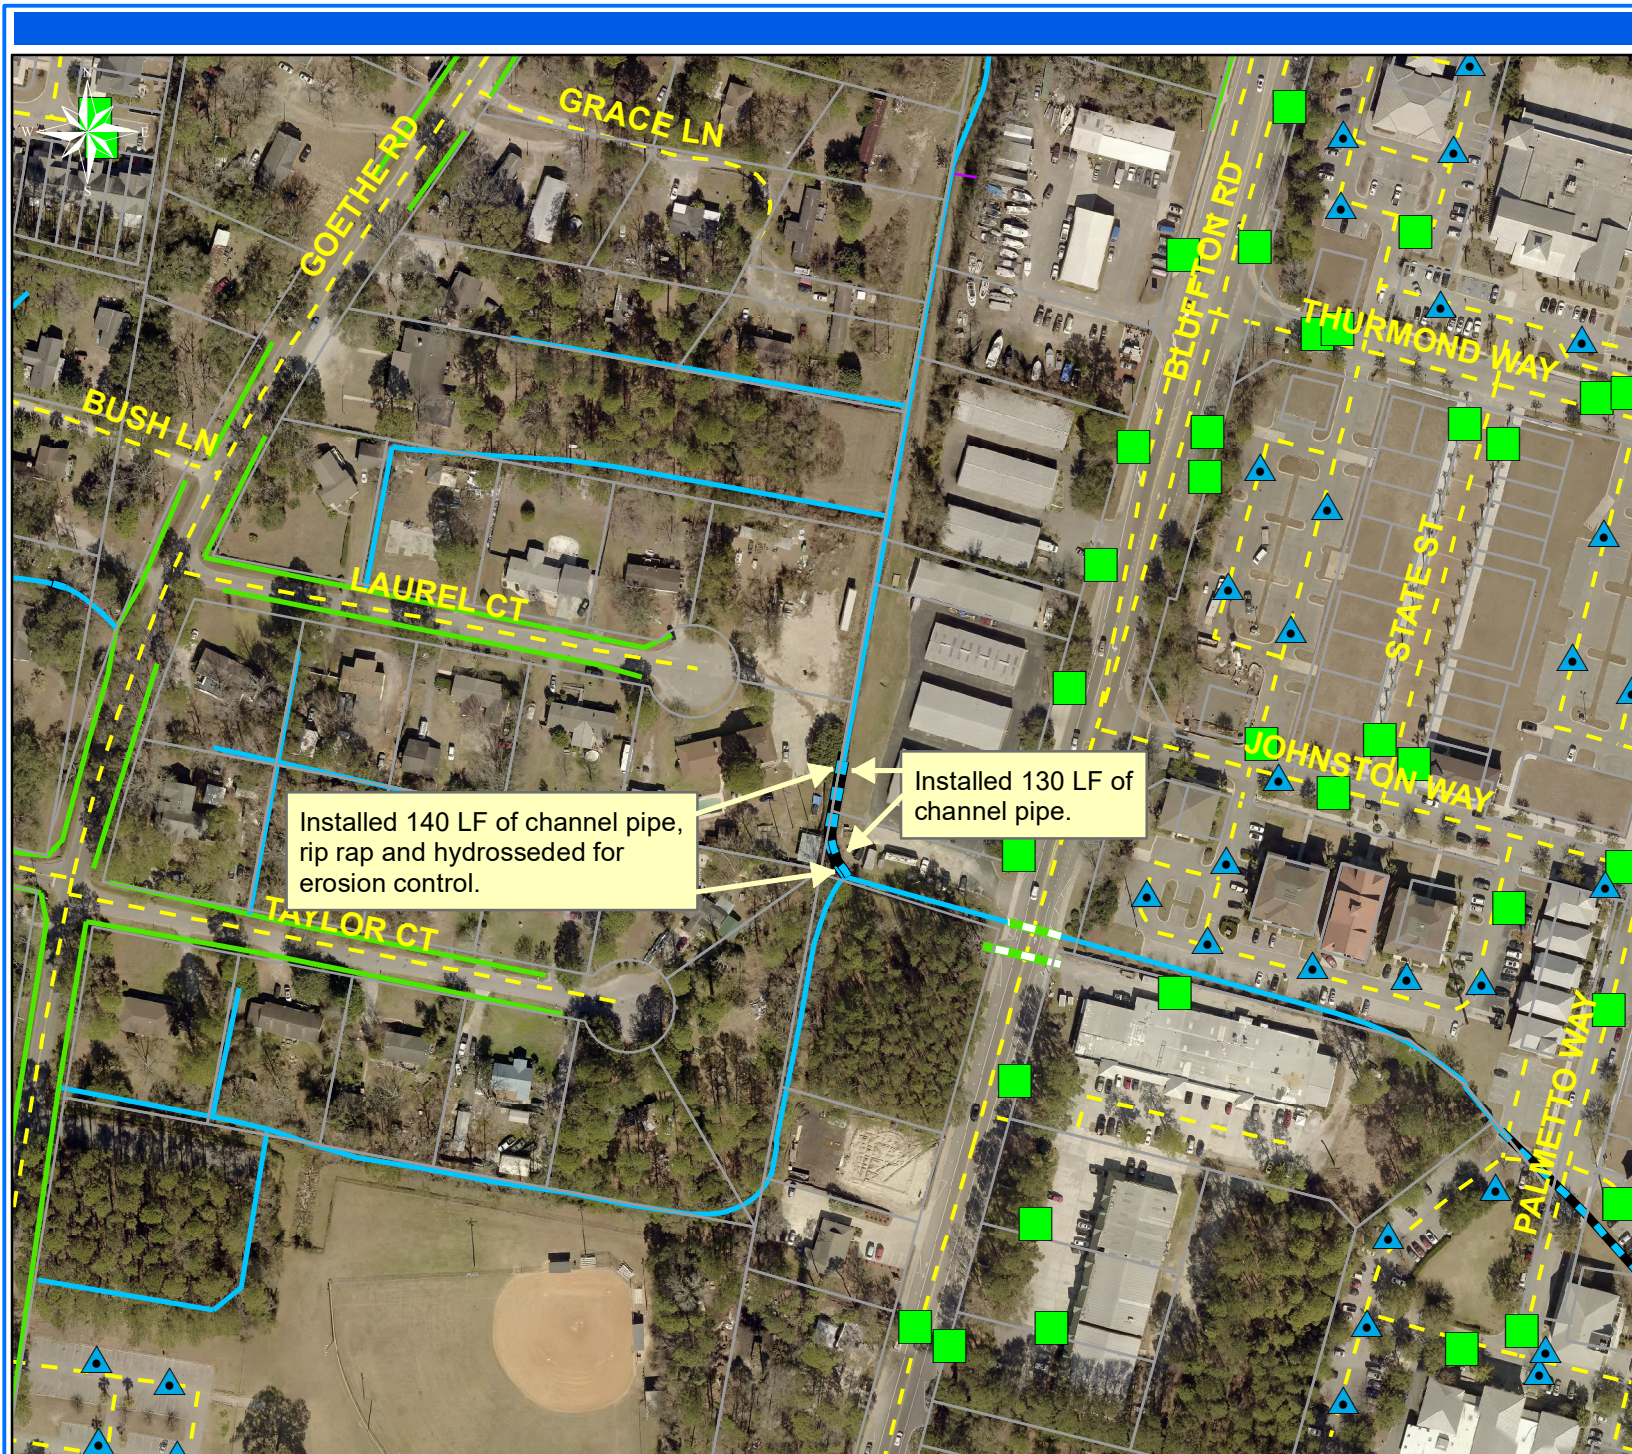

Project: Laurel Court Channel #1

Activity: Routine/
Preventive
Maintenance

Project #:
2018-003

Township/SW Dist:
Bluffton/4

Completed:
December 2017

Legend

Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 50 100 200 300 400
Feet

1 inch = 210 feet

Prepared By: BC Stormwater Management Utility

Date Print: 07/17/18

File: C:\project summaries map\Laurel Court Channel #1_2018-003
