



**Beaufort County Public Works**  
**Stormwater Infrastructure**  
*Project Summary*

**Project Summary:** Gibson Drive

**Activity:** Routine/Preventive Maintenance

**Duration:** 04/19/18-05/08/18

**Narrative Description of Project:**

Project improved 312 L.F. of drainage system. Cleaned out (4) catch basins. Installed 120 L.F. of channel pipe. Jetted (2) crossline pipes, 8 LF of channel pipe and 184 L.F. of roadside pipe. Installed rip rap and hydroseeded for erosion control.

2018-006 / Gibson Drive	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	1.0	\$21.79	\$0.00	\$0.00	\$0.00	\$0.00	\$21.79
CPI / Channel Pipe - Installation	120.0	\$2,559.50	\$371.40	\$1,723.90	\$0.00	\$1,357.20	\$6,012.00
CPJ / Channel Pipe - Jetted	16.0	\$356.48	\$69.44	\$72.60	\$0.00	\$229.44	\$727.96
HAUL / Hauling	45.0	\$1,075.05	\$423.90	\$954.76	\$0.00	\$710.40	\$3,164.11
HYDR / Hydroseeding	15.0	\$328.13	\$30.44	\$985.30	\$0.00	\$148.50	\$1,492.36
RRI / Rip Rap - Installed	20.0	\$433.43	\$60.40	\$47.92	\$0.00	\$214.65	\$756.39
UTLOC / Utility locates	0.5	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
2018-006 / Gibson Drive Sub Total	217.5	\$4,786.72	\$955.58	\$3,784.48	\$0.00	\$2,666.80	\$12,193.59
<b>Grand Total</b>	<b>217.5</b>	<b>\$4,786.72</b>	<b>\$955.58</b>	<b>\$3,784.48</b>	<b>\$0.00</b>	<b>\$2,666.80</b>	<b>\$12,193.59</b>

**Before**




**During**



**After**





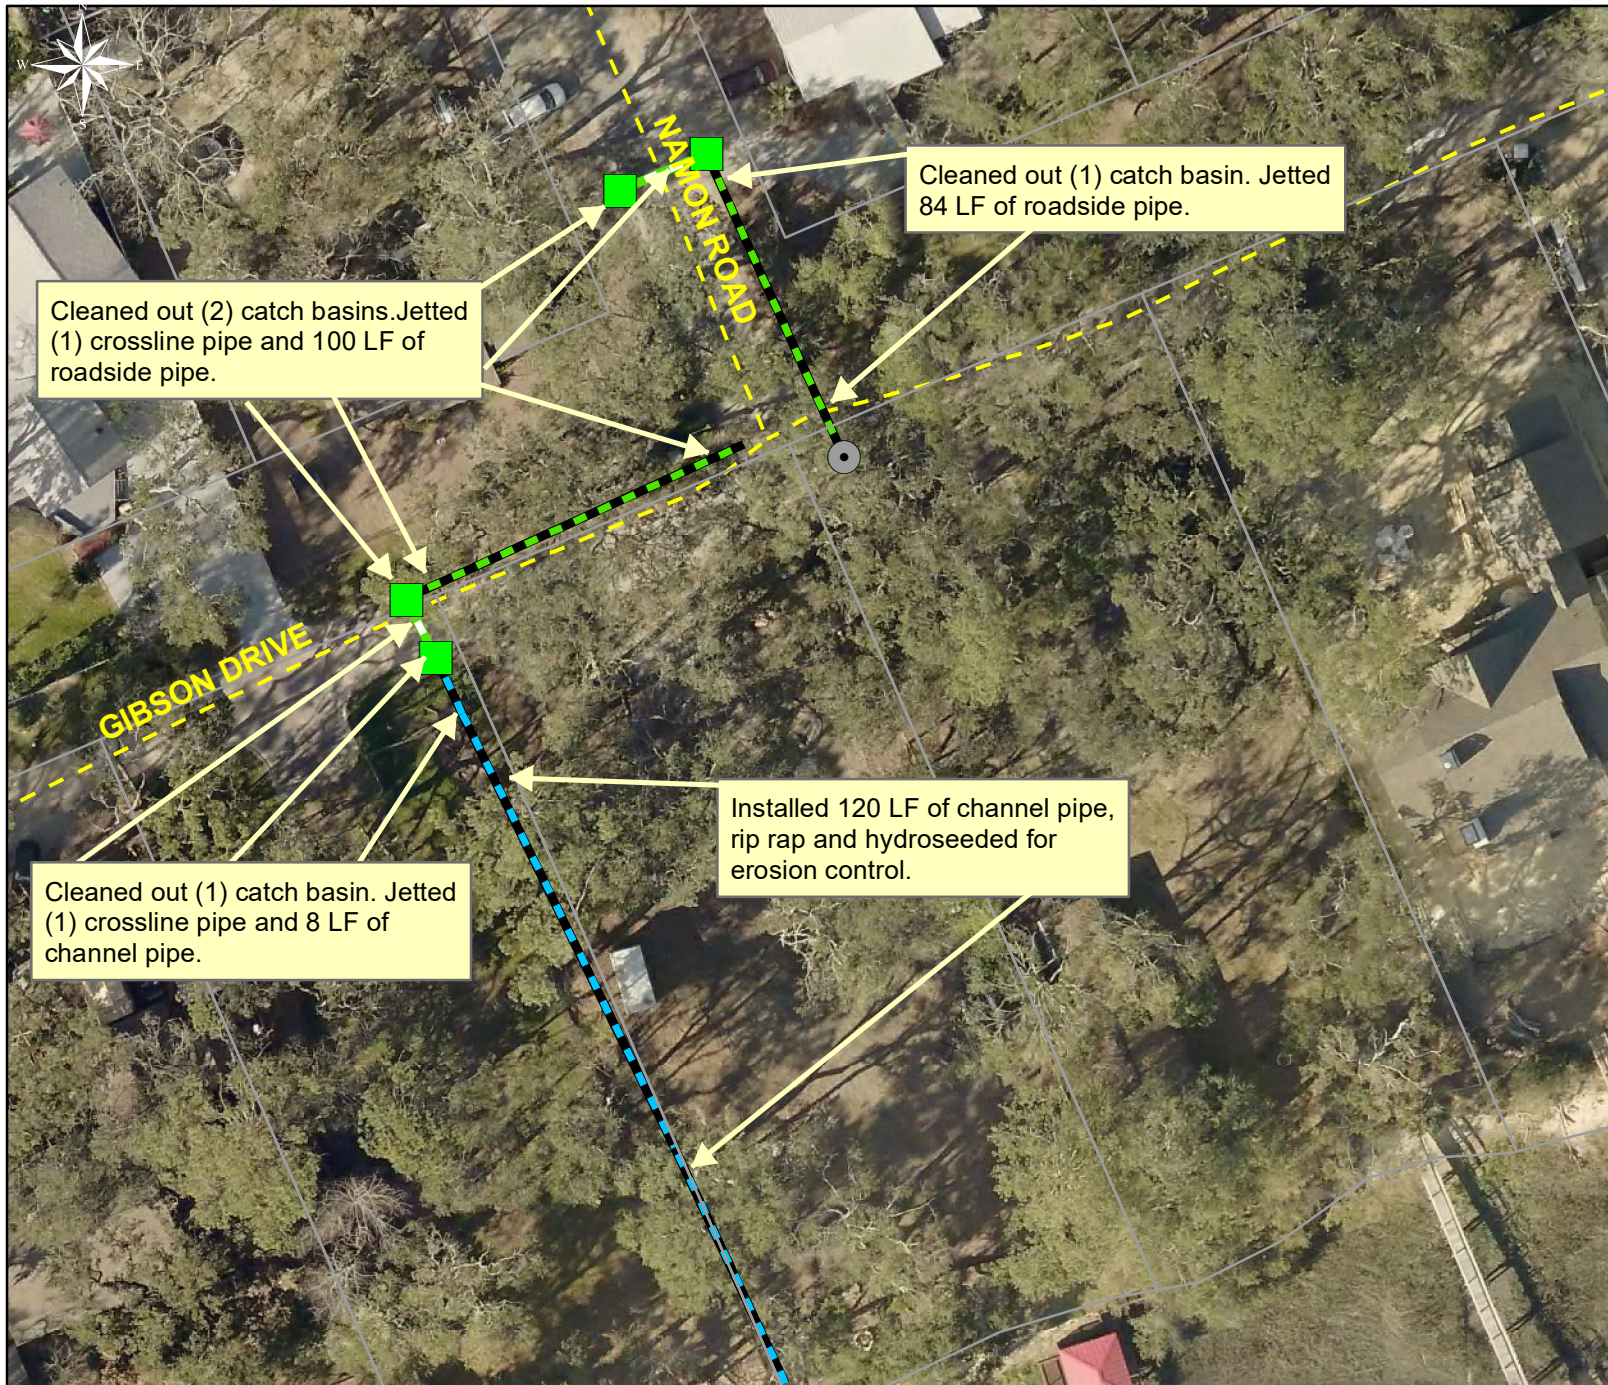

Project: Gibson Drive

Activity: Routine/ Preventive Maintenance

Project #: 2018-006

Township/SW Dist: TOHHI/3

Completed: May 2018

### Legend

#### Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 10 20 40 60 80 Feet

1 inch = 50 feet

Prepared By: BC Stormwater Management Utility

Date Print: 04/02/19

File: C:\project summaries map\Gibson Drive\_2018-006
