

Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Pearl Lane Channel #1

Activity: Routine/Preventive Maintenance **Duration:** 10/15/18-02/20/19

Narrative Description of Project:


Project improved 496 L.F. of drainage system. Grubbed and cleared 466 L.F. of workshelf. Reconstruct 30 L.F. of channel. Cleaned out 466 L.F. of channel. Repaired washout. Installed (1) access pipe, rip rap and hydroseeded for erosion control.

2019-525 / Pearl Lane Channel #1	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
CCO / Channel - cleaned out	60.0	\$1,336.60	\$754.26	\$999.94	\$0.00	\$858.60	\$3,949.40
HAUL / Hauling	116.0	\$2,517.62	\$1,806.40	\$3,781.08	\$0.00	\$1,355.48	\$9,460.58
HYDR / Hydroseeding	20.0	\$423.75	\$30.44	\$827.69	\$0.00	\$148.50	\$1,430.38
LM / Loading Materials	16.0	\$366.16	\$200.31	\$50.98	\$0.00	\$237.60	\$855.05
RPWO / Repaired Washout	40.0	\$847.50	\$150.52	\$59.77	\$0.00	\$297.00	\$1,354.79
UTLOC / Utility locates	0.5	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
WSDR / Workshelf - Dressed	113.0	\$2,507.48	\$1,012.94	\$276.07	\$0.00	\$1,608.39	\$5,404.88
WSGRB / Workshelf - Grubbed	78.0	\$1,737.58	\$665.66	\$196.04	\$0.00	\$1,116.18	\$3,715.46
WSL / Workshelf - Level	19.0	\$410.54	\$180.62	\$30.80	\$0.00	\$201.42	\$823.38
2019-525 / Pearl Lane Channel #1 Sub Total	464.0	\$10,192.27	\$4,801.15	\$6,222.37	\$0.00	\$5,829.78	\$27,045.57
Grand Total Before	464	\$10,192.27 During	\$4,801.15	\$6,222.37	\$0.00	\$5,829.78 After	\$27,045.57







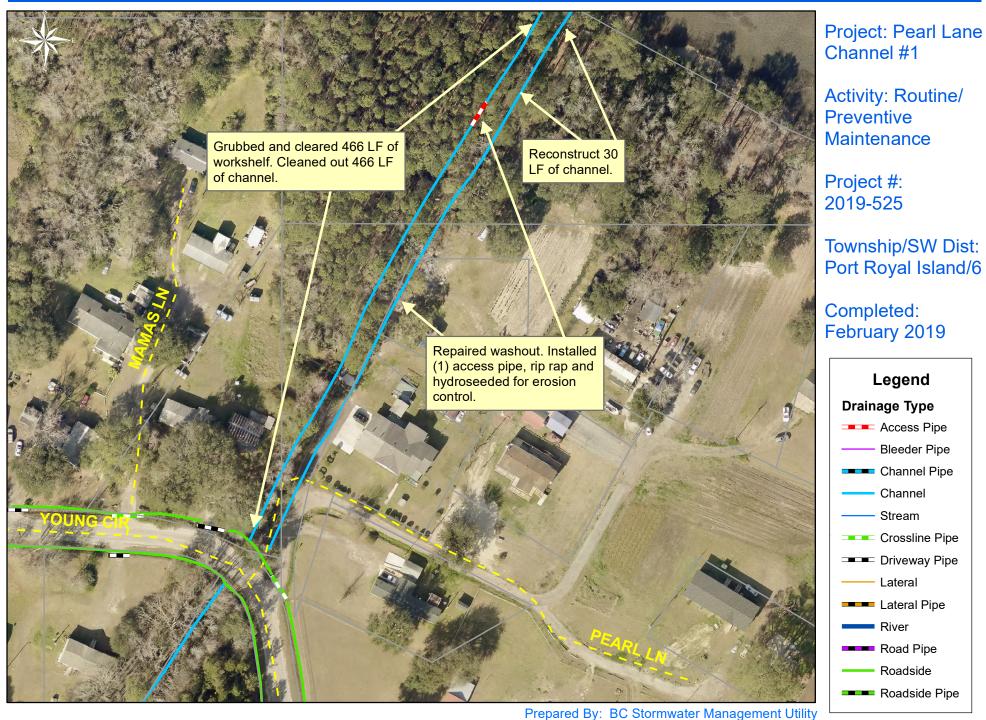

0 25 50 100 150 200 Feet 1 inch = 100 feet

Date Print:06/20/19 File:C:\project summaries map/Pearl Lane Channel #1 2019-525
