

Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Rose Island Drive

Activity: Routine/Preventive Maintenance

Duration: 02/13/18-03/05/18

Narrative Description of Project:

Project improved 2,408 L.F. of drainage system. Removed blockage from flowline. Cleaned out 2,408 L.F. of roadside ditch and valley drain. Jetted (2) driveway pipes. Hydroseeded for erosion control.

2018-578 / Rose Island Drive	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
DPJT / Driveway Pipe - Jetted	8.0	\$178.24	\$34.72	\$22.82	\$0.00	\$114.72	\$350.50
HAUL / Hauling	22.5	\$501.08	\$211.95	\$103.05	\$0.00	\$324.45	\$1,140.53
HYDR / Hydroseeding	40.0	\$818.40	\$68.07	\$424.41	\$0.00	\$386.70	\$1,697.58
RSDCL / Roadside Ditch - Cleanout	80.0	\$1,612.80	\$1,744.28	\$92.95	\$0.00	\$753.00	\$4,203.03
UTLOC / Utility locates	0.5	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
2018-578 / Rose Island Drive Sub Total	152.5	\$3,155.55	\$2,059.02	\$643.23	\$0.00	\$1,585.49	\$7,443.28
Grand Total	152.5	\$3,155.55	\$2,059.02	\$643.23	\$0.00	\$1,585.49	\$7,443.28

Before




During



After



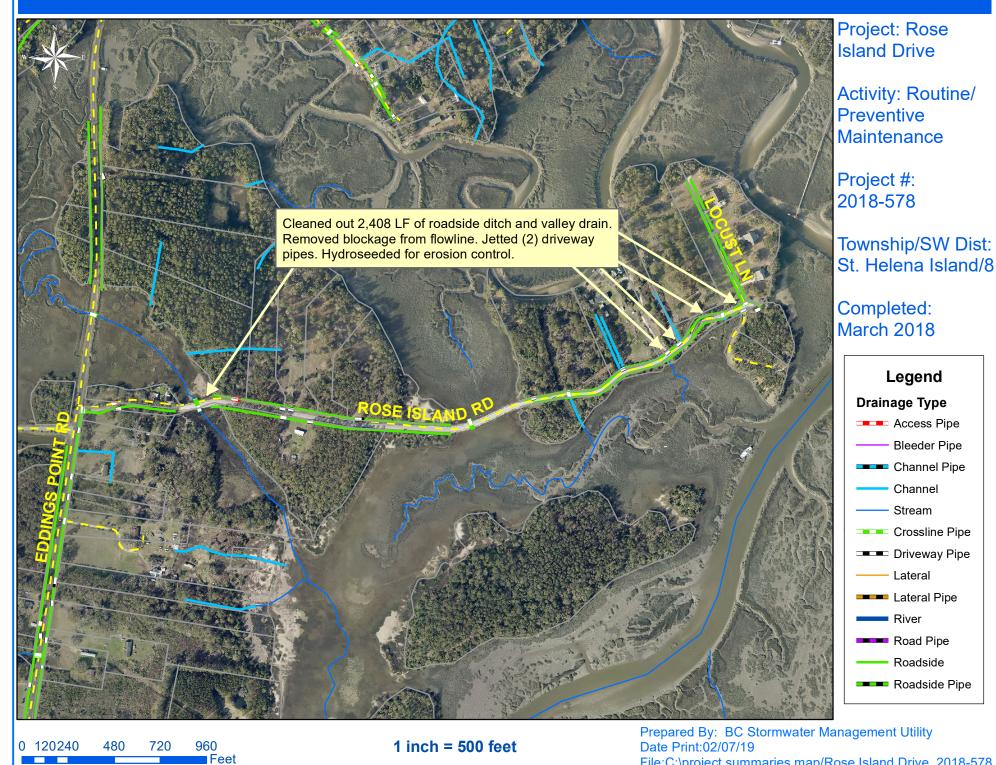

File:C:\project summaries map/Rose Island Drive_2018-578
