

**Beaufort County Public Works** Stormwater Infrastructure

Project Summary

Project Summary: Honeysuckle Lane

**Activity:** Routine/Preventive Maintenance **Duration:** 07/08/19-08/22/19

## Narrative Description of Project:

Project improved 397 L.F. of drainage system. Cleaned out 397 L.F. of roadside ditch. Jetted (1) crossline pipe. Replaced (1) crossline pipe. Installed rip rap for erosion control.

2020-582 / Honeysuckle Lane	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
ASI / Asphalt Installation	21.0	\$456.79	\$92.80	\$27.48	\$0.00	\$207.90	\$784.97
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
CLPJT / Crossline Pipe - Jetted	6.0	\$132.57	\$114.96	\$24.03	\$0.00	\$49.41	\$320.97
CPRPL / Crossline Pipe - Replaced	66.0	\$1,571.27	\$247.52	\$693.14	\$0.00	\$598.41	\$3,110.34
DLO / Ditch Layout	36.0	\$789.50	\$100.10	\$43.26	\$0.00	\$409.68	\$1,342.54
HAUL / Hauling	48.5	\$1,096.66	\$686.76	\$1,395.01	\$0.00	\$367.71	\$3,546.13
LM / Loading Materials	15.0	\$337.80	\$46.63	\$23.94	\$0.00	\$148.50	\$556.87
RRI / Rip Rap - Installed	12.0	\$261.04	\$71.66	\$37.98	\$0.00	\$118.80	\$489.48
RSDCL / Roadside Ditch - Cleanout	30.0	\$862.80	\$136.32	\$43.75	\$0.00	\$266.70	\$1,309.57
STAGING / Staging Materials/Equipment	31.0	\$676.44	\$108.67	\$61.56	\$0.00	\$324.98	\$1,171.64
UTLOC / Utility locates	1.0	\$21.79	\$0.00	\$0.00	\$0.00	\$0.00	\$21.79
2020-582 / Honeysuckle Lane Sub Total	268.0	\$6,239.33	\$1,605.42	\$2,350.14	\$0.00	\$2,492.09	\$12,686.98
Grand Total	268.0	\$6,239.33	\$1,605.42	\$2,350.14	\$0.00	\$2,492.09	\$12,686.98


## Before



During





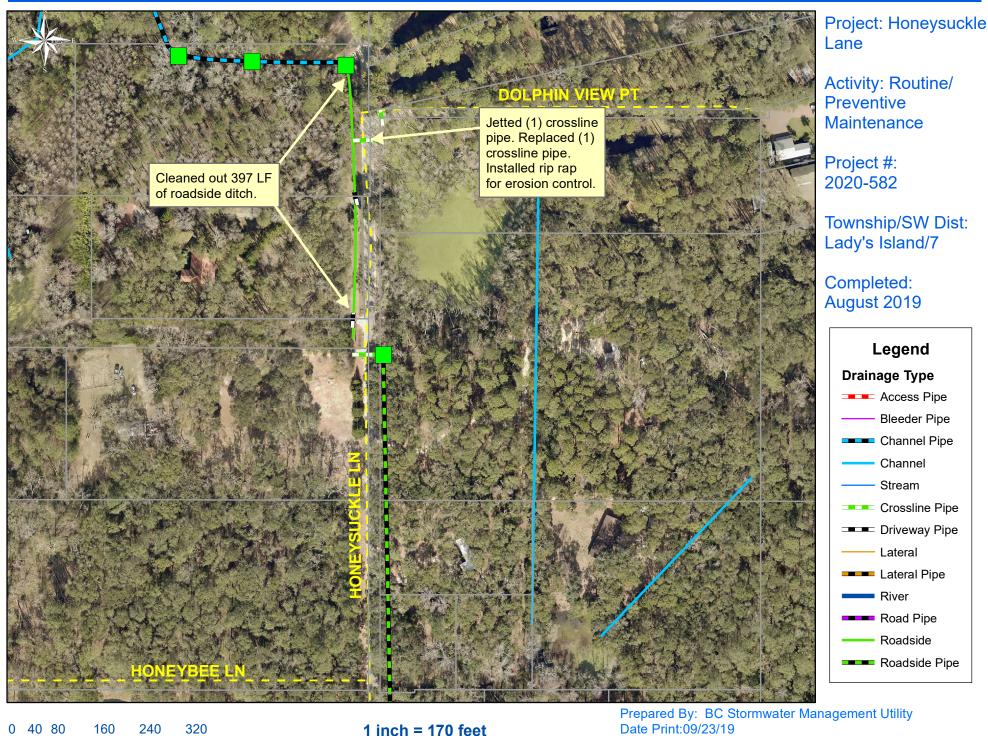

Feet

Date Print:09/23/19 File:C:\project summaries map/Honeysuckle Lane\_2020-582
