

Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Oyster Street **Activity:** Routine/Preventive Maintenance

Duration: 10/23/18-03/19/19

Narrative Description of Project:

2010 F20 / Overton Chroat

Project improved 2,097 L.F. of drainage system. Grubbed and cleared 466 L.F. of workshelf. Removed blockage from flowline. Cleaned out 261 L.F. of channel and 1,371 L.F. of roadside ditch. Installed (1) access pipe and rip rap. Jetted (2) driveway pipes and 260 L.F. of channel pipe. Handseeded and hydroseeded for erosion control.


2019-528 / Oyster Street	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	2.0	\$43.58	\$0.00	\$0.00	\$0.00	\$0.00	\$43.58
CCO / Channel - cleaned out	114.0	\$3,071.36	\$679.96	\$202.97	\$0.00	\$1,297.80	\$5,252.09
CPJ / Channel Pipe - Jetted	8.0	\$178.24	\$153.28	\$56.60	\$0.00	\$114.72	\$502.84
DEBRIS / Debris Removal	70.0	\$1,810.70	\$1,025.74	\$381.57	\$0.00	\$687.40	\$3,905.41
DPJT / Driveway Pipe - Jetted	12.0	\$267.36	\$229.92	\$53.93	\$0.00	\$172.08	\$723.29
HAND / HANDSEEDED	15.0	\$425.40	\$18.00	\$274.20	\$0.00	\$128.25	\$845.85
HAUL / Hauling	135.5	\$2,908.02	\$2,059.00	\$1,871.11	\$0.00	\$570.92	\$7,409.04
PP / Project Preparation	20.0	\$428.50	\$38.40	\$29.70	\$0.00	\$132.30	\$628.90
PRRECON / Project Reconnaissance	4.0	\$167.80	\$7.20	\$7.92	\$0.00	\$59.82	\$242.74
PS / Push up soil	20.0	\$481.80	\$355.31	\$47.06	\$0.00	\$276.50	\$1,160.67
RB / Remove blockage from flowline	20.0	\$423.75	\$43.08	\$30.29	\$0.00	\$148.50	\$645.62
RSDCL / Roadside Ditch - Cleanout	60	\$1,392.10	\$301.59	\$49.74	\$0.00	\$685.30	\$2,428.73
WSGRB / Workshelf - Grubbed	120	\$3,386.30	\$852.82	\$243.70	\$0.00	\$1,100.40	\$5,583.22
WSL / Workshelf - Level	128	\$2,960.24	\$1,068.35	\$277.23	\$0.00	\$1,220.68	\$5,526.50
2019-528 / Oyster Street Sub Total	728.5	\$17,945.15	\$6,832.65	\$3,526.02	\$0.00	\$6,594.67	\$34,898.48
Grand Total	728.5	\$17,945.15	\$6,832.65	\$3,526.02	\$0.00	\$6,594.67	\$34,898.48
Before		During				After	










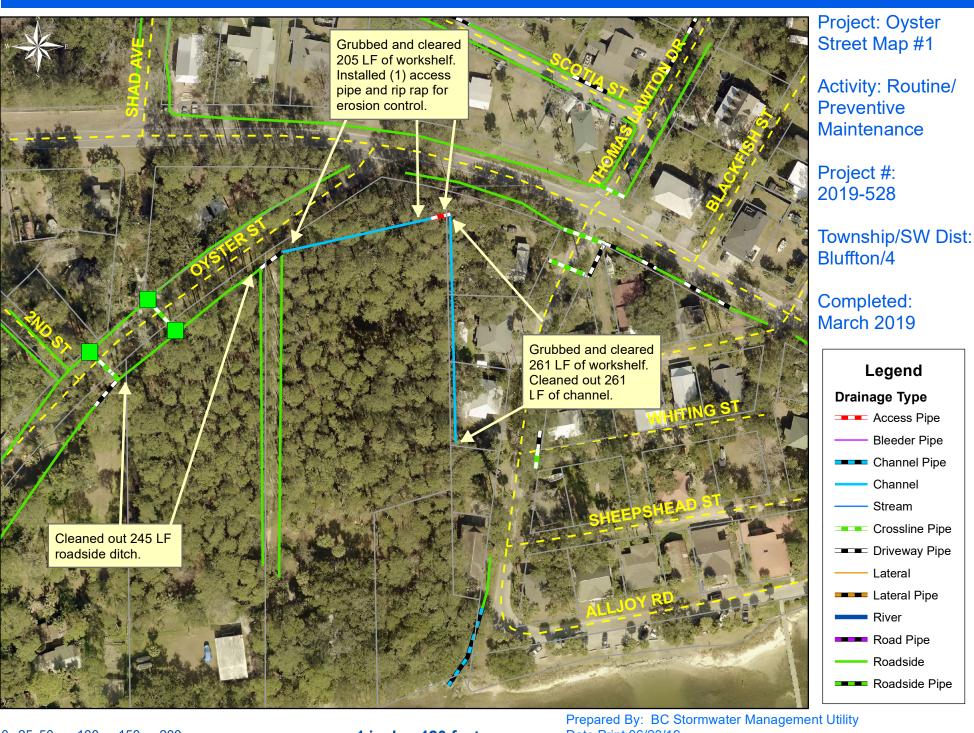

River Road Pipe Roadside Roadside Pipe

Date Print:06/20/19

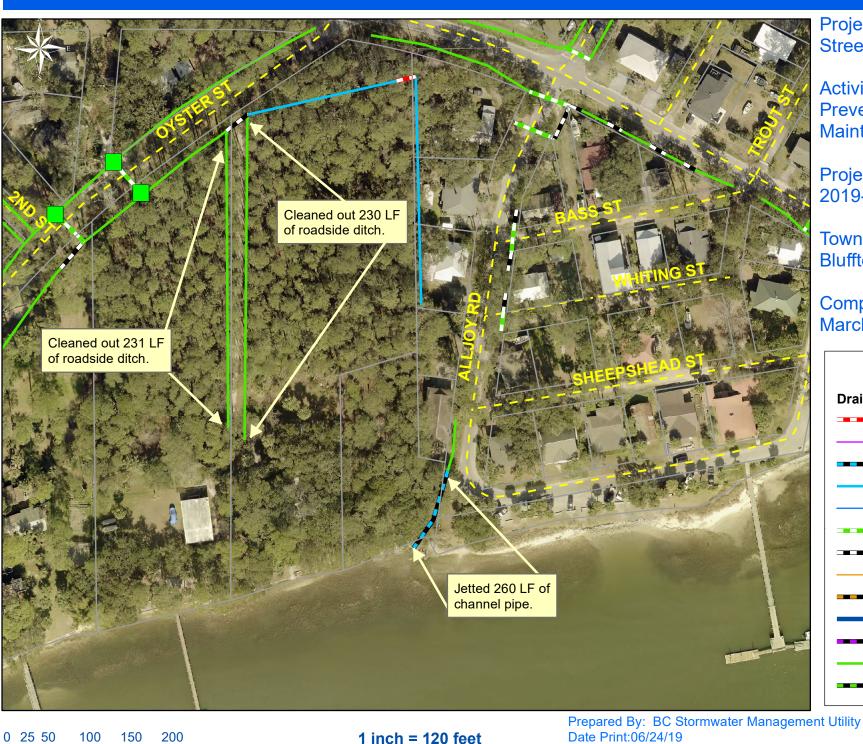

Project: Oyster Street Map #2

Activity: Routine/ Preventive Maintenance

Project #: 2019-528

Township/SW Dist: Bluffton/4

Completed: March 2019

Legend

Drainage Type

- Access Pipe
 - Bleeder Pipe
- Channel Pipe
 - Channel
 - Stream
- Crossline Pipe
- Driveway Pipe
 - Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

Date Print:06/24/19

File:C:\project summaries map/Oyster Street Map #2_2019-528



File:C:\project summaries map/Oyster Street Map #3_2019-528

