

Project Summary: Peaches Hill Circle

Activity: Routine/Preventive Maintenance

Duration: 08/08/19-12/31/19

Narrative Description of Project:

Project improved 1,567 L.F. of drainage system. Removed blockages from flowline. Cleaned out 1,237 L.F. of roadside ditch and 330 L.F. of channel. Upsized (1) access pipe. Installed straw mat and hydroseeded for erosion control.


2019-551A / Peaches Hill Circle	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
APREM / Access pipe - removed	30.0	\$621.60	\$63.98	\$88.34	\$0.00	\$259.50	\$1033.42
APUP / Access pipe - upsized	40.0	\$814.70	\$206.08	\$806.40	\$0.00	\$386.70	\$2213.88
AUDIT / Audit Project	1.0	\$21.79	\$0.00	\$0.00	\$0.00	\$0.00	\$21.79
CCO / Channel - cleaned out	30.0	\$843.50	\$143.35	\$37.81	\$0.00	\$388.80	\$1,413.46
HAUL / Hauling	66.5	\$1496.80	\$941.64	\$1022.92	\$0.00	\$641.69	\$4103.05
HYDR / Hydroseeding	18.0	\$371.88	\$47.92	\$853.21	\$0.00	\$232.02	\$1,505.03
RB / Remove blockage from flowline	20.0	\$528.85	\$39.47	\$24.10	\$0.00	\$133.35	\$725.77
RSDCL / Roadside Ditch - Cleanout	92.0	\$2,425.81	\$340.44	\$133.66	\$0.00	\$613.41	\$3,513.32
UTLOC / Utility locates	0.5	\$10.90	\$0.00	\$0.00	\$0.00	\$0.00	\$10.90
2019-551A / Peaches Hill Circle Sub Total	298.0	\$7,135.82	\$1,782.88	\$2,966.45	\$0.00	\$2,655.47	\$14,540.62
Grand Total	298.0	\$7,135.82	\$1,782.88	\$2,966.45	\$0.00	\$2,655.47	\$14,540.62

Before During After

(Picture Not Available)





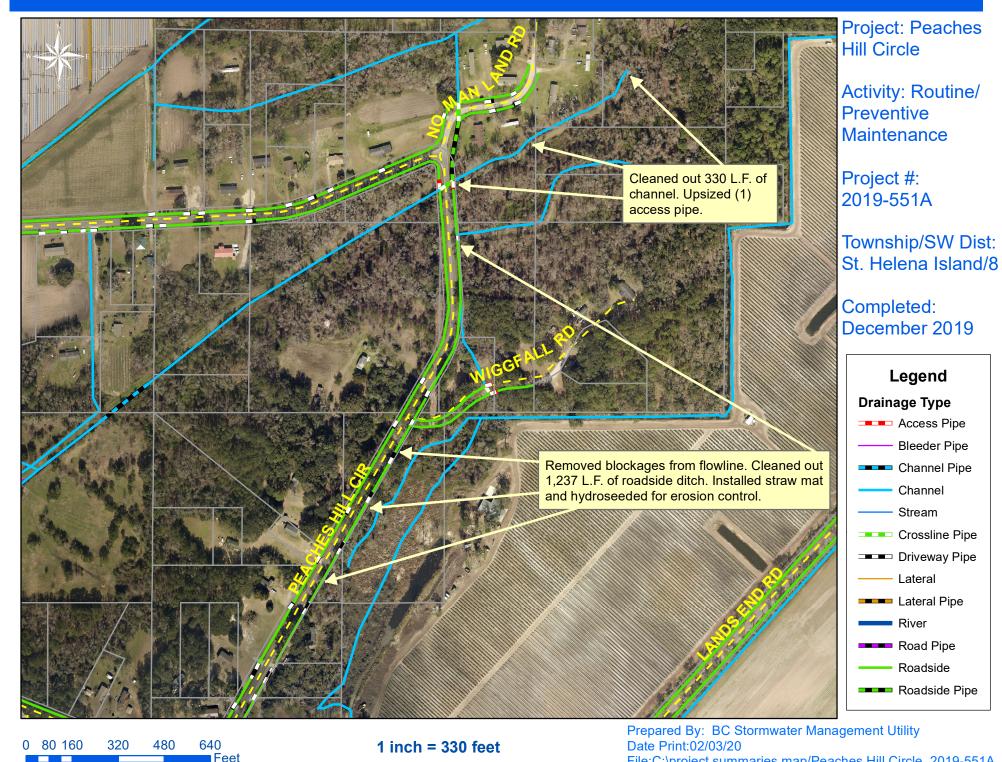

File:C:\project summaries map/Peaches Hill Circle_2019-551A
