

Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: Buckwalter Parkway

Activity: Routine/Preventive Maintenance Duration: 09/21/20-11/25/20

Narrative Description of Project:

Project improved 2,636 L.F. of drainage system. Grubbed and cleared 41 L.F. of workshelf. Bush hogged 2,139 L.F. of roadside ditch. Cleaned out 2,595 L.F. of roadside ditch. Repaired sinkhole. Installed rip rap and handseeded for erosion control.

2021-507 / Buckwalter Parkway	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	2.0	\$43.58	\$0.00	\$0.00	\$0.00	\$0.00	\$43.58
CBH / Channel- bushhogged	48.0	\$1,011.27	\$468.96	\$72.00	\$0.00	\$639.12	\$2,191.35
HAND / HANDSEEDED	32.0	\$689.16	\$139.23	\$121.54	\$0.00	\$158.76	\$1,108.69
HAUL / Hauling	97.0	\$2,203.42	\$1,911.14	\$1,241.76	\$0.00	\$807.52	\$6,163.84
PP / Project Preparation	18.0	\$383.46	\$26.10	\$15.60	\$0.00	\$152.64	\$577.80
RSDCL / Roadside Ditch - Cleanout	211.0	\$4,665.87	\$1,008.64	\$245.58	\$0.00	\$1,409.40	\$7,329.49
SG / Shoot Grade	28.0	\$608.88	\$51.72	\$31.20	\$0.00	\$158.76	\$850.56
SR / Sinkhole repair	12.0	\$249.36	\$17.40	\$17.60	\$0.00	\$52.92	\$337.28
UTLOC / Utility locates	2.0	\$49.40	\$0.00	\$0.00	\$0.00	\$26.46	\$75.86
WSGRB / Workshelf - Grubbed	40.0	\$837.36	\$156.63	\$50.72	\$0.00	\$211.68	\$1,256.39
2021-507 / Buckwalter Parkway Project Sub Total	490.0	\$10,741.76	\$3,779.82	\$1,796.01	\$0.00	\$3,617.26	\$19,934.85
Grand Total	490.0	\$10,741.76	\$3,779.82	\$1,796.01	\$0.00	\$3,617.26	\$19,934.85

(Before)




(During)



(After)



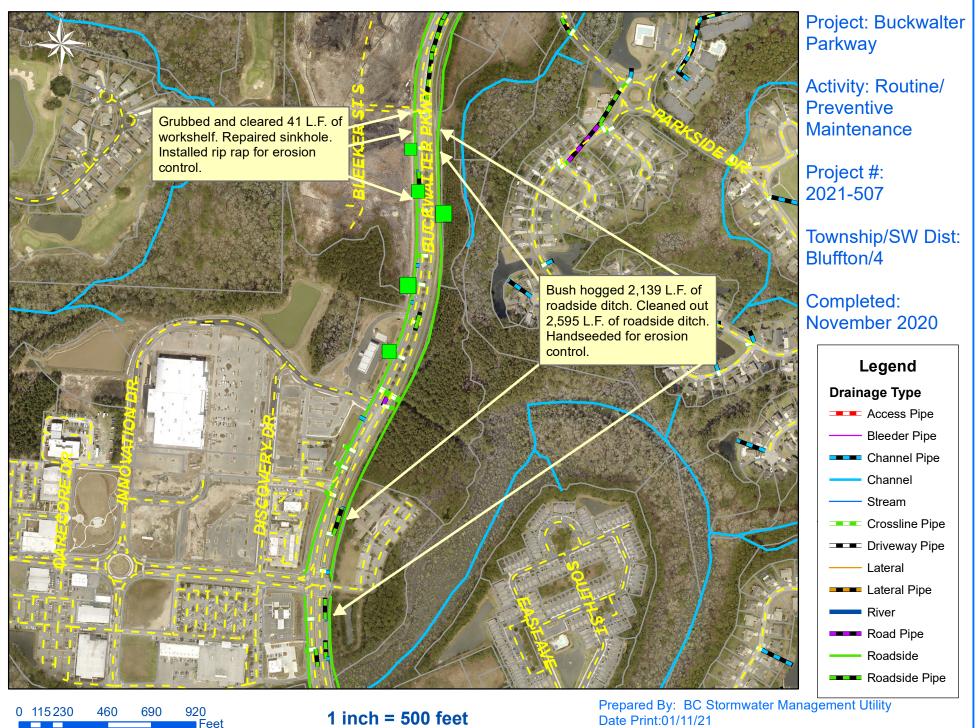

File:C:\project summaries map/Buckwalter Parkway_2021-507
