



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: River Oaks Road

Activity: Routine/Preventive Maintenance

Duration: 11/16/20-12/15/20

Narrative Description of Project:

Project improved 2,580 L.F. of drainage system. Removed blockage from flowline. Repaired 700 L.F. of worksheff. Cleaned out 1,680 L.F. of roadside ditch and 200 L.F. of channel. Jetted (10) driveway pipes and (4) crossline pipes. Hydroseeded for erosion control.

2021-512 / River Oaks Road	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	2.0	\$43.58	\$0.00	\$0.00	\$0.00	\$0.00	\$43.58
CCO / Channel - cleaned out	48.0	\$1,014.64	\$202.92	\$127.12	\$0.00	\$309.36	\$1,654.04
CLPJT / Crossline Pipe - Jetted	36.0	\$830.80	\$630.52	\$136.48	\$0.00	\$65.88	\$1,663.68
DPJT / Driveway Pipe - Jetted	42.0	\$960.75	\$804.72	\$158.56	\$0.00	\$0.00	\$1,924.03
HAUL / Hauling	87.0	\$1,920.93	\$1,658.22	\$1,029.94	\$0.00	\$288.40	\$4,897.49
HYDR / Hydroseeding	32.0	\$684.36	\$145.73	\$460.54	\$0.00	\$158.76	\$1,449.39
RSDCL / Roadside Ditch - Cleanout	120.0	\$2,555.20	\$543.90	\$160.32	\$0.00	\$521.04	\$3,780.46
UTLOC / Utility locates	1.0	\$24.70	\$0.00	\$0.00	\$0.00	\$13.23	\$37.93
WSREC / Workshelf - Reconstructed	48.0	\$1,014.64	\$178.11	\$38.40	\$0.00	\$309.36	\$1,540.51
2021-512 / River Oaks Road Project Sub Total	416.0	\$9,049.60	\$4,164.12	\$2,111.36	\$0.00	\$1,666.03	\$16,991.11
Grand Total	416.0	\$9,049.60	\$4,164.12	\$2,111.36	\$0.00	\$1,666.03	\$16,991.11

(Before)




(During)



(Ending)



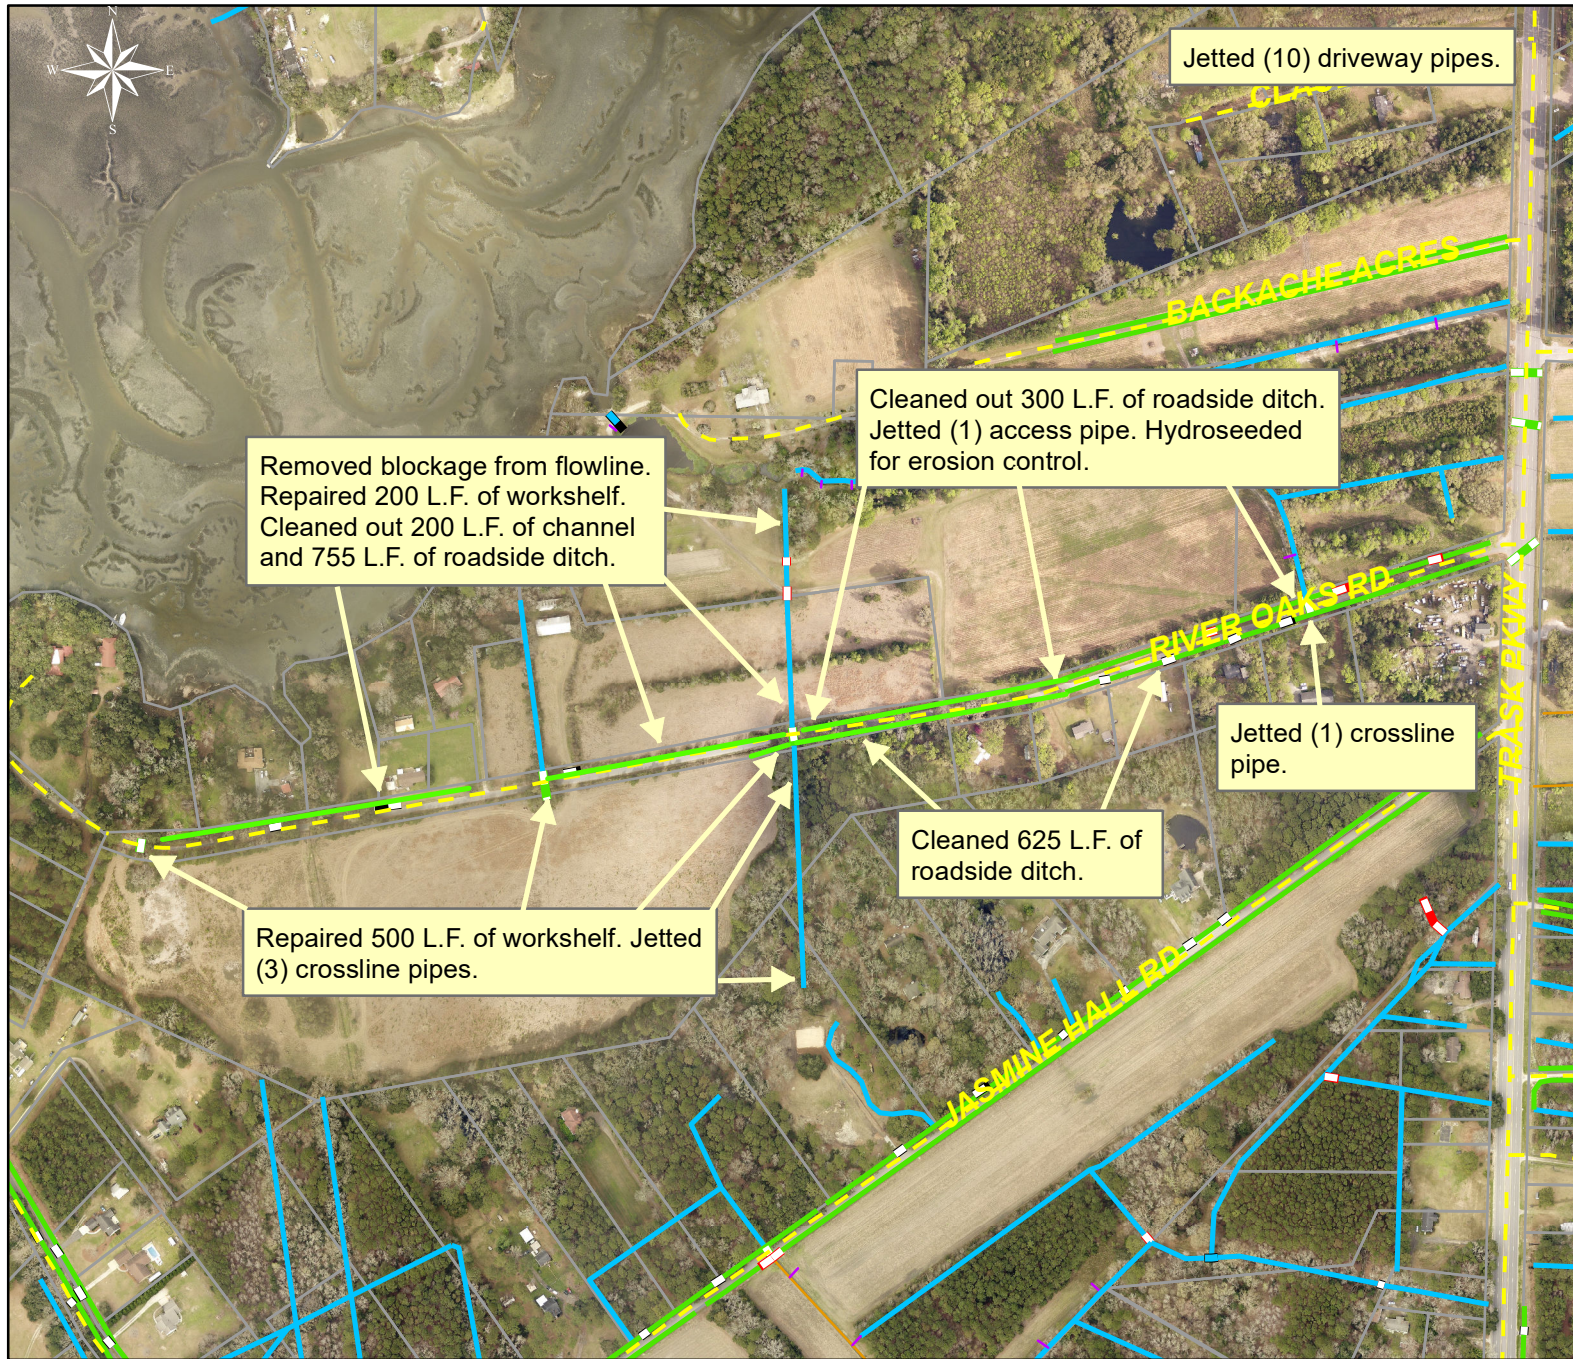

Project: River Oaks Road

Activity: Routine/ Preventive Maintenance

Project #: 2021-512

Township/SW Dist: Sheldon/5

Completed: December 2020

Legend

Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 120 240 480 720 960
Feet

1 inch = 500 feet

Prepared By: BC Stormwater Management Utility

Date Print: 01/19/21

File: C:\project summaries map\River Oaks Road_2021-512
