



**Beaufort County Public Works**  
**Stormwater Infrastructure**  
Project Summary

**Project Summary:** Hawkes Road Channel

**Activity:** Routine/Preventive Maintenance

**Duration:** 06/09/2025 - 06/12/2025

**Narrative Description of Project:**

Project improved 40 L.F. of drainage system. Upsized 40 L.F. of channel pipe.

2025-580 / Hawkes Road Channel	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Total Cost
AUDIT / Audit Project	1.50	\$38.67	\$768.24	\$0.00	\$0.00	\$806.91
CGRB / Channel - grubbed	24.00	\$518.08	\$863.92	\$0.00	\$0.00	\$1,382.00
CLJS / Cleaned up jobsite	56.00	\$1,209.76	\$1,540.64	\$0.00	\$0.00	\$2,750.40
CPUPD / Channel Pipe - Upsized	32.00	\$691.68	\$1,101.21	\$2,161.60	\$0.00	\$3,954.49
HAUL / Hauling	16.00	\$397.36	\$1,536.48	\$215.95	\$0.00	\$2,149.79
UC / Utility Coordination	1.00	\$26.22	\$0.00	\$0.00	\$0.00	\$26.22
UTLOC / Utility locates	2.00	\$52.44	\$0.00	\$0.00	\$0.00	\$52.44
<b>Grand Total</b>	<b>132.50</b>	<b>\$2,934.21</b>	<b>\$5,810.49</b>	<b>\$2,377.55</b>	<b>\$0.00</b>	<b>\$11,122.25</b>

**(Before)**




**(During)**



**(After)**





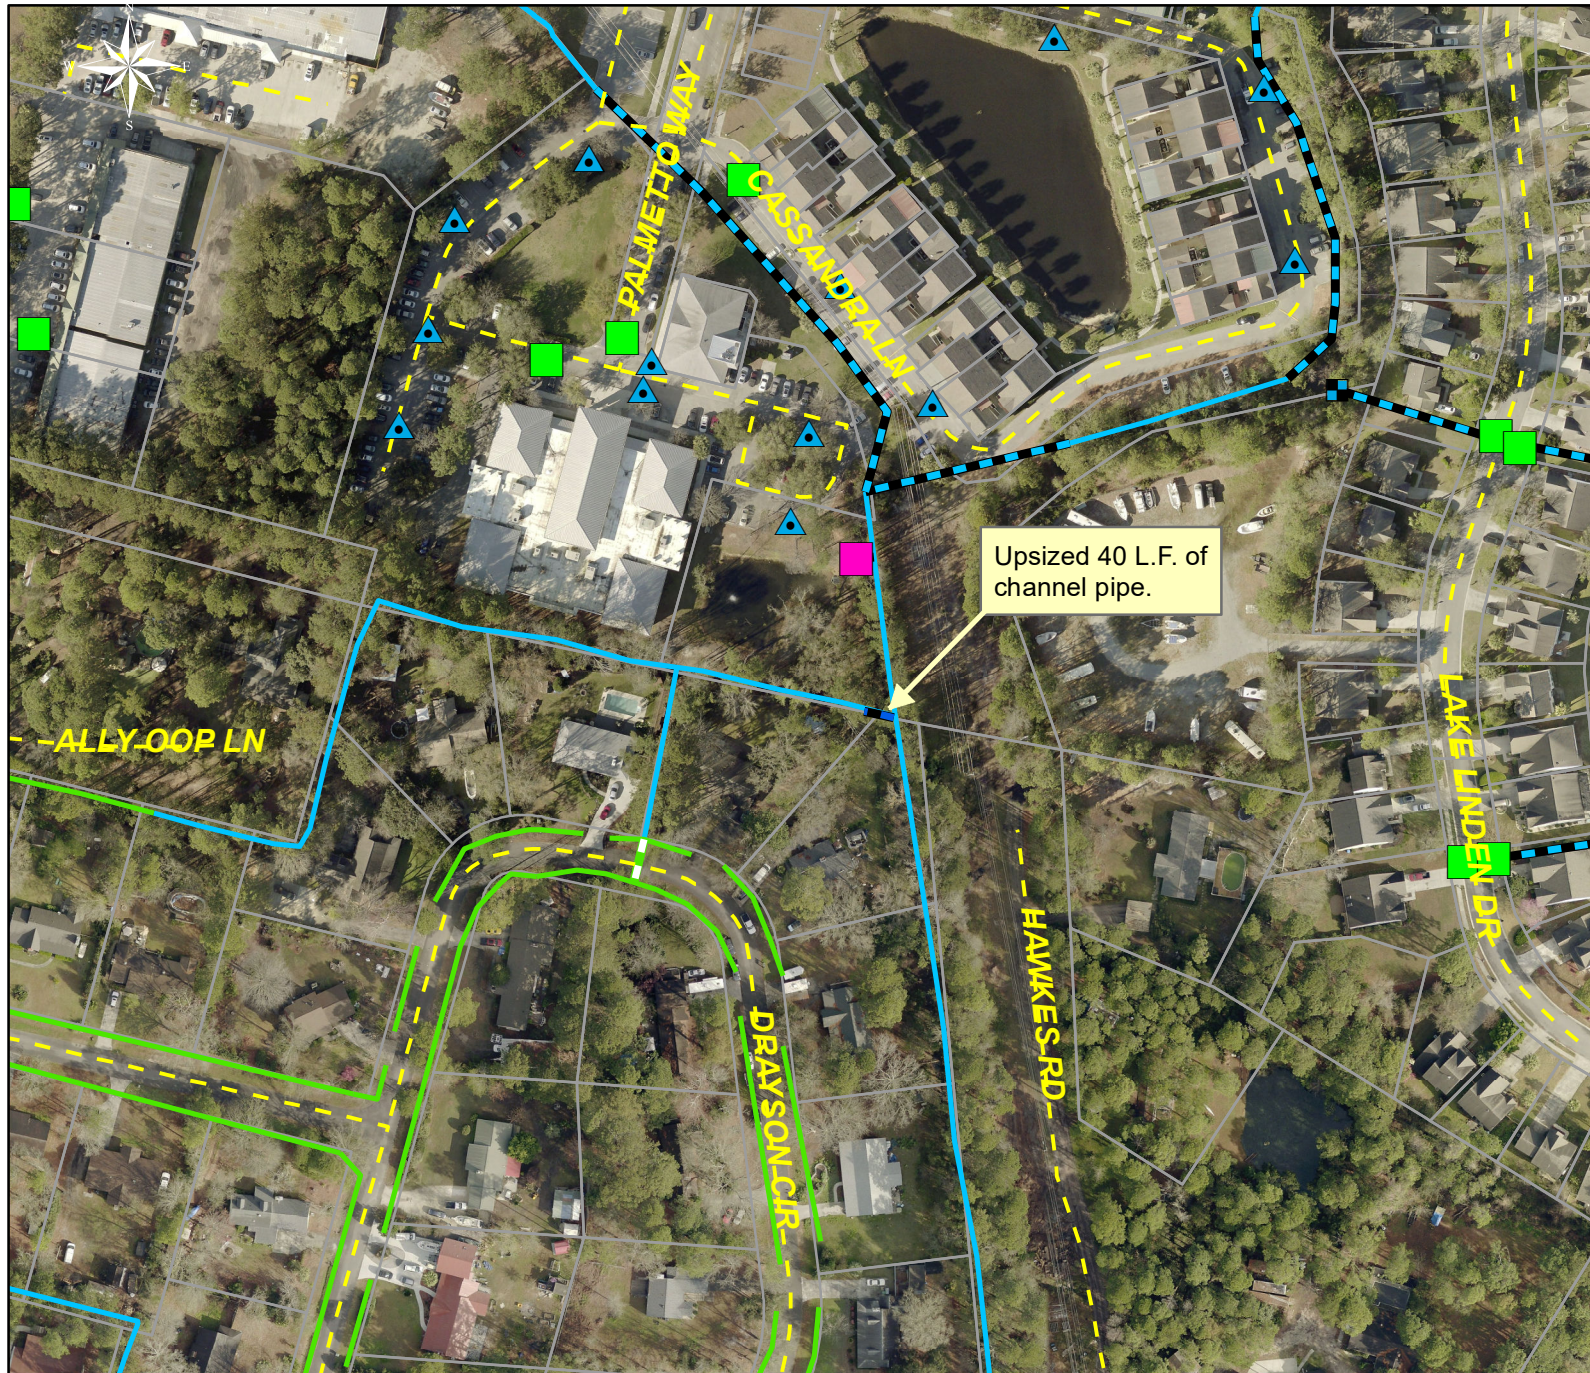

Project: Hawkes Road Channel

Activity: Routine/  
Preventive  
Maintenance

Project #:  
2025-580

Township/SW Dist:  
Bluffton/4

Completed:  
June 2025

### Legend

#### Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 37.5 75 150 225 300  
Feet

1 inch = 170 feet

Prepared By: BC Stormwater Management Utility

Date Print: 07/10/25

File: C:\project summaries map\Hawkes Road Channel\_2025-580
