

Beaufort County Public Works Stormwater Infrastructure

Project Summary: Simmonsville Road Drop-Off Center

Channel

Activity: Routine/Preventive Maintenance

Duration: 07/25/2025 - 08/27/2025

Narrative Description of Project:

Project improved 2,842 L.F. of drainage system. Grubbed, cleared and cleaned out 2,298 L.F. of channel, grubbed and cleared 544 L.F. of channel and perimeter of the pond. Cleaned out (1) catch basin and installed (1) bleeder pipe.


2026-505 / Simmonsville Road Drop-Off Center	Labor	Labor	Equipment	Material	Contractor	Total
Channel	Hours	Cost	Cost	Cost	Cost	Cost
AUDIT / Audit Project	5.00	\$126.00	\$0.00	\$0.00	\$0.00	\$126.00
CBCO / Catch basin - clean out	8.00	\$254.28	\$439.88	\$4.00	\$0.00	\$698.16
CCO / Channel - cleaned out	104.00	\$4,267.04	\$8,801.04	\$0.00	\$0.00	\$13,068.08
CGRB / Channel - grubbed	280.00	\$7,467.84	\$11,475.07	\$0.00	\$0.00	\$18,942.91
CLJS / Cleaned up jobsite	56.00	\$2,345.76	\$1,727.84	\$0.00	\$0.00	\$4,073.60
HAUL / Hauling	131.00	\$4,495.10	\$12,195.81	\$4,283.86	\$0.00	\$20,974.77
PGC / Pond - Grubb and Clear	80.00	\$3,166.40	\$1,727.84	\$266.93	\$0.00	\$5,161.17
Grand Total	664.00	\$22,122.42	\$36,367.48	\$4,554.79	\$0.00	\$63,044.69


Before During After







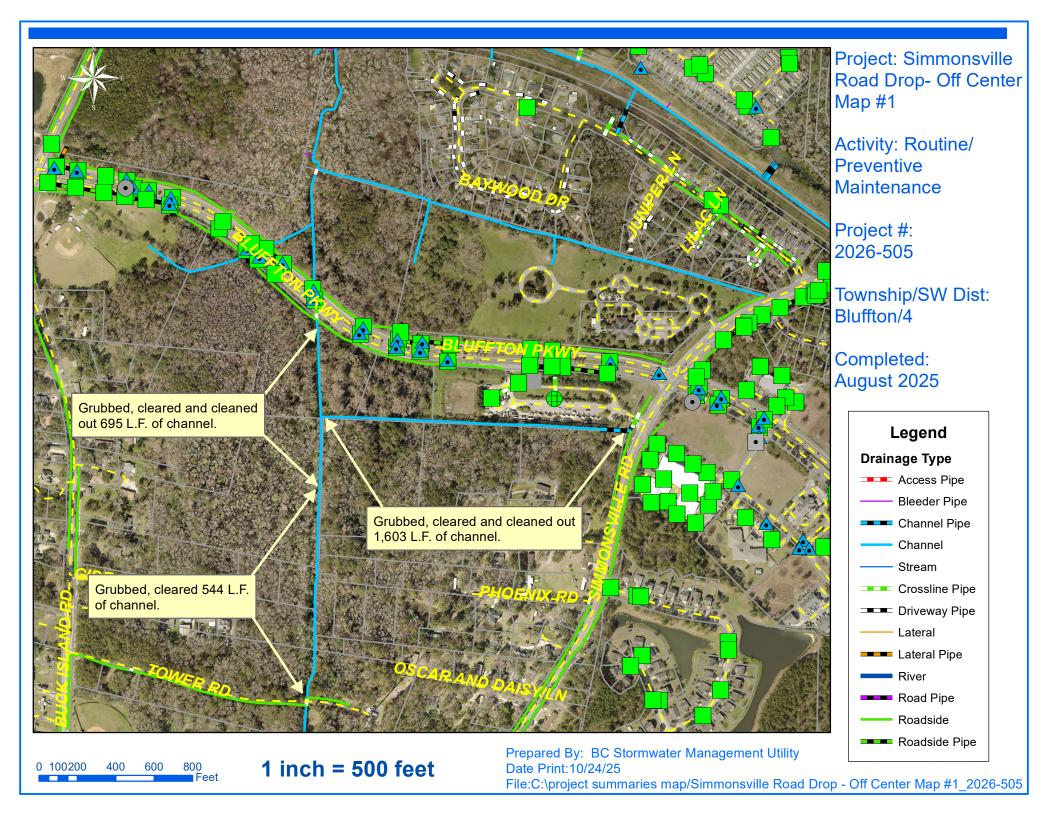

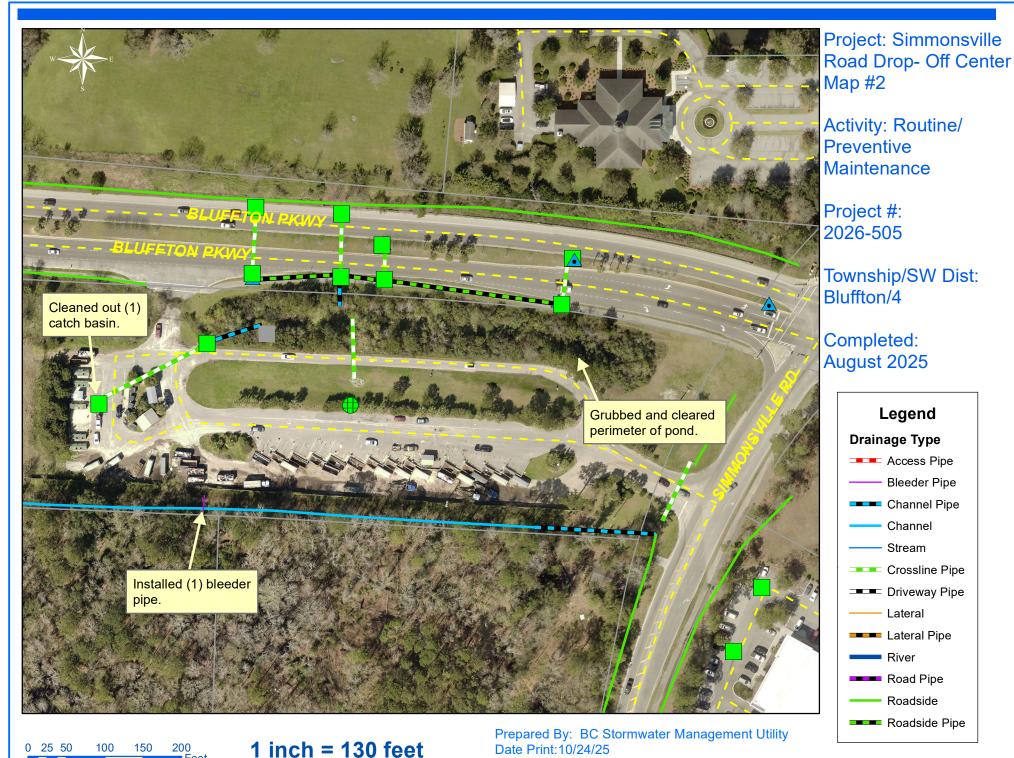

File:C:\project summaries map/Simmonsville Road Drop - Off Center Map #2_2026-505

Legend

Bleeder Pipe

Channel Stream

Lateral

River

Roadside
