

Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Pine Grove Road Channel

Activity: Drainage Improvement Duration: 10/02/2020-10/19/2020

Narrative Description of Project:

Project improved 1,163 L.F. of drainage system. Dismantle trees and cleared ditch bank. Grubbed and cleared 350 L.F. of workshelf. Cleaned out 813 L.F. of channel. Installed (1) access pipe and rip rap. Hand seeded for erosion control.

2020-023A / Pine Grove Road	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
APINS / Access pipe - installed	32.0	\$721.36	\$175.99	\$376.58	\$0.00	\$203.52	\$1477.45
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
CCO / Channel - cleaned out	52.0	\$1,144.44	\$167.37	\$24.27	\$0.00	\$305.28	\$1,641.36
DEBREM / Debris Removal - Jobsite	8.0	\$183.92	\$113.28	\$101.75	\$0.00	\$0.00	\$398.95
HAUL / Hauling	28.0	\$561.96	\$416.08	\$1,108.22	\$0.00	\$0.00	\$2,086.26
NONPRO / Non-Professional Services	0.0	\$0.00	\$0.00	\$0.00	\$2,000.00	\$0.00	\$2,000.00
RRI / Rip Rap - Installed	16.0	\$333.60	\$76.72	\$459.36	\$0.00	\$101.76	\$971.44
WSDR / Workshelf - Dressed	20.0	\$439.56	\$34.32	\$13.04	\$0.00	\$105.84	\$592.76
WSGRB / Workshelf - Grubbed	48.0	\$1,022.56	\$429.75	\$56.78	\$0.00	\$407.04	\$1,916.13
2020-023A / Pine Grove Road Project Sub Total	205.5	\$4,440.09	\$1,413.51	\$2,140.00	\$2,000.00	\$1,123.44	\$11,117.03
Grand Total	205.5	\$4,440.09	\$1,413.51	\$2,140.00	\$2,000.00	\$1,123.44	\$11,117.03

(Before)




(During)



(Ending)



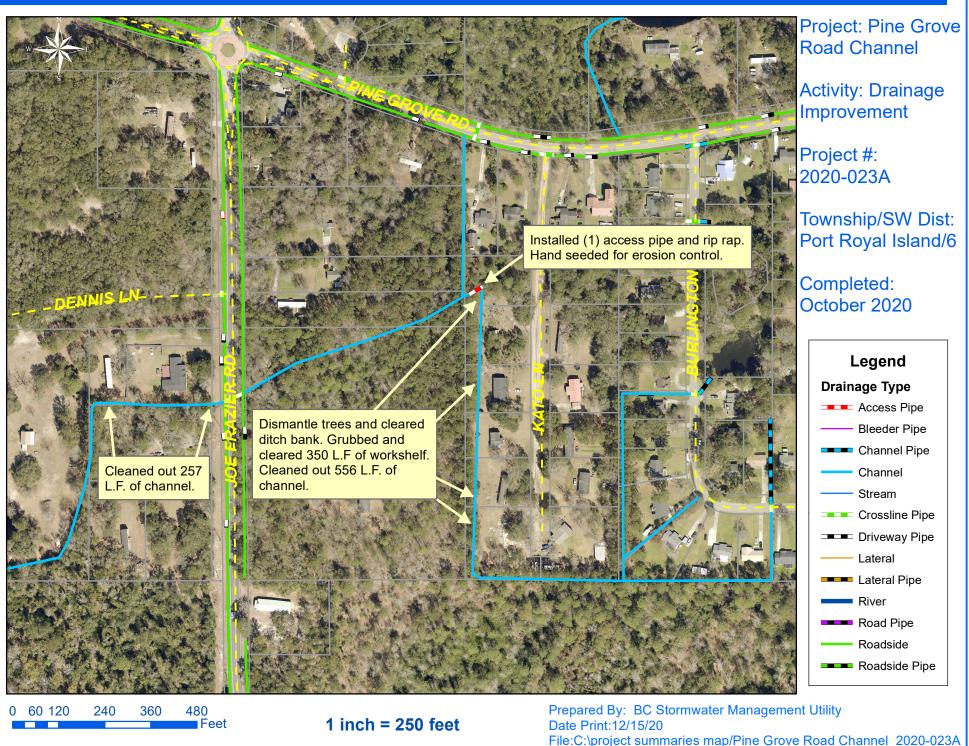

File:C:\project summaries map/Pine Grove Road Channel_2020-023A
