

**Project Summary:** Jesse Chisholm Road

**Activity:** Routine/Preventive Maintenance

**Duration:** 06/25/2021 - 04/26/2022

## **Narrative Description of Project:**

Project improved 5,160 L.F. of drainage system. Cleaned out 4,848 L.F. of channel ditch and 312 L.F. of roadside ditch. Installed (1) access pipe and rip rap for erosion control.

2021-554 / Jesse Chisholm Road	Labor	Labor	<b>Equipment</b>	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Cost	Cost
APEX / Access Pipe - Extended	16.00	\$520.56	\$265.20	\$1,027.11	\$0.00	\$337.52	\$2,150.39
APINS / Access pipe - installed	29.00	\$857.69	\$376.80	\$2,179.94	\$0.00	\$577.27	\$3,991.70
AUDIT / Audit Project	1.00	\$32.74	\$0.00	\$0.00	\$0.00	\$20.21	\$52.95
BKFILL / Back Fill	24.00	\$689.04	\$241.11	\$165.28	\$0.00	\$467.92	\$1,563.35
CCO / Channel - cleaned out	112.00	\$3,578.94	\$951.75	\$641.58	\$0.00	\$2,209.20	\$7,381.47
HAUL / Hauling	66.00	\$2,209.08	\$1,257.96	\$2,773.97	\$0.00	\$1,381.22	\$7,622.23
HEQ / Haul equipment	6.00	\$189.51	\$17.40	\$24.15	\$0.00	\$116.98	\$348.04
RRI / Rip Rap - Installed	16.00	\$438.32	\$34.80	\$65.55	\$0.00	\$305.36	\$844.03
Grand Total	270.00	\$8,515.87	\$3,145.02	\$6,877.58	\$0.00	\$5,415.68	\$23,954.16

**Before** 




**During** 



**After** 



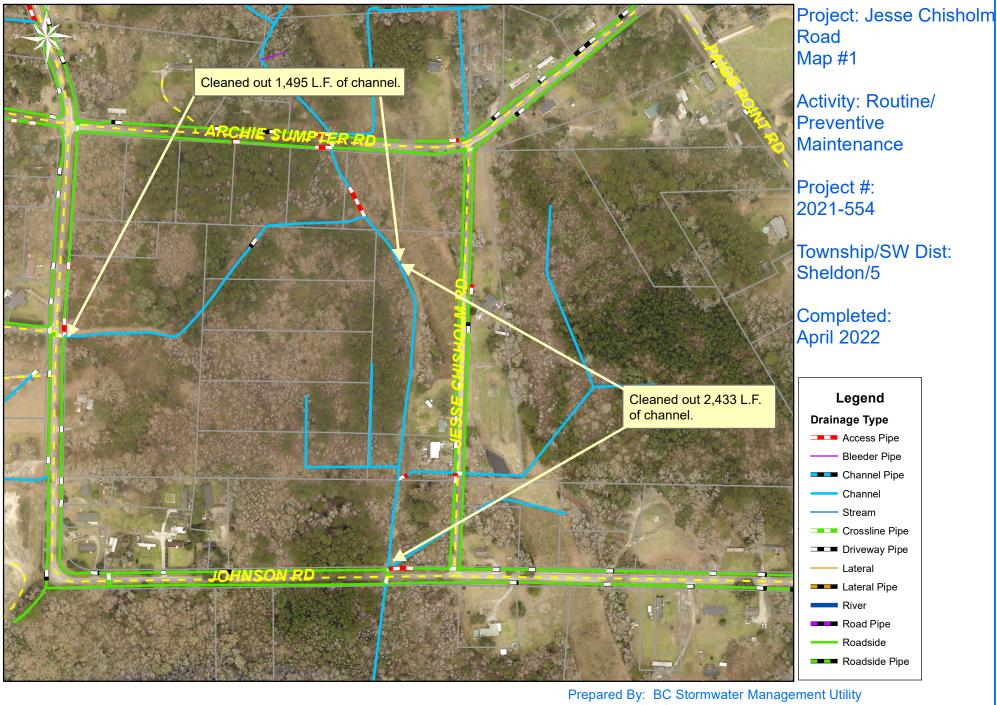


0 55110 220 330 440 Fee

1 inch = 330 feet

Prepared By: BC Stormwater Management Utility
Date Print:11/01/22

File:C:\project summaries map/Jesse Chisholm Rd Map 1\_2021-554

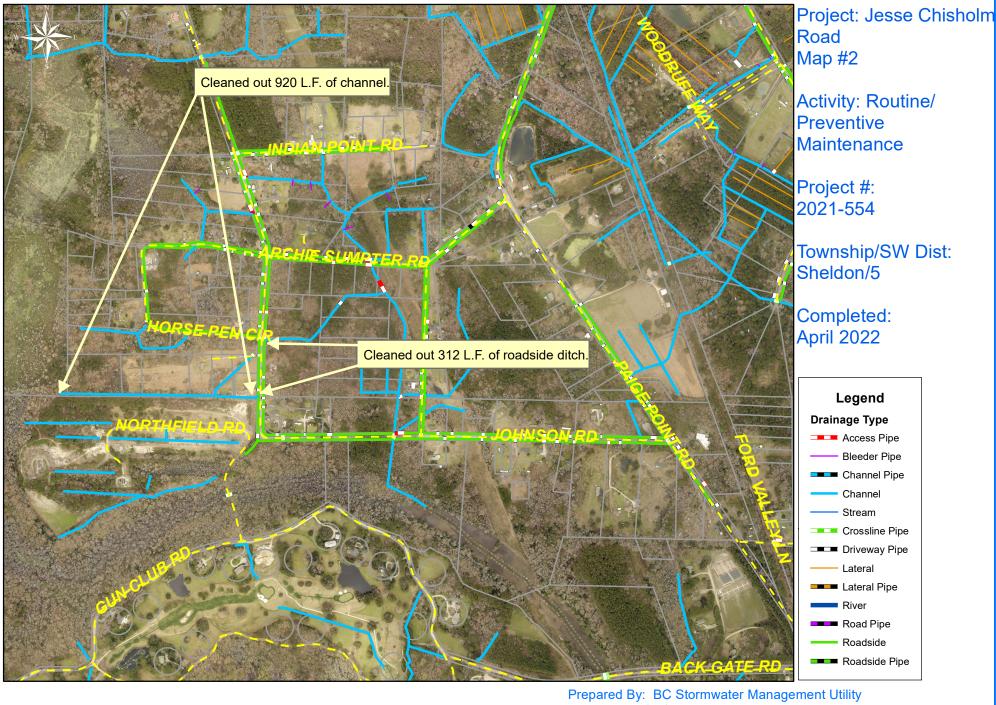


0 150300 600 900 1,200 Feet

1 inch = 830 feet

Prepared By: BC Stormwater Management Utility Date Print:11/01/22

File:C:\project summaries map/Jesse Chisholm Rd Map 2\_2021-554

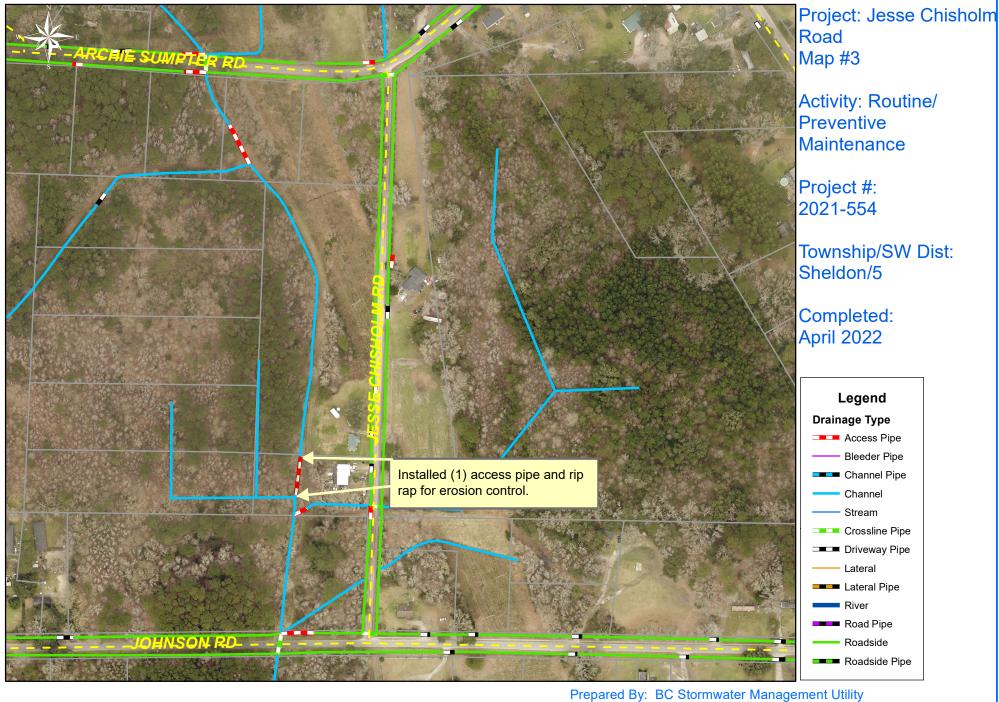

1 inch = 250 feet

Prepared By: BC Stormwater Management Utility
Date Print:11/01/22
File:C:\project summaries map/Jesse Chisholm Rd Map 3\_2021-554

0 40 80 160 240 320 Feet
