



Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: SCDOT - Monson Street / Boundary Street

Project #: 2010-045

Completed: Sep-09

Narrative Description of Project:

Cleaned out (9) catch basins. Jetted (5) crosslines pipes and 417 L.F. of roadside pipe.

Material Cost, Rental Equipment Summary, and Labor

Material	Unit	Cost/Unit	Qty	Cost
Water	gallon	\$0.01	10,500	\$105.00
Diesel	gallon	\$2.20	77.0	\$169.02
Labor	hours		43.0	\$1,372.18
Total Cost of Materials, Rental Equip., and Labor				\$1,646.20

Note: Labor cost includes the employee's salary plus fringe benefits.

Equipment Cost

Item	Asset	Cost/Hour	Hrs.	Cost
Vacuum Truck	22812	\$20.30	21.0	\$426.30
Total Equipment Cost				\$426.30

Cost/hour excludes fuel cost.

Total Cost: \$2,072.50

Site Photographs

Before




During



After



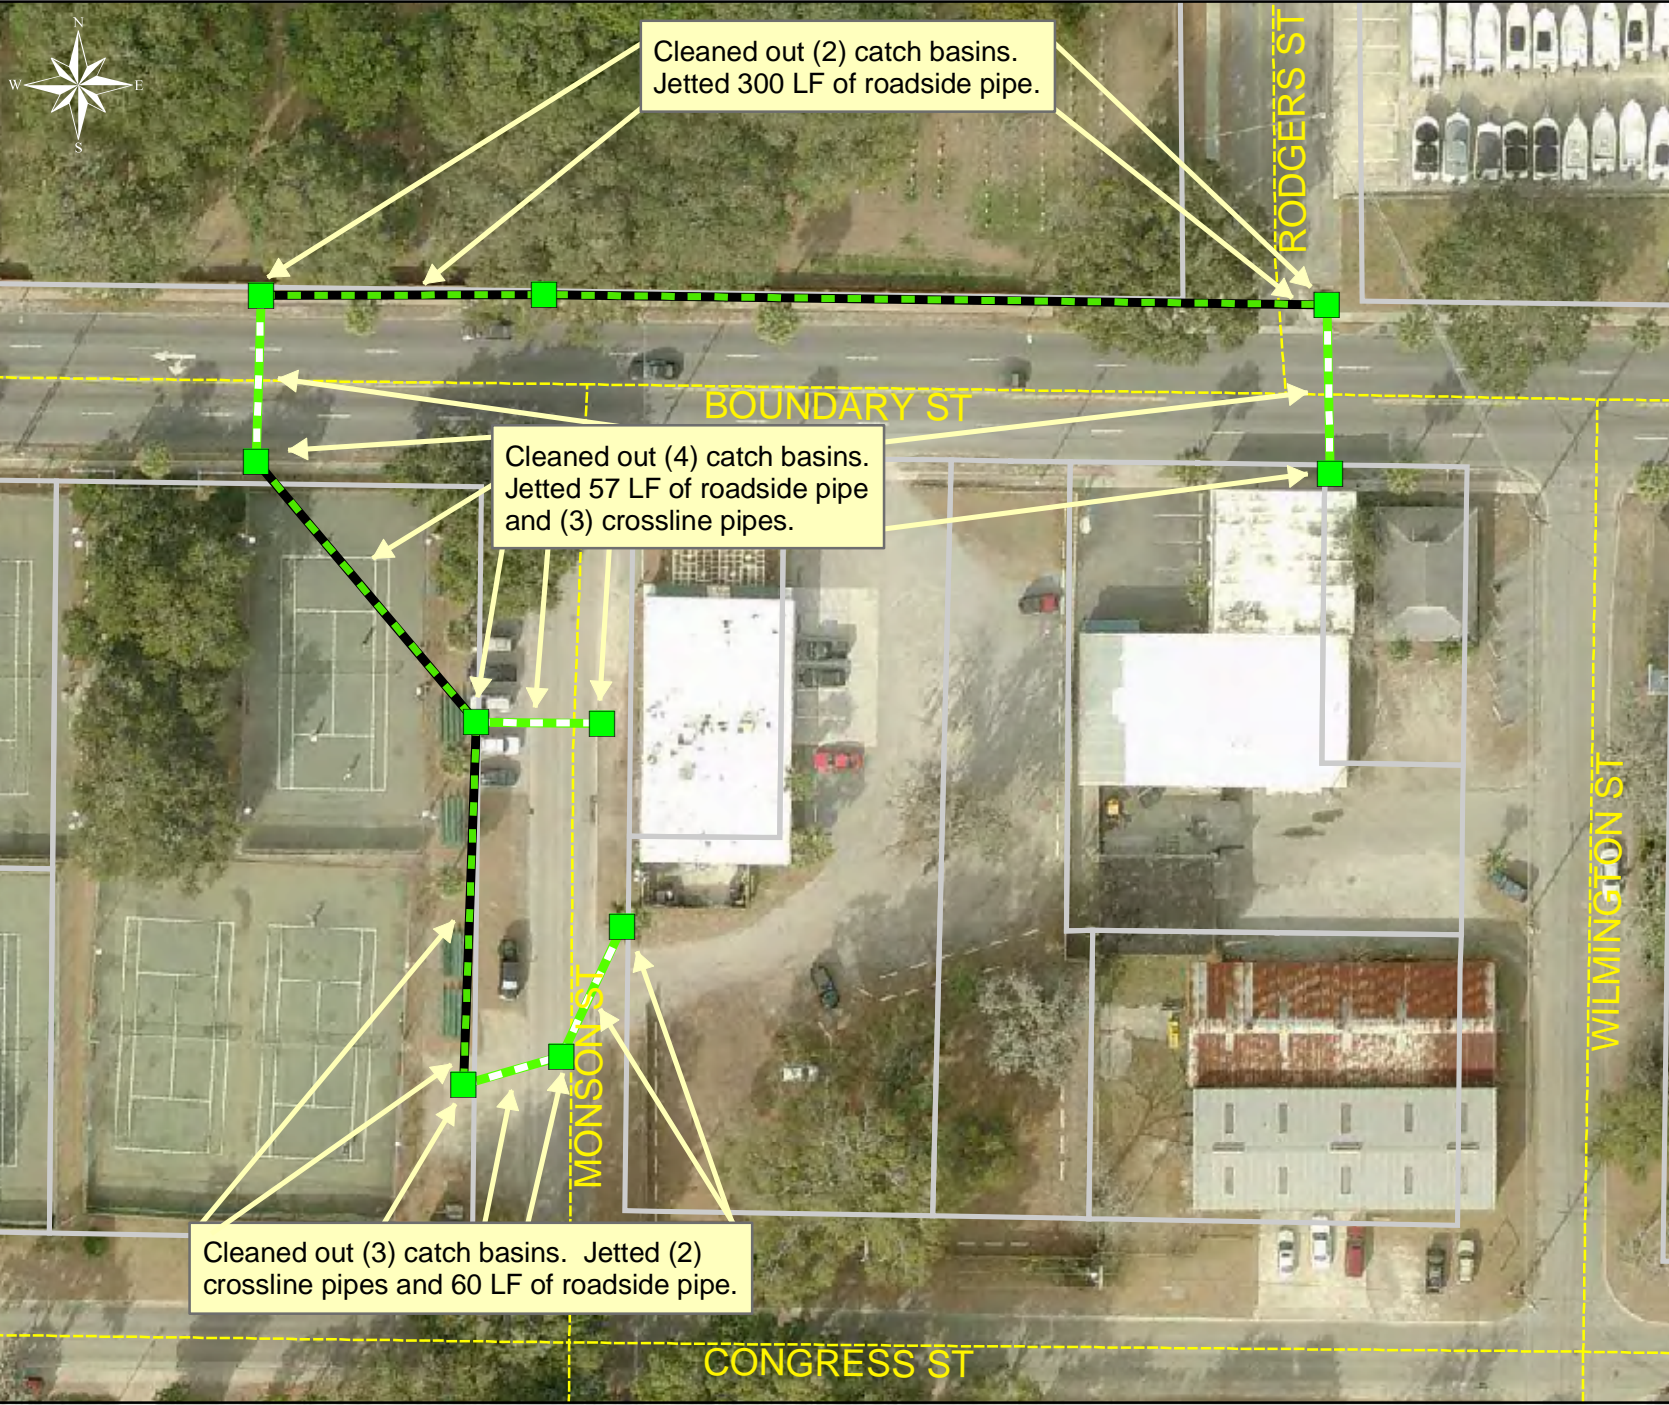

Project: SCDOT -
Monson Street/
Boundary Street
(Reimbursement)

Activity: Vacuum
Truck

Project #:
2010-045

Township: City
of Beaufort

Completed:
September 2009

Legend

Drainage Type

- Rivers
- Streams
- Outfall Ditch
- Lateral
- Roadside
- Roadside Pipe
- Crossline
- Driveway
- Access Pipe
- Piped Ditch
- Bleeder Ditch
- Parcels



1 inch equals 64 feet
