



Beaufort County Public Works

Stormwater Infrastructure

Project Summary

Project Summary: Royal Pines Blvd Outfall

Narrative Description of Project:

Project improved 1,015 L.F. of drainage system. Grubbed, cleared and reconstructed 250 L.F. of outfall ditch and workshelf. Cleaned out 765 L.F. of outfall ditch. Jetted (1) crossline pipe and (2) access pipes. Hydroseeded for erosion control.

Completion: Aug-11

2012-502 / Royal Pines Blvd Outfall	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	1.0	\$20.48	\$0.00	\$0.00	\$0.00	\$0.00	\$20.48
HAUL / Hauling	28.5	\$592.64	\$339.41	\$611.47	\$0.00	\$0.00	\$1,543.52
HYDR / Hydroseeding	12.0	\$261.48	\$41.16	\$266.53	\$0.00	\$0.00	\$569.17
ODCO / Outfall ditch - cleaned out	51.0	\$1,141.28	\$152.74	\$114.09	\$0.00	\$0.00	\$1,408.11
ODCON / Outfall ditch - constructed	27.0	\$618.70	\$267.57	\$62.18	\$0.00	\$0.00	\$948.45
ODGRB / Outfall ditch - grubbed	66.0	\$1,527.44	\$123.41	\$138.07	\$0.00	\$0.00	\$1,788.92
OFPJ / Outfall Pipe - Jetted	10.0	\$214.15	\$0.00	\$0.00	\$0.00	\$0.00	\$214.15
Indirect Labor, Services and Supplies	0.0	\$0.00	\$0.00	\$0.00	\$0.00	\$3,001.08	\$3,001.08
2012-502 / Royal Pines Blvd Outfall Sub Total	195.5	\$4,376.17	\$924.29	\$1,192.35	\$0.00	\$3,001.08	\$9,493.88
Grand Total	195.5	\$4,376.17	\$924.29	\$1,192.35	\$0.00	\$3,001.08	\$9,493.88

Before



During



After



Project: Royal Pines Blvd Outfall
Map 1

Activity: Drainage
Maintenance














Project #:
2012-502

Township: Lady's
Island

Completed:
August 2011

Legend

Drainage Type

-  River
-  Stream
-  Outfall
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Crossline
-  D/W
-  Access
-  Piped
-  Bleeder
-  Parcels

Grubbed, cleared and reconstructed
250 LF of outfall ditch and workshelp.
Hydroseeded for erosion control.

Cleaned out 240 LF
of outfall ditch.

Cleaned out 395 LF
of outfall ditch.

Cleaned out 130 LF
of outfall ditch.



1 inch = 183 feet

Prepared By: BC Stormwater Management Utility

Date Print: 2/21/12

File: C:/sethdata/projects/projectmaps/Royal Pines Blvd 12-502

Project: Royal Pines Blvd Outfall
Map 2

Activity: Vacuum
Truck














Project #:
2012-502


Township: Lady's
Island

Completed:
Augues 2011

Legend

Drainage Type

-  River
-  Stream
-  Outfall
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Crossline
-  D/W
-  Access
-  Piped
-  Bleeder
-  Parcels

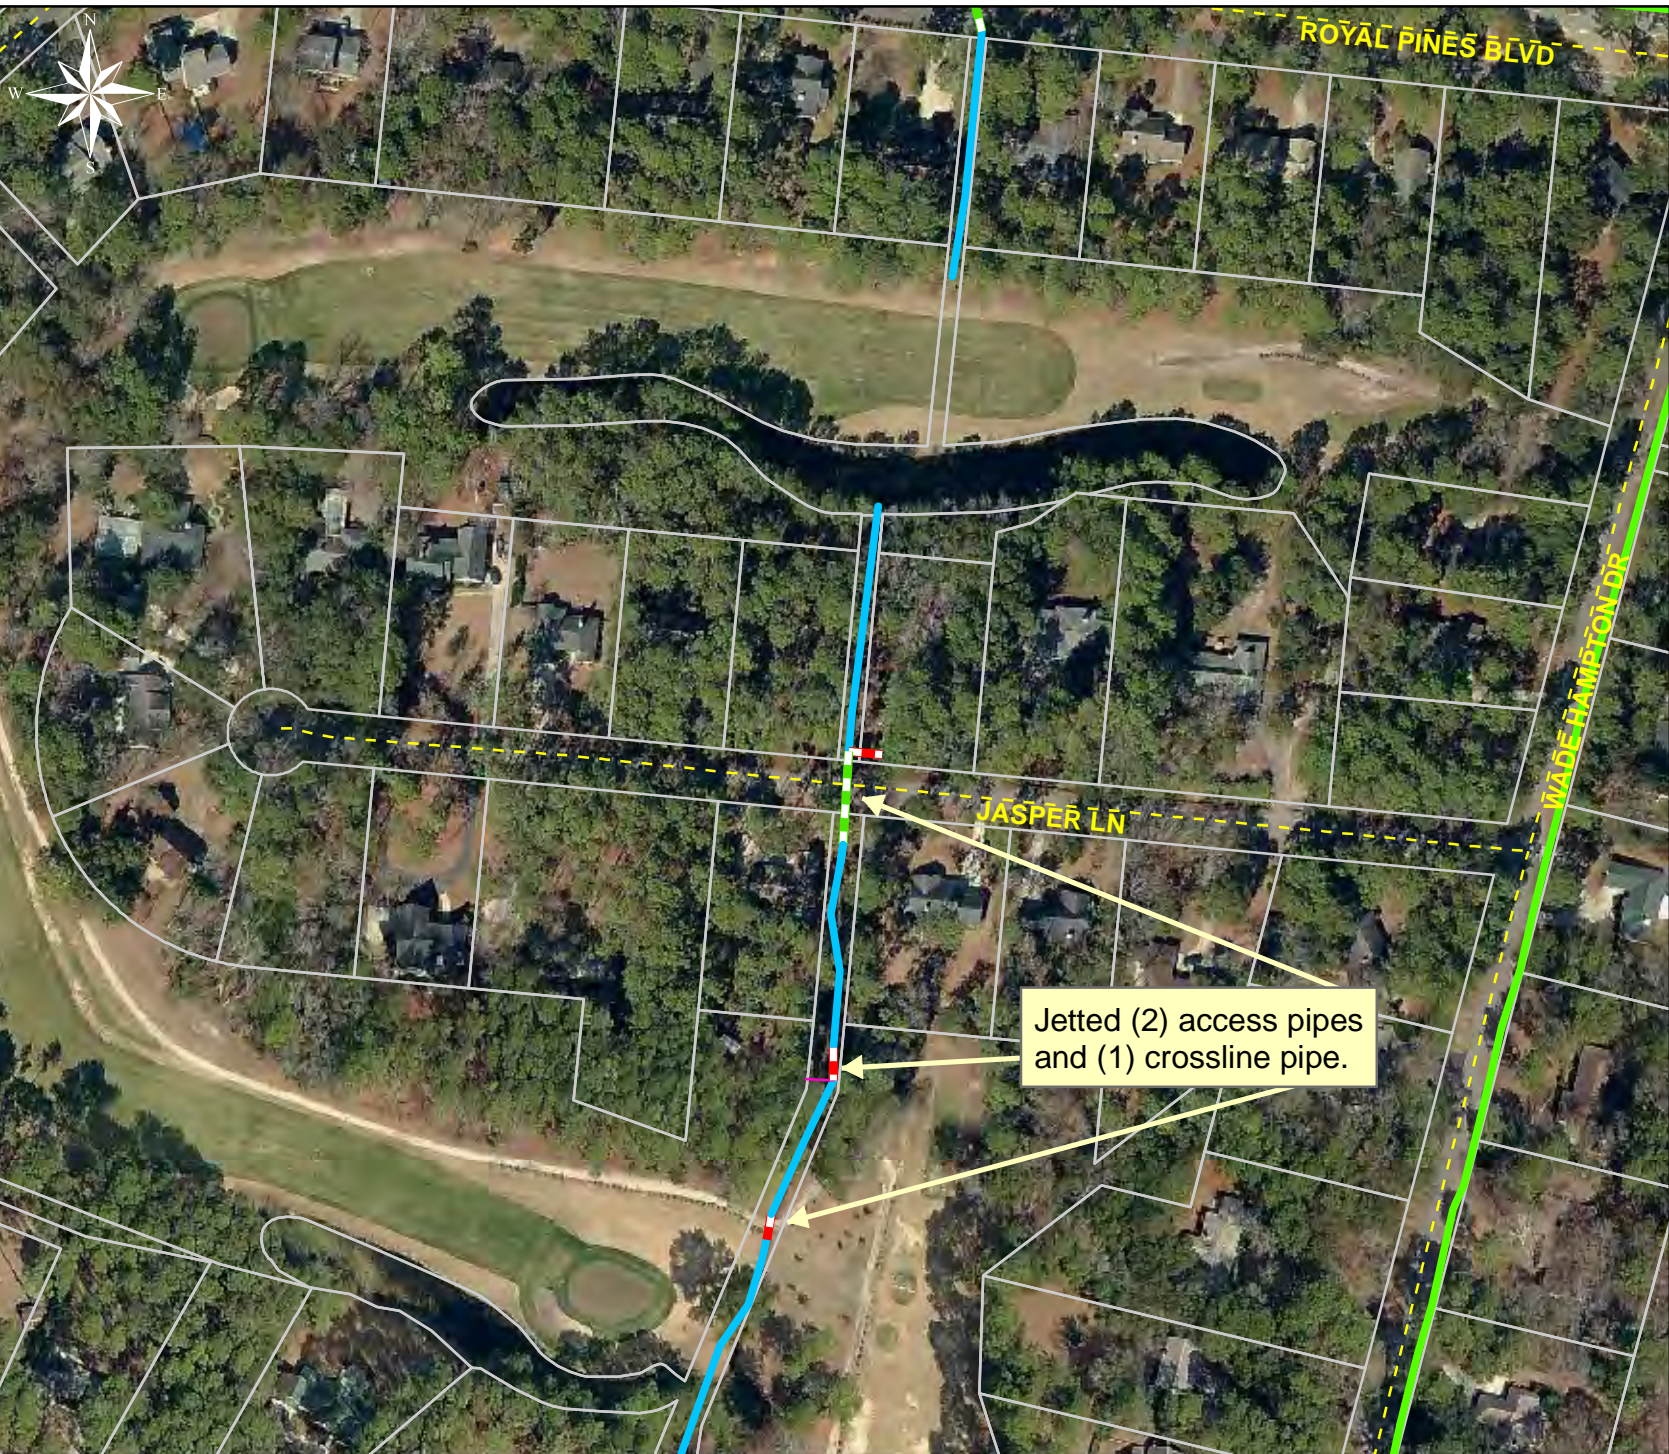

1 inch = 183 feet

Prepared By: BC Stormwater Management Utility

Date Print: 2/21/12

File: C:/sethdata/projects/projectmaps/Vac/Royal Pines Blvd 12-502
