



Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: Lawson Road

Narrative Description of Project:

Project improved 1,246 L.F. of drainage system. Cleaned out 500 L.F. of outfall ditch and 738 L.F. of roadside ditch. Cleaned out (1) catch basin. Jetted (1) crossline pipe, (3) driveway pipes and 8 L.F. of outfall pipe.

Completion: Apr-12

2012-582 / Lawson Road	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	0.5	\$10.24	\$0.00	\$0.00	\$0.00	\$0.00	\$10.24
DLO / Ditch Layout	15.0	\$338.60	\$20.35	\$8.14	\$0.00	\$0.00	\$367.09
DPJT / Driveway Pipe - Jetted	9.0	\$197.78	\$99.72	\$24.48	\$0.00	\$0.00	\$321.98
HAUL / Hauling	35.0	\$730.90	\$465.85	\$466.98	\$0.00	\$0.00	\$1,663.73
ODCO / Outfall ditch - cleaned out	30.0	\$677.20	\$219.97	\$7.24	\$0.00	\$0.00	\$904.41
RSDCL / Roadside Ditch - Cleanout	15.0	\$325.90	\$81.03	\$65.16	\$0.00	\$0.00	\$472.09
WSBH / Workshelf - Bush Hogged	10.0	\$204.80	\$59.61	\$24.62	\$0.00	\$0.00	\$289.03
Indirect Labor, Services and Supplies	0.0	\$0.00	\$0.00	\$0.00	\$0.00	\$1,661.36	\$1,661.36
2012-582 / Lawson Road Sub Total	114.5	\$2,485.42	\$946.53	\$596.62	\$0.00	\$1,661.36	\$5,689.92
Grand Total	114.5	\$2,485.42	\$946.53	\$596.62	\$0.00	\$1,661.36	\$5,689.92

Before



During



After




Project: Lawson Road Map 1

Activity: Drainage Maintenance

Project #: 2012-582

Township: Port Royal Island

Completed: April 2012

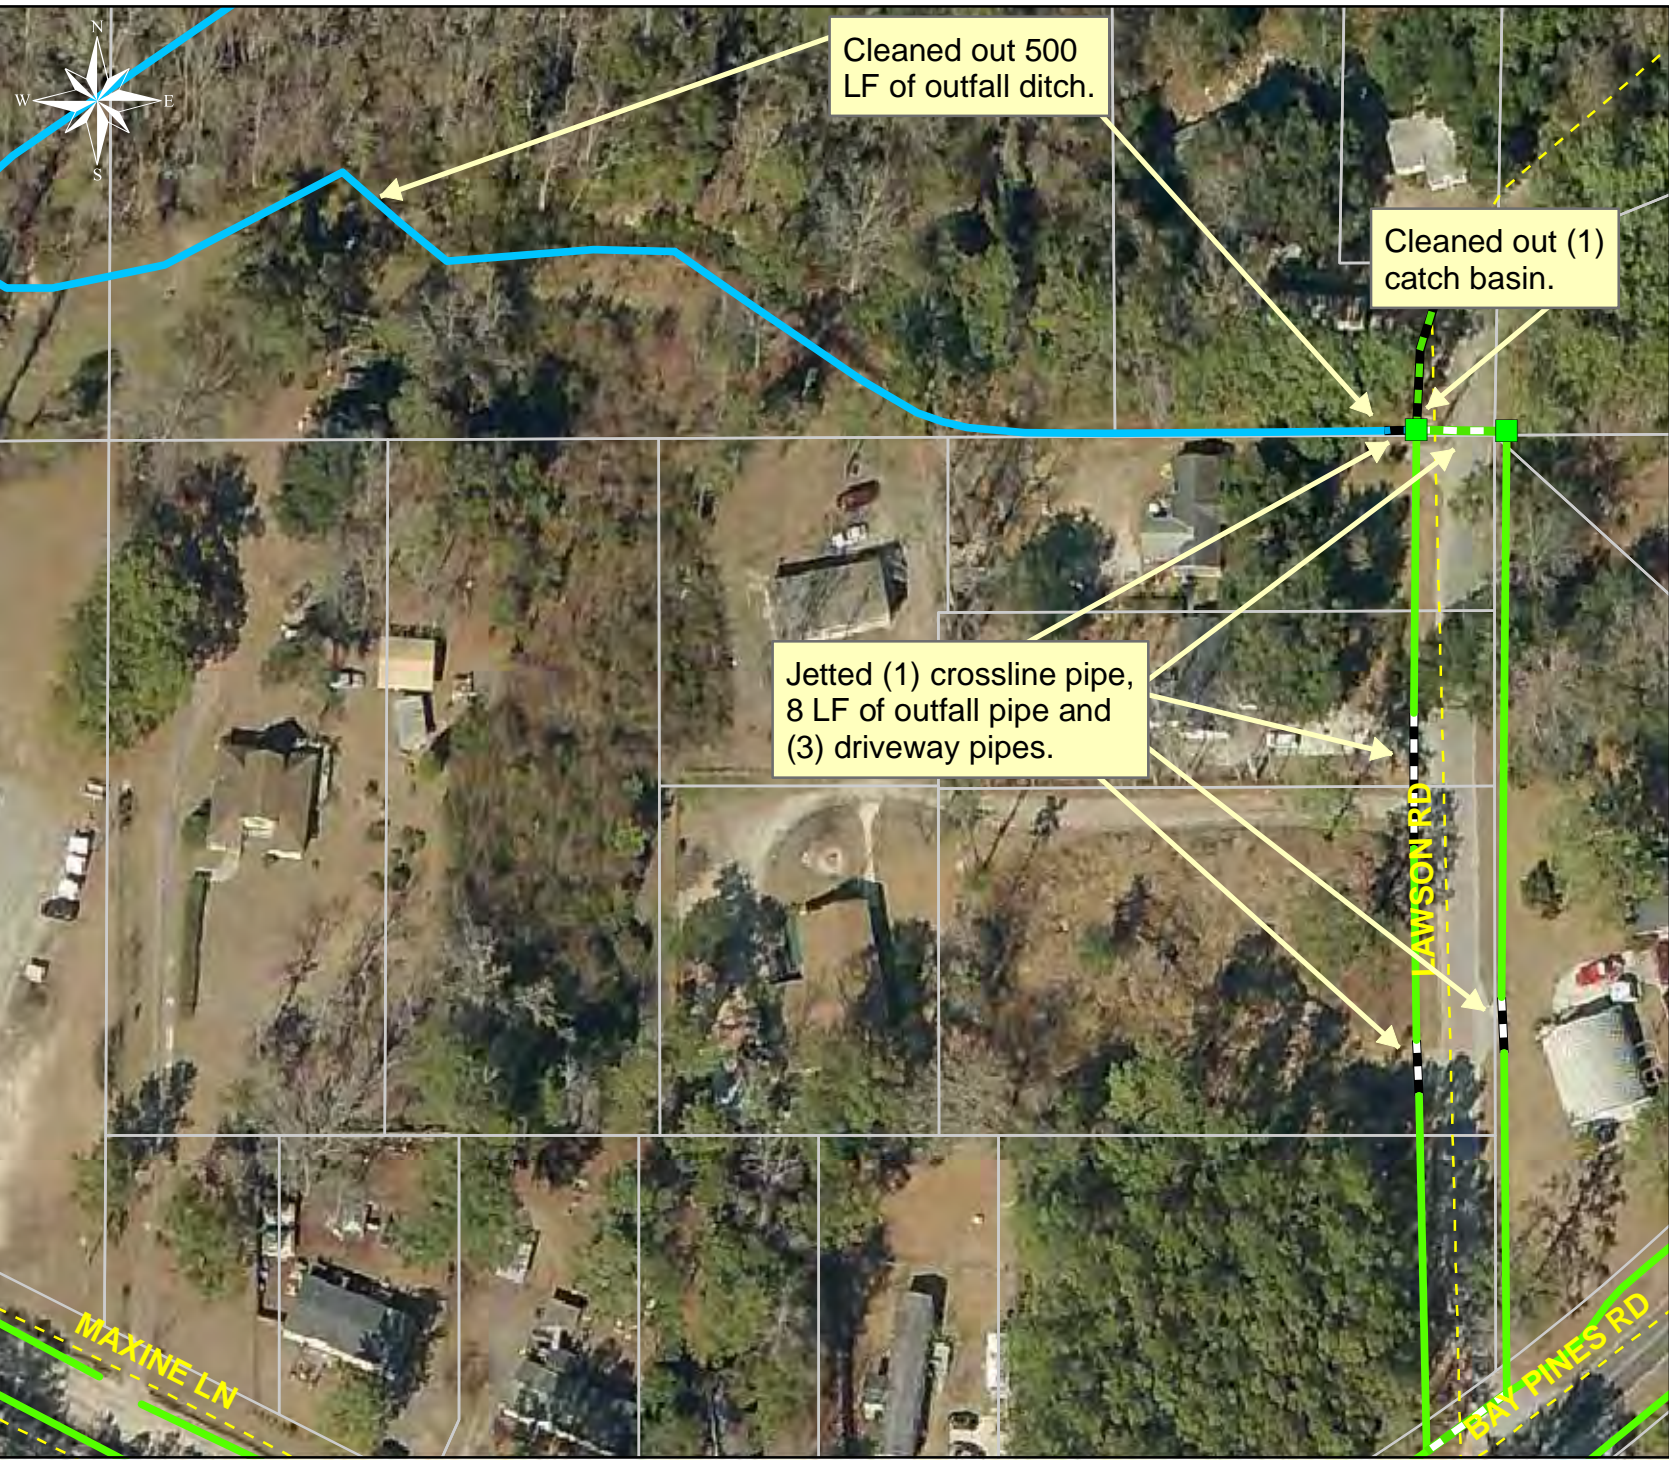

Legend

Drainage Type

- River
- Stream
- Outfall
- Lateral
- Lateral Pipe
- Roadside
- Roadside Pipe
- Crossline
- D/W
- Access
- Piped
- Bleeder
- Parcels



1 inch = 91 feet

Project: Lawson Road Map 2

Activity: Drainage Maintenance














Project #: 2012-582

Township: Port Royal Island

Completed: April 2012

Legend

Drainage Type

-  River
-  Stream
-  Outfall
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Crossline
-  D/W
-  Access
-  Piped
-  Bleeder
-  Parcels

Cleaned out 395 LF of roadside ditch.

Cleaned out 343 LF of roadside ditch.



1 inch = 91 feet
