



# Beaufort County Public Works Stormwater Infrastructure Project Summary

**Project Summary:** Albertha Fields Circle

**Activity:** Routine/Preventive Maintenance

**Narrative Description of Project:**

Project improved 1,953 L.F. of drainage system. Removed blockage from flowline. Cleaned out 1,953 L.F. of outfall ditch. Upsized (1) crossline pipe. Installed rip rap for erosion control.


**Completion:** Mar-13

2013-624 / Albertha Fields Circle	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	0.5	\$10.45	\$0.00	\$0.00	\$0.00	\$6.62	\$17.06
CPUP / Crossline Pipe - Upsized	40.0	\$916.80	\$237.20	\$1,227.79	\$0.00	\$399.00	\$2,780.79
HAUL / Hauling	51.5	\$1,125.28	\$551.05	\$2,523.63	\$0.00	\$707.27	\$4,907.22
ODCO / Outfall ditch - cleaned out	54.0	\$1,258.38	\$300.72	\$72.73	\$0.00	\$506.10	\$2,137.93
ONJV / Onsite Job Visit	20.0	\$507.82	\$80.40	\$50.54	\$0.00	\$380.33	\$1,019.09
PRRECON / Project Reconnaissance	8.0	\$204.13	\$78.54	\$33.40	\$0.00	\$146.35	\$462.42
RB / Remove blockage from flowline	10.0	\$227.95	\$79.60	\$21.23	\$0.00	\$91.15	\$419.93
<b>2013-624 / Albertha Fields Circle Sub Total</b>	<b>184.0</b>	<b>\$4,250.80</b>	<b>\$1,327.51</b>	<b>\$3,929.32</b>	<b>\$0.00</b>	<b>\$2,236.81</b>	<b>\$11,744.45</b>
<b>Grand Total</b>	<b>184.0</b>	<b>\$4,250.80</b>	<b>\$1,327.51</b>	<b>\$3,929.32</b>	<b>\$0.00</b>	<b>\$2,236.81</b>	<b>\$11,744.45</b>

Before



During

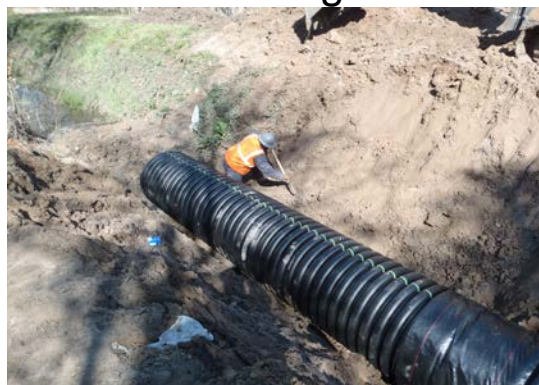

After




**Project: Albertha Fields Circle**

**Activity: Routine/ Preventive Maintenance**

**Project #: 2013-624**





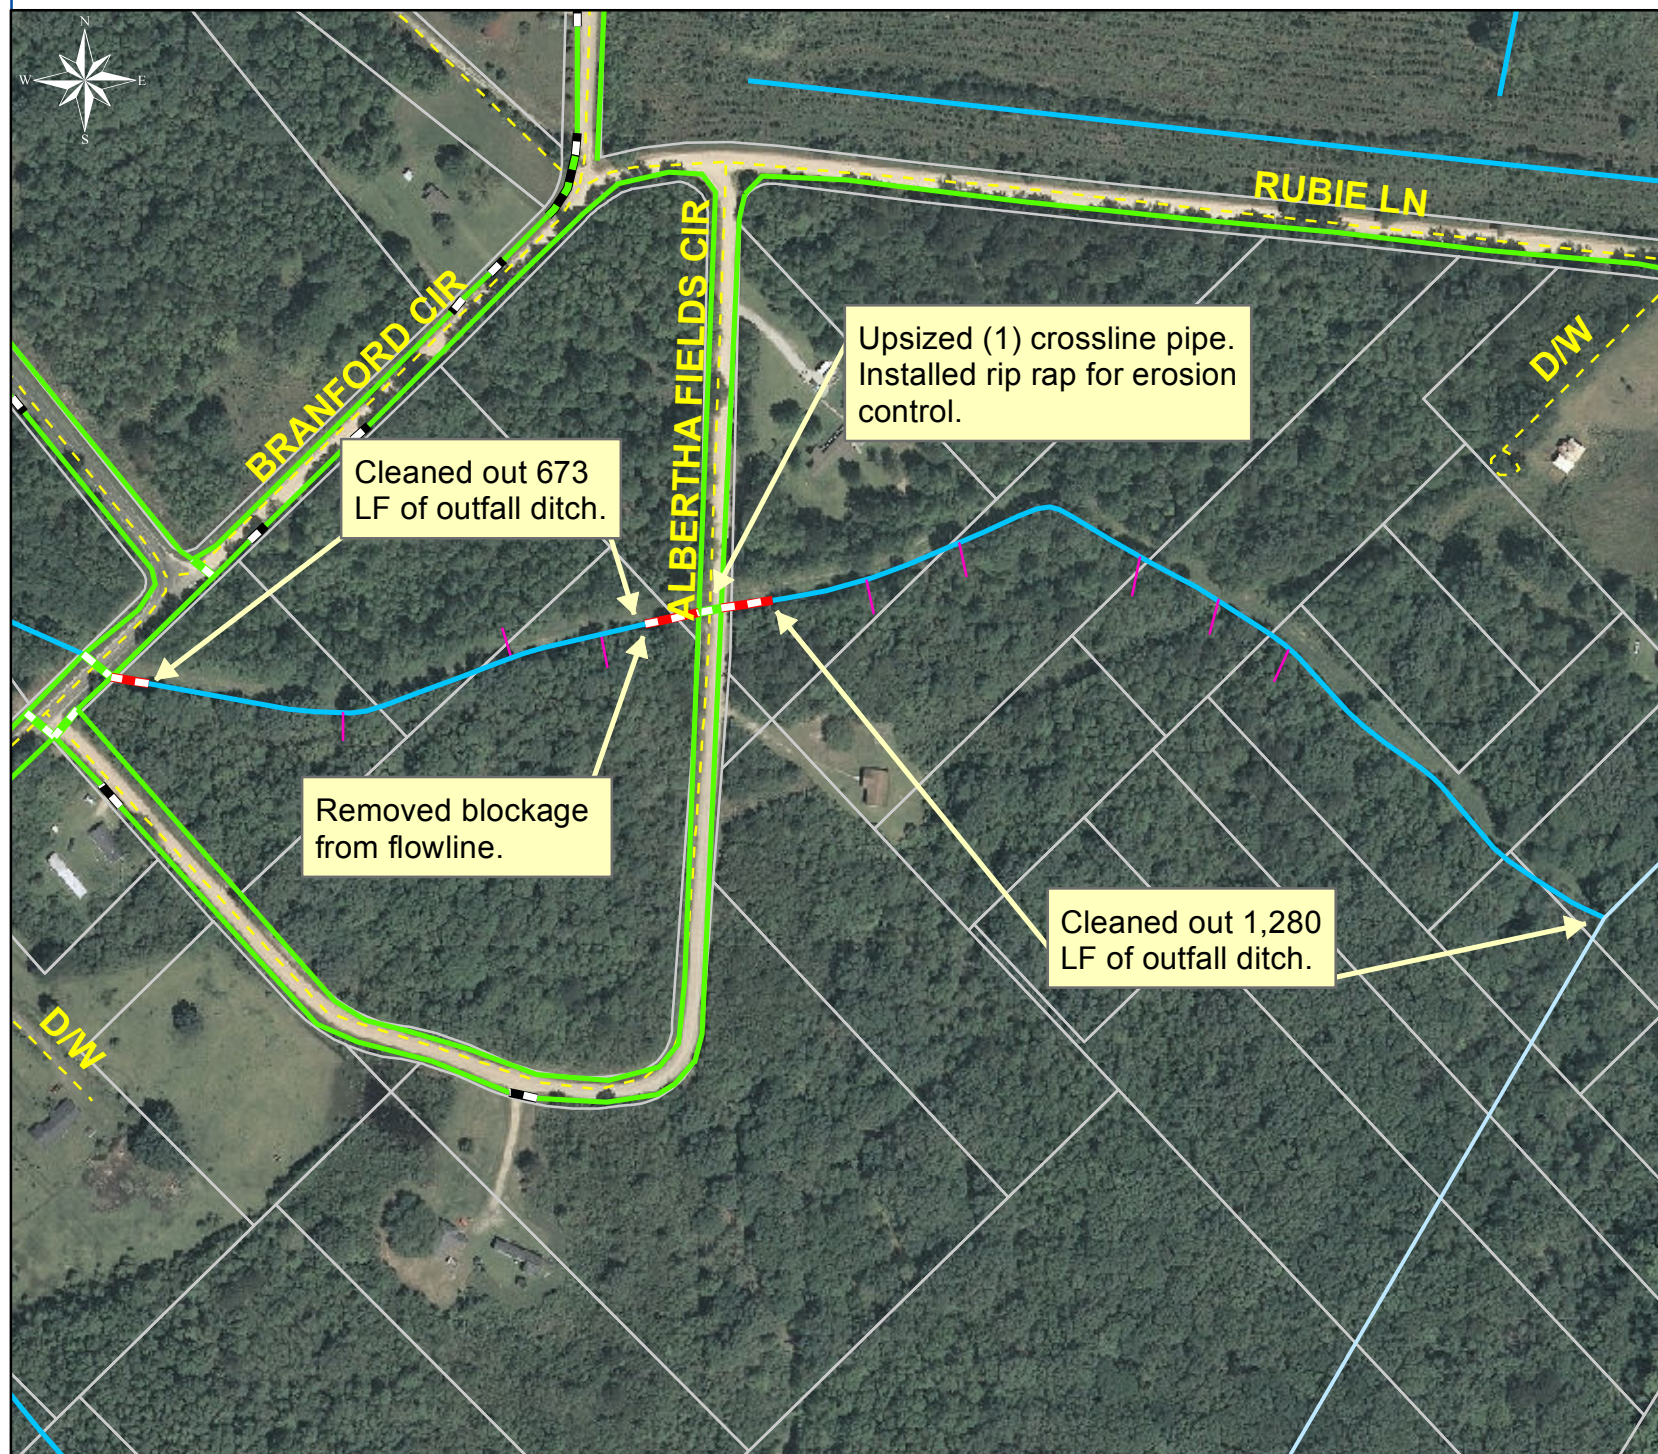










**Township: Sheldon**

**Completed: March 2013**



**Legend**

**TYPE**

-  River
-  Creek/Stream
-  River/Creek/Marsh BANK
-  Channel (fka Outfall)
-  Channel Pipe
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Road Pipe
-  Crossline Pipe
-  Driveway Pipe
-  Access Pipe
-  Bleeder Pipe
-  Parcels



**1 inch = 250 feet**
