Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Browns Island Road / Stroup Road

Narrative Description of Project:

Project improved 7,550 L.F. of drainage system. Cleaned out 6,454 L.F. of roadside ditch and 1,096 L.F. of outfall ditch. Jetted (2) crossline pipes and (13) diveway pipes.

Activity: Routine/Preventive Maintenance

Completion: Mar-13

2013-598 / Browns Island Road / Stroup Road	Labor	Labor	Equipment	Material	Contractor	Indirect	
	Hours	Cost	Cost	Cost	Cost	Labor	Total Cost
AUDIT / Audit Project	1.0	\$20.89	\$0.00	\$0.00	\$0.00	\$13.23	\$34.12
CLPJT / Crossline Pipe - Jetted	12.0	\$283.38	\$132.96	\$71.37	\$0.00	\$194.82	\$682.53
DPJT / Driveway Pipe - Jetted	6.0	\$141.69	\$66.48	\$27.45	\$0.00	\$97.41	\$333.03
HAUL / Hauling	201.0	\$4,410.85	\$2,150.70	\$933.72	\$0.00	\$2,914.50	\$10,409.77
HYDR / Hydroseeding	15.0	\$337.15	\$57.42	\$308.73	\$0.00	\$224.85	\$928.15
NONPRO / Non-Professional Services	0.0	\$0.00	\$0.00	\$0.00	\$27.25	\$0.00	\$27.25
ONJV / Onsite Job Visit	20.0	\$585.81	\$80.40	\$90.17	\$0.00	\$451.96	\$1,208.34
RSDCL / Roadside Ditch - Cleanout	386.0	\$8,627.41	\$2,594.65	\$600.24	\$0.00	\$5,659.17	\$17,481.47
2013-598 / Browns Island Road / Stroup Road Sub Total	641.0	\$14,407.18	\$5,082.61	\$2,031.68	\$27.25	\$9,555.94	\$31,104.66

Grand Total	641.0	\$14,407.18	\$5,082.61	\$2,031.68	\$27.25	\$9,555.94	\$31,104.66


Before










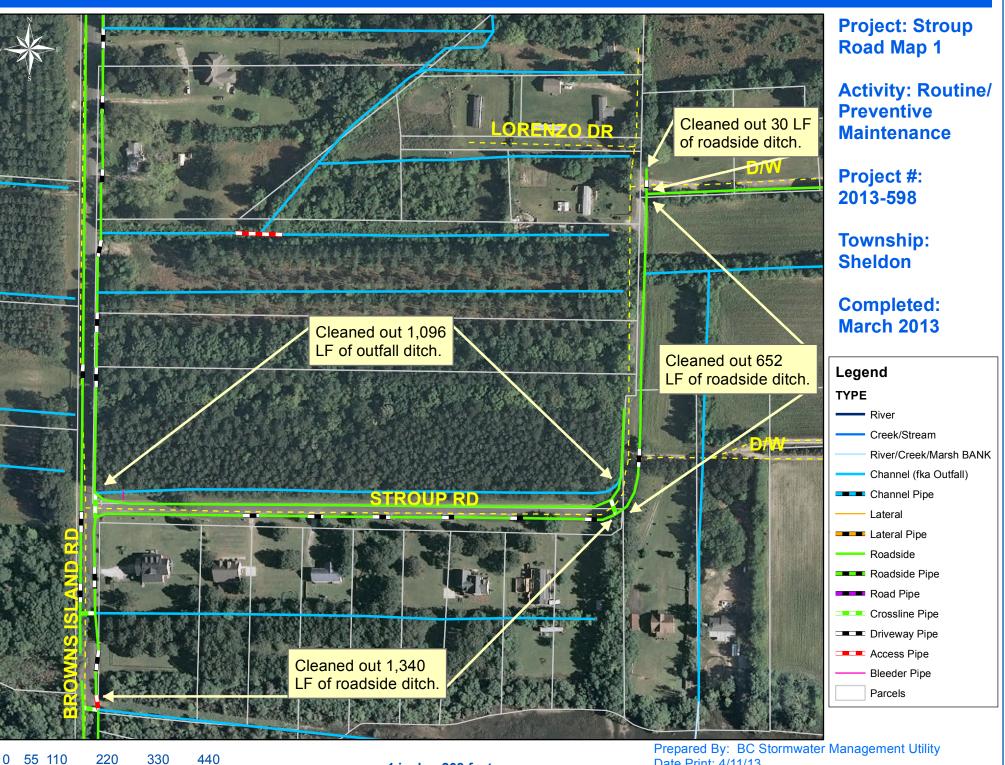

1 inch = 208 feet

Feet

Date Print: 4/11/13 File:C:/sethdata/projects/projectmaps/Stroup Rd 2013-598

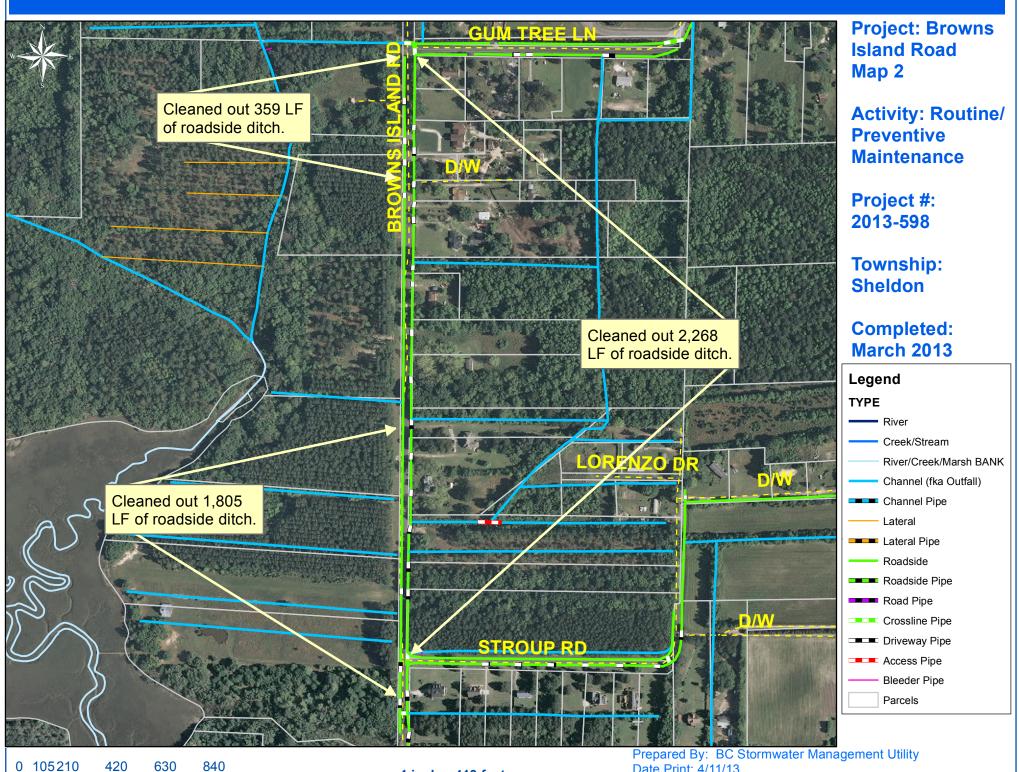

1 inch = 413 feet

Feet

Date Print: 4/11/13 File:C:/sethdata/projects/projectmaps/Browns Island Rd 2013-598

