## **Beaufort County Public Works** Stormwater Infrastructure

Project Summary

**Project Summary:** Myrtle Park

Activity: Routine/Preventive Maintenance

## Narrative Description of Project:

Project improved 600 L.F. of drainage system. Constructed 440 L.F. of valley drain. Raised (1) catch basin to correct elevation. Jetted (2) crossline pipes and 160 L.F. of outfall pipe. Hydroseeded for erosion control.

| 2013-612 / Myrtle Park           | Labor | Labor      | Equipment | Material | Contractor | Indirect   |                   |
|----------------------------------|-------|------------|-----------|----------|------------|------------|-------------------|
|                                  | Hours | Cost       | Cost      | Cost     | Cost       | Labor      | <b>Total Cost</b> |
| AUDIT / Audit Project            | 0.5   | \$10.45    | \$0.00    | \$0.00   | \$0.00     | \$6.62     | \$17.06           |
| CBCO / Catch basin - clean out   | 4.0   | \$124.88   | \$16.08   | \$12.48  | \$0.00     | \$97.88    | \$251.32          |
| COVD / Cleaned Out Valley Drains | 100.0 | \$2,168.60 | \$324.70  | \$184.77 | \$0.00     | \$1,171.60 | \$3,849.67        |
| HAUL / Hauling                   | 20.0  | \$437.00   | \$214.00  | \$124.80 | \$0.00     | \$244.20   | \$1,020.00        |
| HYDR / Hydroseeding              | 10.0  | \$208.70   | \$44.98   | \$109.59 | \$0.00     | \$132.30   | \$495.57          |
| OFPJ / Outfall Pipe - Jetted     | 11.0  | \$259.77   | \$121.88  | \$67.35  | \$0.00     | \$178.59   | \$627.58          |
| ONJV / Onsite Job Visit          | 3.0   | \$120.69   | \$12.06   | \$15.60  | \$0.00     | \$101.88   | \$250.23          |
| PRRECON / Project Reconnaissance | 14.0  | \$358.39   | \$28.14   | \$21.84  | \$0.00     | \$256.73   | \$665.10          |
| 2013-612 / Myrtle Park           | 162.5 | \$3,688.47 | \$761.84  | \$536.43 | \$0.00     | \$2,189.79 | \$7,176.53        |
| Sub Total                        |       |            |           |          |            |            |                   |

| Grand Total | 162.5 | \$3,688.47 | \$761.84 | \$536.43 | \$0.00 | \$2,189.79 | \$7,176.53 |
|-------------|-------|------------|----------|----------|--------|------------|------------|
|             |       |            |          |          |        |            |            |

## Before









After






Completion: Mar-13

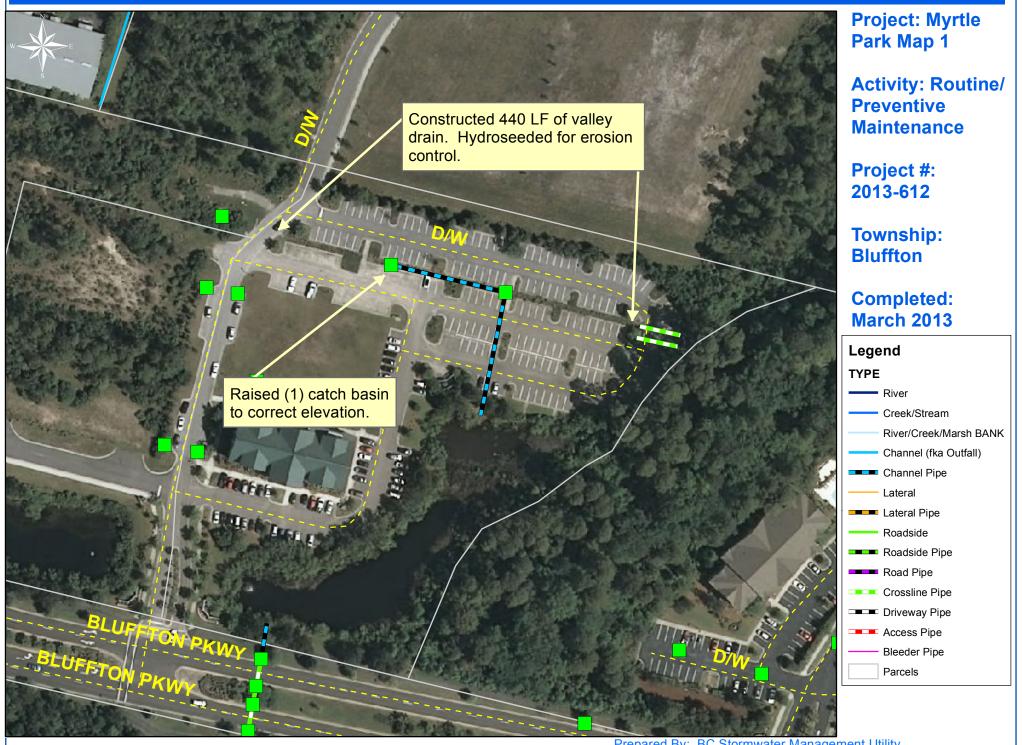

0 30 60 120 180 240 Feet

1 inch = 117 feet

Prepared By: BC Stormwater Management Utility Date Print: 6/20/13 File:C:/sethdata/projects/projectmaps/Myrtle Park Map1 2013-612

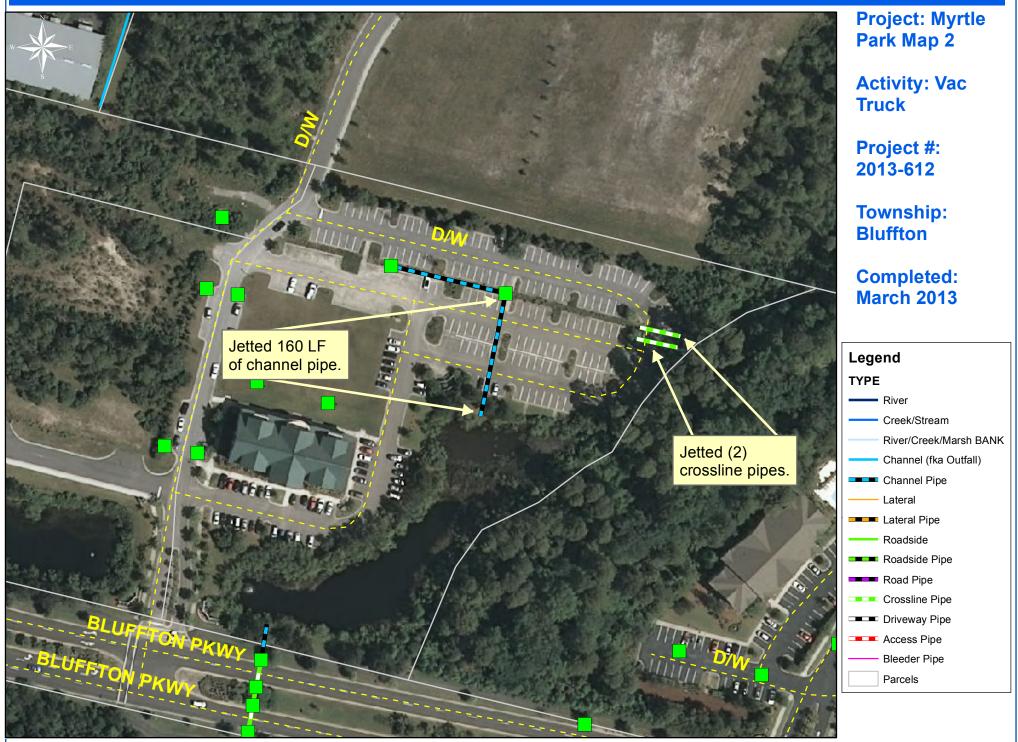

0 30 60 120 180 240 Feet

1 inch = 117 feet

Prepared By: BC Stormwater Management Utility Date Print: 6/24/13 File:C:/sethdata/projects/projectmaps/Vac/Myrtle Park Map2 2013-612
