



# Beaufort County Public Works Stormwater Infrastructure Project Summary

**Project Summary:** Bluffton Vacuum Truck - Sandy Pointe Drive, Skylark Drive, Benton Field Road and Devonwood Drive

**Activity:** Routine/Preventive Maintenance

**Narrative Description of Project:**

**Completion:** Oct-13

Project improved 16 L.F. of drainage system. Cleaned out (9) catch basins. Jetted (4) driveway pipes, (4) crossline pipes and 16 L.F. of channel pipe.

2014-310 / Bluffton Vacuum Truck	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	0.5	\$10.23	\$0.00	\$0.00	\$0.00	\$6.62	\$16.85
CBCO / Catch basin - clean out	18.0	\$389.29	\$206.68	\$142.50	\$0.00	\$148.23	\$886.70
CBIN / Catch basin - inspected	20.0	\$432.54	\$36.20	\$23.76	\$0.00	\$164.70	\$657.20
CLPJT / Crossline Pipe - Jetted	40.0	\$912.06	\$443.20	\$276.09	\$0.00	\$494.10	\$2,125.45
DPJT / Driveway Pipe - Jetted	10.0	\$239.76	\$110.80	\$40.58	\$0.00	\$164.70	\$555.84
ONJV / Onsite Job Visit	2.0	\$88.54	\$7.24	\$11.88	\$0.00	\$67.92	\$175.58
RB / Remove blockage from flowline	10.0	\$216.27	\$110.80	\$51.45	\$0.00	\$82.35	\$460.87
<b>2014-310 / Bluffton Vacuum Truck Sub Total</b>	<b>100.5</b>	<b>\$2,288.69</b>	<b>\$914.92</b>	<b>\$546.26</b>	<b>\$0.00</b>	<b>\$1,128.62</b>	<b>\$4,878.48</b>
<b>Grand Total</b>	<b>100.5</b>	<b>\$2,288.69</b>	<b>\$914.92</b>	<b>\$546.26</b>	<b>\$0.00</b>	<b>\$1,128.62</b>	<b>\$4,878.48</b>

Before



During



After



**Project:**  
Devonwood Drive  
and Benton  
Field Road

**Activity:** Vacuum  
Truck
















**Project #:**  
2014-310

**Township:**  
Bluffton

**Completed:**  
October 2013

**Legend**

**TYPE**

-  River
-  Creek/Stream
-  River/Creek/Marsh BANK
-  Channel (fka Outfall)
-  Channel Pipe
-  Lateral
-  Lateral Pipe
-  Roadside
-  Roadside Pipe
-  Road Pipe
-  Crossline Pipe
-  Driveway Pipe
-  Access Pipe
-  Bleeder Pipe
-  Catch Basin

Jetted (1) crossline  
pipe.

Jetted (1) crossline  
pipe and (2) driveway  
pipes.

Jetted (2)  
driveway pipes.



1 inch = 123 feet

Prepared By: BC Stormwater Management Utility

Date Print: 2/21/14

File: C:/sethdata/projects/projectmaps/Vac/Devonwood Dr 2014-310


**Project: Sandy Point Drive and Skylark Drive**

**Activity: Vacuum Truck**

**Project #: 2014-310**

**Township: Bluffton**

**Completed: October 2013**

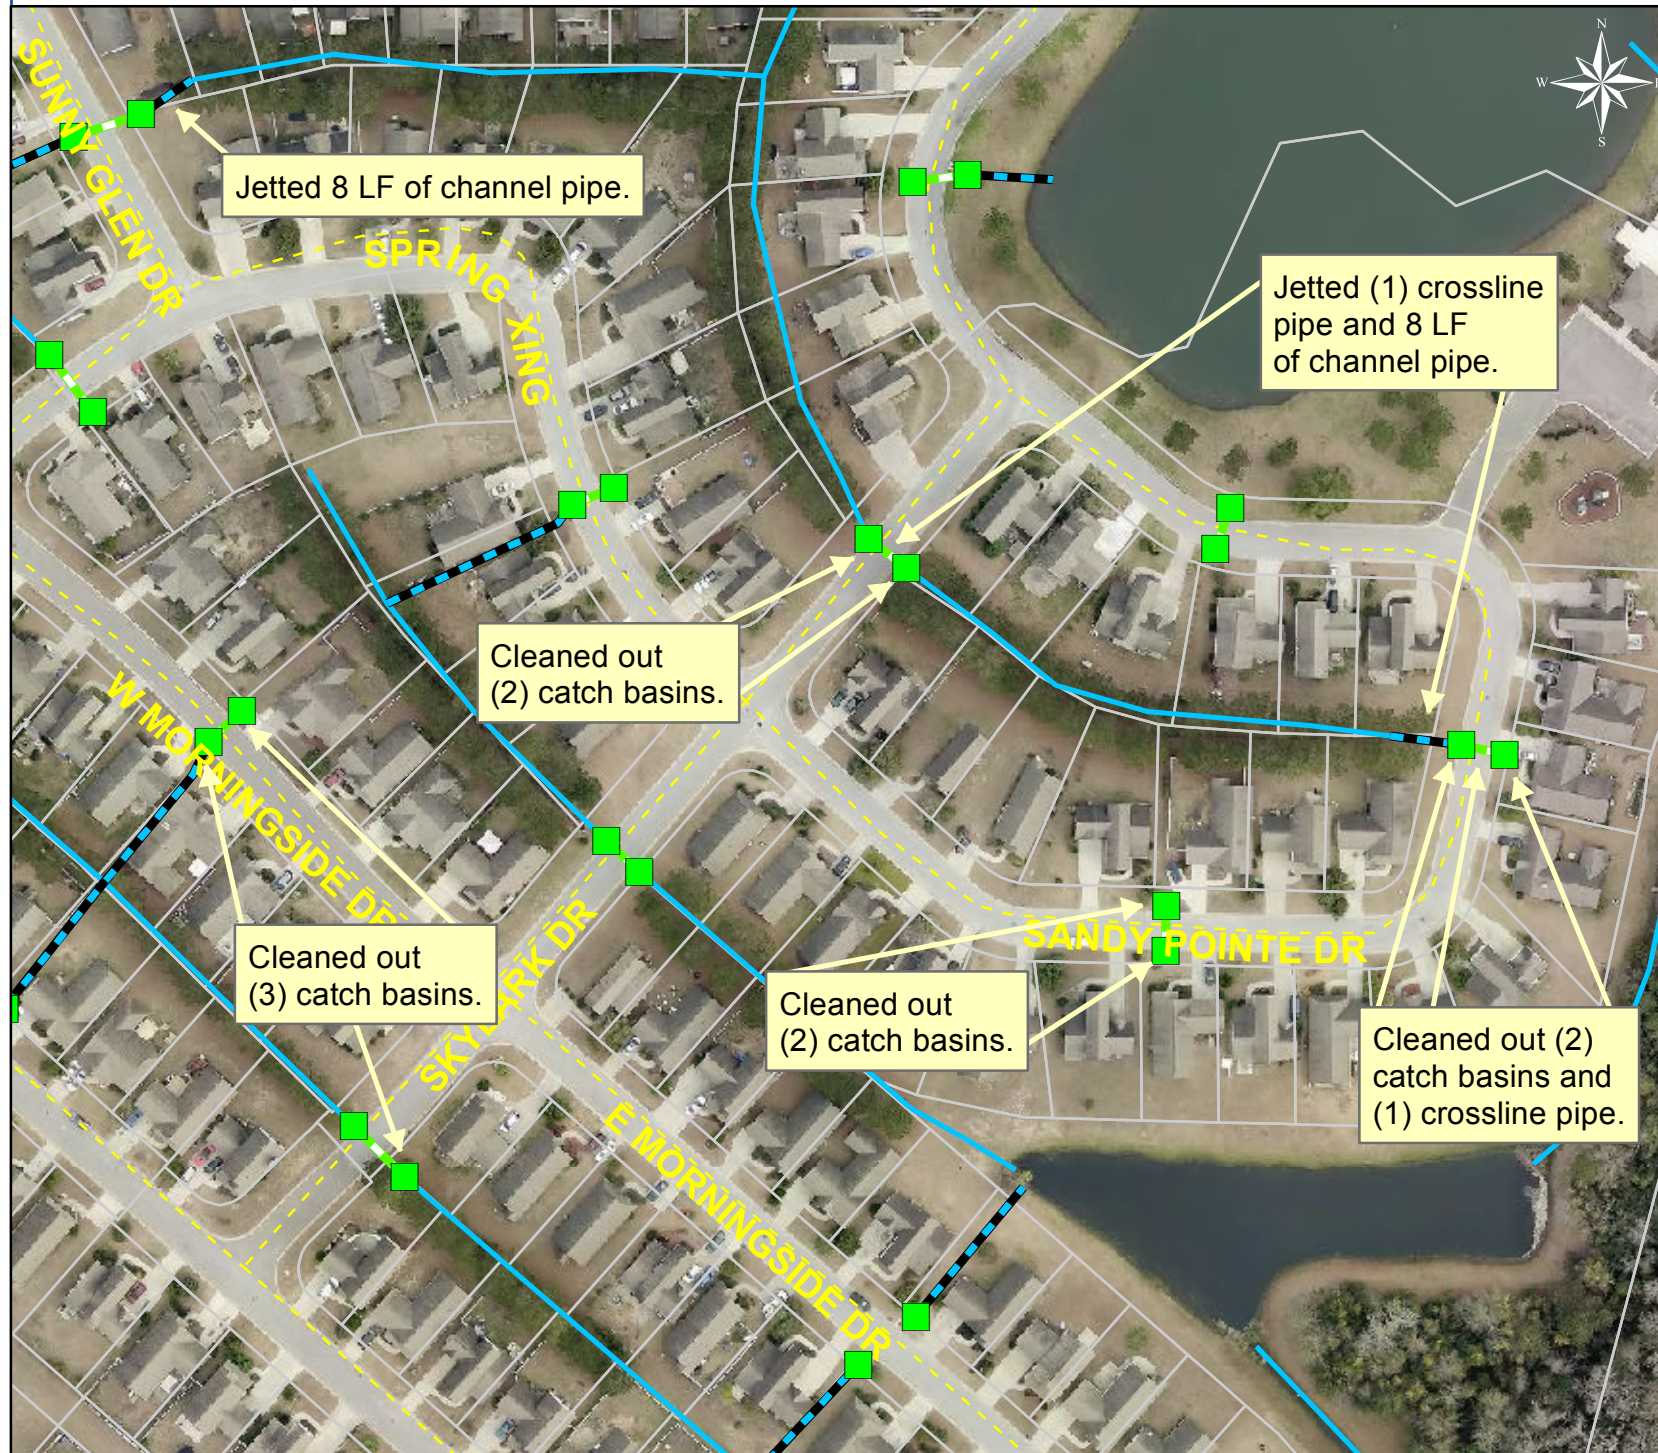

**Legend**

**TYPE**

- River
- Creek/Stream
- River/Creek/Marsh BANK
- Channel (fka Outfall)
- Channel Pipe
- Lateral
- Lateral Pipe
- Roadside
- Roadside Pipe
- Road Pipe
- Crossline Pipe
- Driveway Pipe
- Access Pipe
- Bleeder Pipe
- Catch Basin



1 inch = 125 feet

Prepared By: BC Stormwater Management Utility

Date Print: 2/27/14

File: C:\sethdata\projects\projectmaps\Vac/Skylark Dr 2014-310
