Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Bluffton Center Channel #1

Activity: Routine/Preventive Maintenance

Completion: Nov-14

Narrative Description of Project:

Project improved 968 L.F. of drainage system. Cleaned out 341 L.F. of channel and 360 L.F. of roadside ditch. Jetted 267 L.F. of channel pipe.


2015-550 / Bluffton Center Ch #1	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	0.5	\$10.23	\$0.00	\$0.00	\$0.00	\$6.62	\$16.85
DLO / Ditch Layout	30.0	\$648.90	\$36.20	\$19.53	\$0.00	\$429.30	\$1,133.93
HAUL / Hauling	31.5	\$681.35	\$337.05	\$171.00	\$0.00	\$454.23	\$1,643.63
ODCO / Channel - cleaned out	100.0	\$2,144.40	\$388.08	\$110.12	\$0.00	\$1,415.80	\$4,058.40
OFPJ / Channel Pipe - Jetted	16.0	\$369.59	\$531.84	\$129.08	\$0.00	\$250.56	\$1,281.06
ONJV / Onsite Job Visit	18.0	\$597.24	\$65.16	\$39.36	\$0.00	\$440.46	\$1,142.22
PI / Project Inspection	1.0	\$44.27	\$3.62	\$7.38	\$0.00	\$33.96	\$89.23
UB / Underbrush	28.0	\$597.45	\$25.34	\$10.58	\$0.00	\$393.12	\$1,026.49
UTLOC / Utility locates	0.5	\$10.23	\$0.00	\$0.00	\$0.00	\$6.62	\$16.85
2015-550 / Bluffton Center Ch #1 Sub Total	225.5	\$5,103.65	\$1,387.29	\$487.04	\$0.00	\$3,430.66	\$10,408.64
Grand Total	225.5	\$5,103.65	\$1,387.29	\$487.04	\$0.00	\$3,430.66	\$10,408.64

Before





After

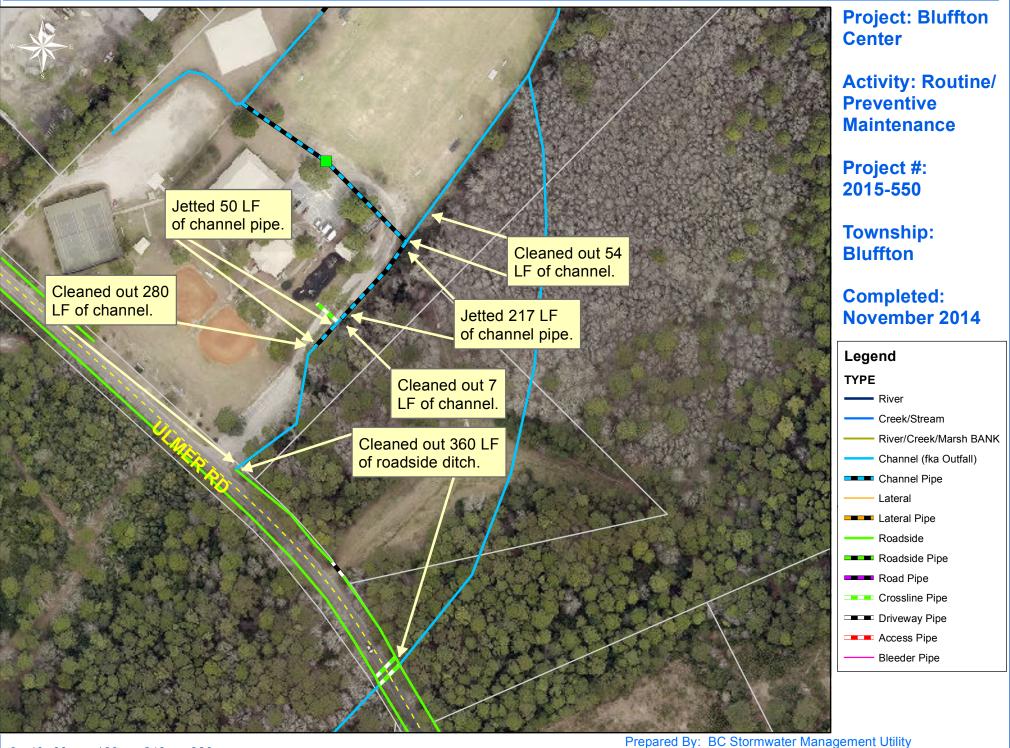

0 40 80 160 240 320 Feet

1 inch = 163 feet

Prepared By: BC Stormwater Management Utility Date Print: 1/23/15 File:C:/sethdata/projects/projectmaps/Bluffton Center 2015-550
