



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Carolina Estates- Charleston Drive and Colleton Drive

Activity: Routine/Preventive Maintenance

Duration: 02/15/18-03/01/18

Narrative Description of Project:

Project improved 2,915 L.F. of drainage system. Cleaned out 2,915 L.F. of roadside ditch. Jetted (2) crossline pipes and (31) driveway pipes. Hydroseeded for erosion control.

2018-574 / Carolina Estates	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
DPJT / Driveway Pipe - Jetted	41.5	\$923.41	\$177.94	\$123.49	\$0.00	\$594.05	\$1,818.89
HAUL / Hauling	58.5	\$1,291.20	\$532.23	\$167.17	\$0.00	\$61.78	\$2,052.38
HYDR / Hydroseeding	12.0	\$243.12	\$51.72	\$812.97	\$0.00	\$101.76	\$1,209.57
RSDCL / Roadside Ditch - Cleanout	177.0	\$3,590.14	\$824.02	\$192.96	\$0.00	\$1,797.48	\$6,404.60
2018-574 / Carolina Estates Sub Total	290.5	\$6,080.55	\$1,585.91	\$1,296.59	\$0.00	\$2,555.07	\$11,518.12
Grand Total	290.5	\$6,080.55	\$1,585.91	\$1,296.59	\$0.00	\$2,555.07	\$11,518.12

Before




During



After



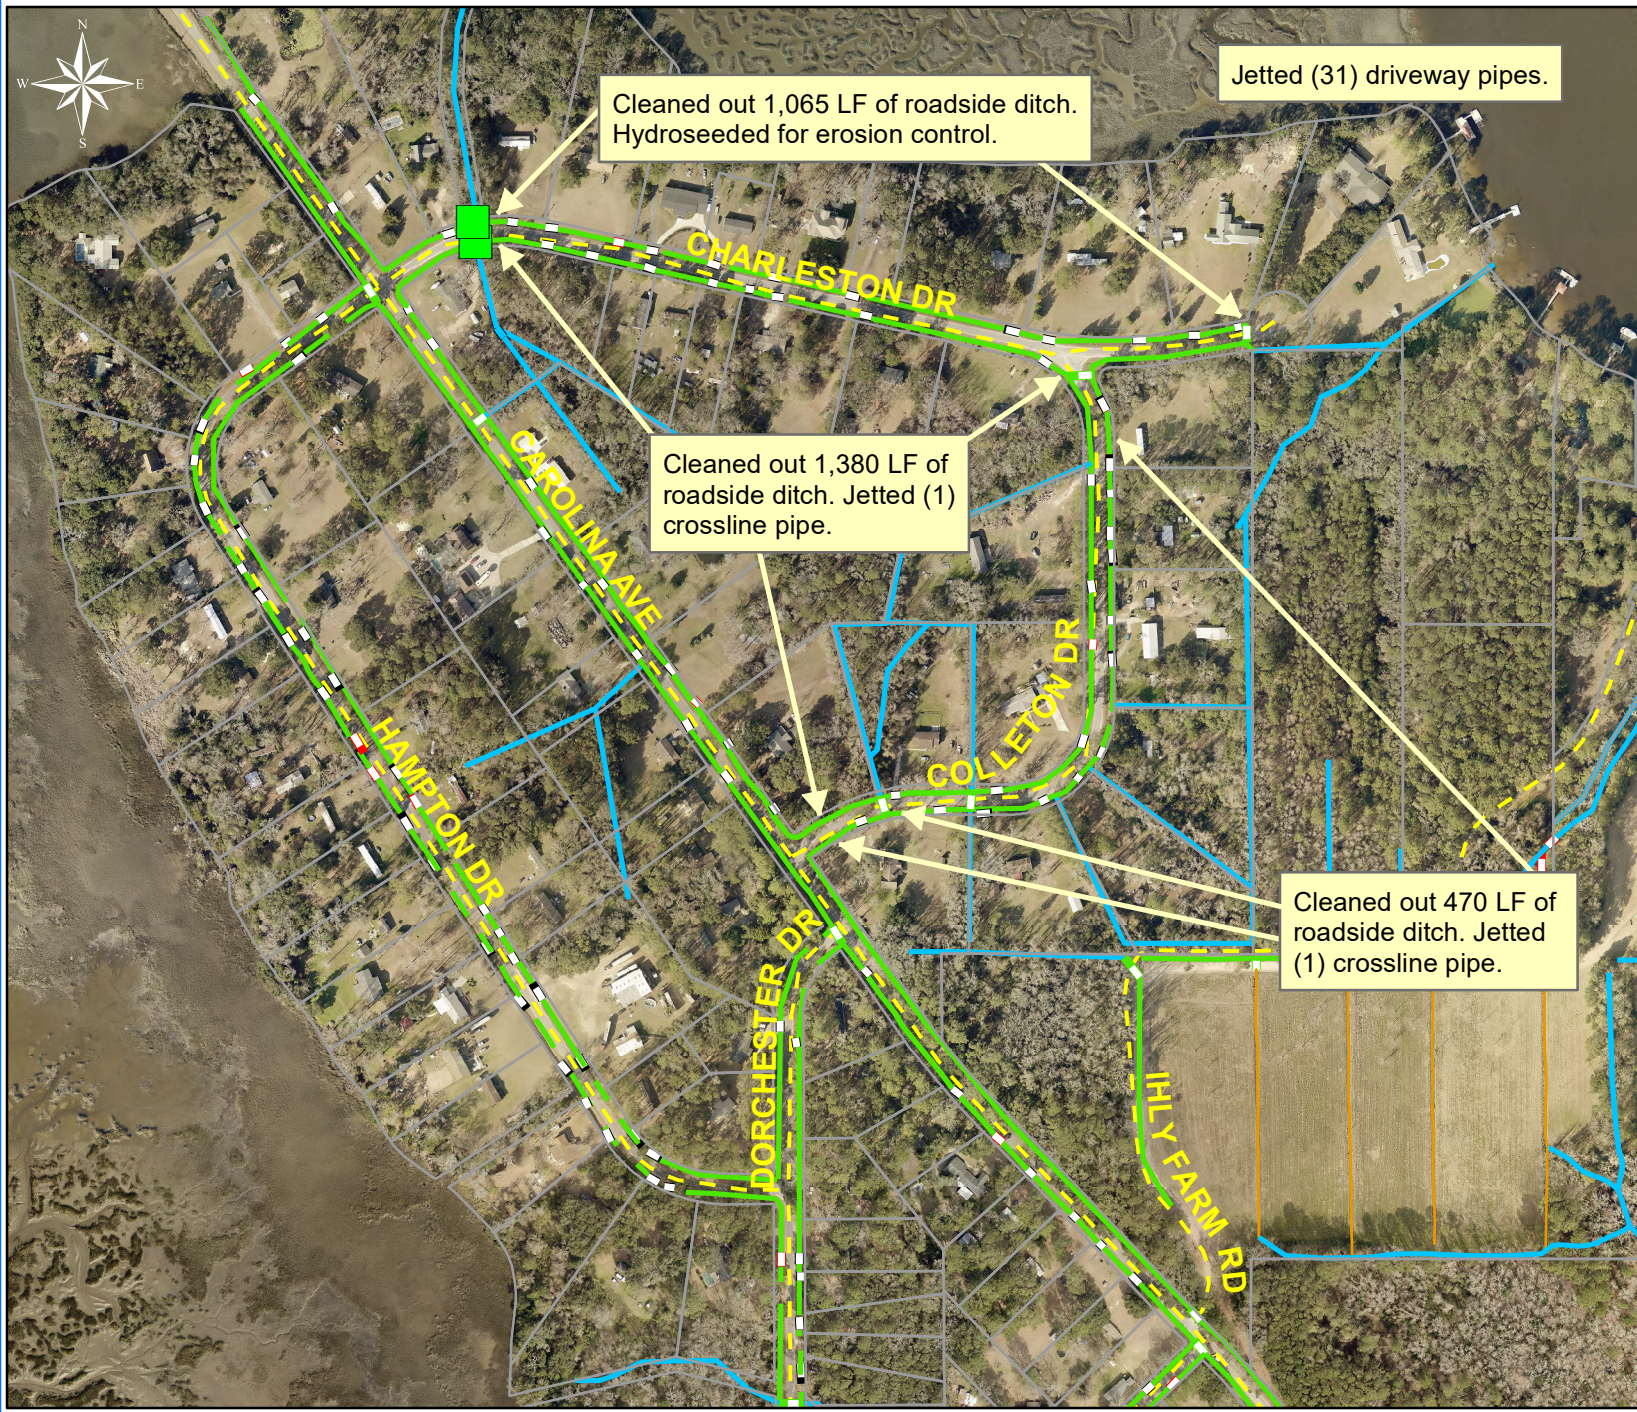

Project: Carolina Estates - Charleston Drive and Colleton Drive

Activity: Routine/ Preventive Maintenance

Project #: 2018-574

Township/SW Dist: Port Royal Island/6

Completed: March 2018

Legend	
Drainage Type	
	Access Pipe
	Bleeder Pipe
	Channel Pipe
	Channel
	Stream
	Crossline Pipe
	Driveway Pipe
	Lateral
	Lateral Pipe
	River
	Road Pipe
	Roadside
	Roadside Pipe



1 inch = 420 feet

Prepared By: BC Stormwater Management Utility
 Date Print: 02/07/19
 File: C:\project summaries map\Carolina Estates_2018-574
