

Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: Sandhill Estates Subdivision Shannon Lane, Craig Lane, Sandhill Drive, Tammy Lane

Narrative Description of Project:

Project improved 7,205 L.F. of drainage system. Removed debris from roads. Cleaned out 7,109 L.F. of roadside ditch. Jetted (3) crossline pipes, (60) driveway pipes and 96 L.F. of roadside pipe.

2018-560 / Sandhill Estates	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
CLPJT / Crossline Pipe - Jetted	20.0	\$445.60	\$86.80	\$94.26	\$0.00	\$286.80	\$913.46
DPJT / Driveway Pipe - Jetted	37.0	\$836.46	\$182.28	\$121.88	\$0.00	\$541.23	\$1,681.85
HAUL / Hauling	130.0	\$2,739.50	\$1,224.60	\$425.07	\$0.00	\$216.30	\$4,605.47
RMTR / Remove trees-roads	20.0	\$403.20	\$110.56	\$16.66	\$0.00	\$188.25	\$718.67
RMTRD / Remove trees - Ditch	15.0	\$303.90	\$18.00	\$2.03	\$0.00	\$127.20	\$451.13
RSDCL / Roadside Ditch - Cleanout	285.0	\$5,762.10	\$1,703.61	\$420.22	\$0.00	\$3,139.20	\$11,025.13
UTLOC / Utility locates	1.5	\$37.05	\$0.00	\$0.00	\$0.00	\$19.85	\$56.90
2018-560 / Sandhill Estates Sub Total	510.0	\$10,560.50	\$3,325.85	\$1,080.12	\$0.00	\$4,518.82	\$19,485.29
Grand Total	510.0	\$10,560.50	\$3,325.85	\$1,080.12	\$0.00	\$4,518.82	\$19,485.29

Before






During

After

Activity: Routine/Preventive Maintenance

Duration: 12/19/17-02/15/18



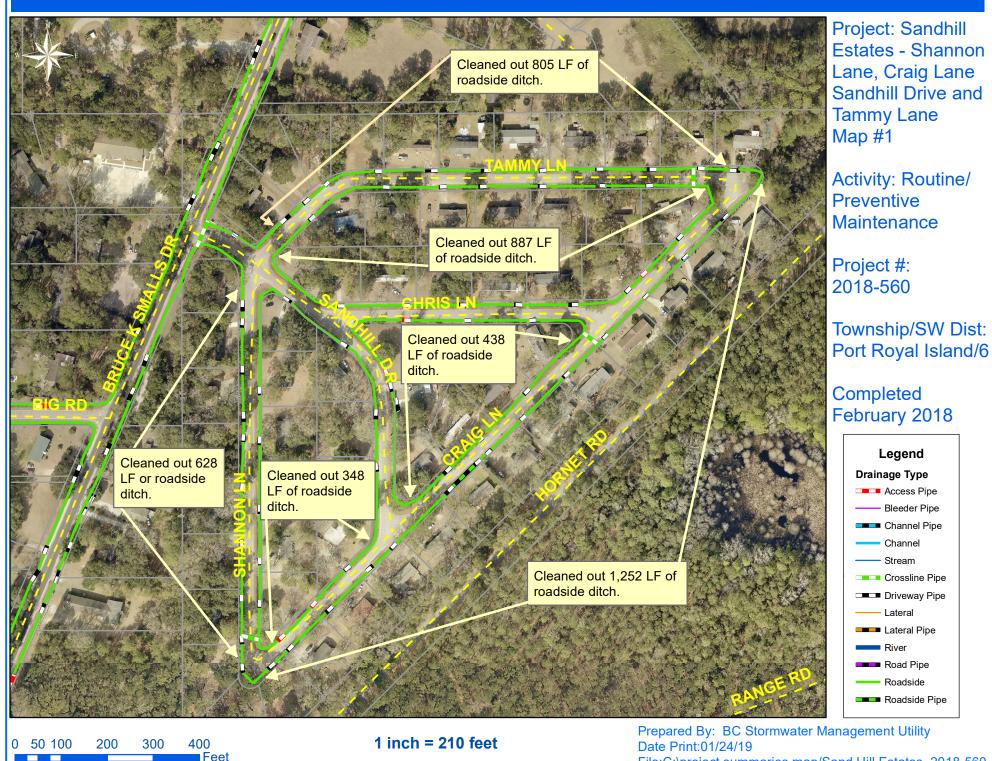

File:C:\project summaries map/Sand Hill Estates 2018-560



File:C:\project summaries map/Sand Hill Estates Map#2_2018-560

