



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Parrot Creek Drive

Activity: Drainage Improvement

Duration: 12/04/18-12/5/18

Narrative Description of Project:

Project improved 48 L.F. of drainage system. Installed 48 L.F. of roadside pipe and rip rap for erosion control.

2018-587A / Parrot Creek	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	1.0	\$21.79	\$0.00	\$0.00	\$0.00	\$0.00	\$21.79
HAUL / Hauling	23.0	\$531.65	\$325.68	\$118.18	\$0.00	\$348.06	\$1,323.57
RRI / Rip Rap - Installed	40.0	\$1,134.00	\$38.40	\$31.38	\$0.00	\$410.90	\$1,614.68
RSPI / Roadside Pipe - Installed	40.0	\$1,134.00	\$173.48	\$1,505.92	\$0.00	\$410.90	\$3,224.30
2018-587A / Parrot Creek Sub Total	104.0	\$2,821.44	\$537.56	\$1,655.48	\$0.00	\$1,169.86	\$6,184.34
Grand Total	104.0	\$2,821.44	\$537.56	\$1,655.48	\$0.00	\$1,169.86	\$6,184.34

(No Pictures Available)


Project: Parrot Creek Drive

Activity: Drainage Improvement

Project #: 2018-587A

Township/SW Dist: Bluffton/4

Completed: December 2018

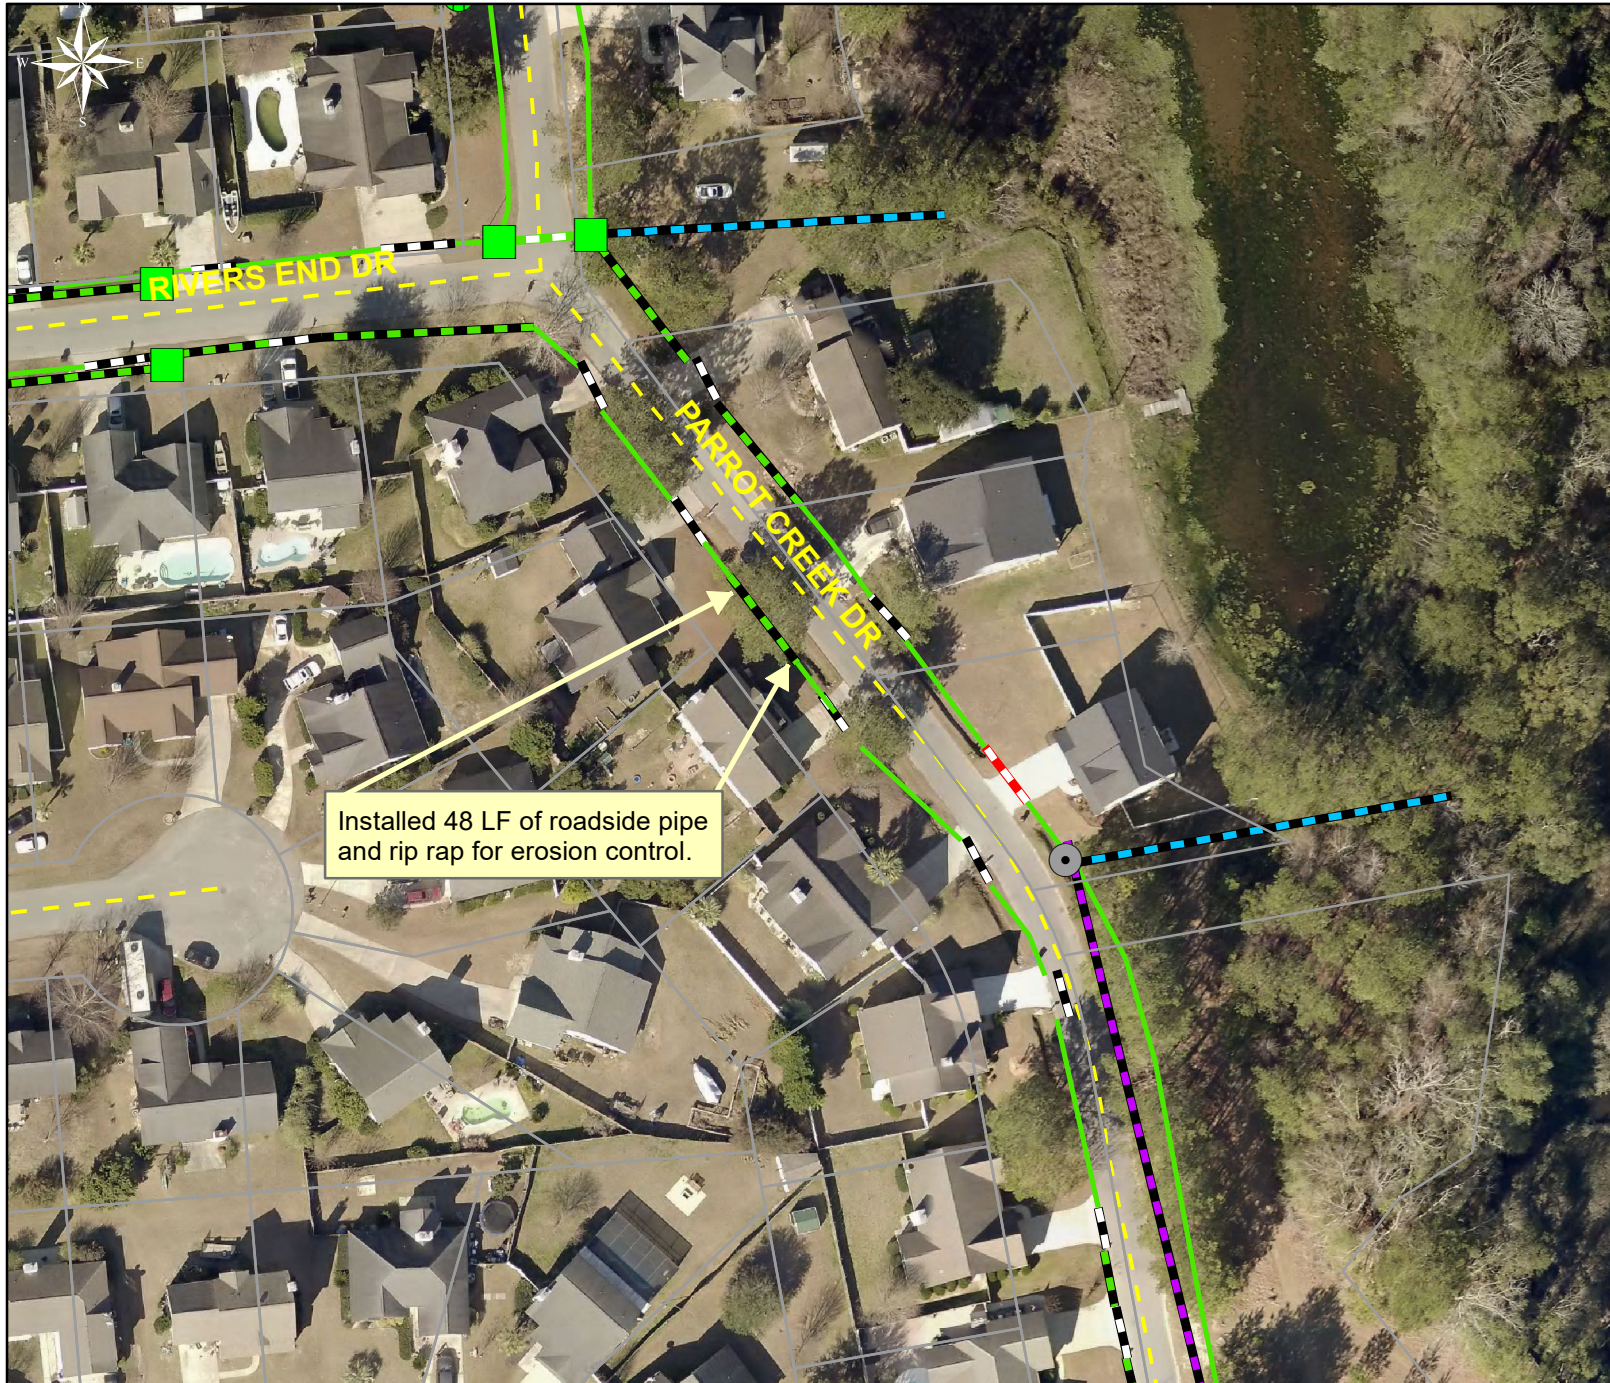

Installed 48 LF of roadside pipe and rip rap for erosion control.

Legend

Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 20 40 80 120 160 Feet

1 inch = 83 feet

Prepared By: BC Stormwater Management Utility
Date Print: 02/20/19
File: C:\project summaries map\Parrot Creek_2018-587A
