

Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Broad River Drive

Activity: Routine/Preventive Maintenance

Duration: 10/21/19-11/25/19

Narrative Description of Project:

Project improved 700 L.F. of drainage system. Cleaned out 313 L.F. of roadside ditch and 95 L.F. of channel. Jetted 292 L.F. of roadside pipe and (2) crossline pipes. Replaced (1) and repaired (1) catch basin lid. Hyrdoseeded for erosion control.

2020-020 / Broad River Drive	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
CBLR / Catch Basin Lid - Replaced	28.0	\$617.75	\$109.29	\$579.95	\$0.00	\$207.90	\$1,514.89
CBLREP / Catch Basin Lid - Repaired	12.0	\$261.04	\$28.80	\$31.97	\$0.00	\$118.80	\$440.61
HAUL / Hauling	20.0	\$445.40	\$283.20	\$294.46	\$0.00	\$288.40	\$1,311.46
HYDR / Hydroseeding	10.0	\$202.75	\$55.32	\$869.73	\$0.00	\$66.15	\$1,193.95
RSDCL / Roadside Ditch - Cleanout	100.0	\$2,096.00	\$370.30	\$108.40	\$0.00	\$396.90	\$2,971.60
RSPJ / Roadside Pipe - Jetted	10.0	\$222.80	\$191.60	\$44.90	\$0.00	\$143.40	\$602.70
UTLOC / Utility locates	1.0	\$21.79	\$0.00	\$0.00	\$0.00	\$0.00	\$21.79
2020-020 / Broad River Drive Sub Total	182.5	\$3,900.22	\$1,038.51	\$1,929.41	\$0.00	\$1,221.55	\$8,089.69
Grand Total	182.5	\$3,900.22	\$1,038.51	\$1,929.41	\$0.00	\$1,221.55	\$8,089.69

Before





During



After



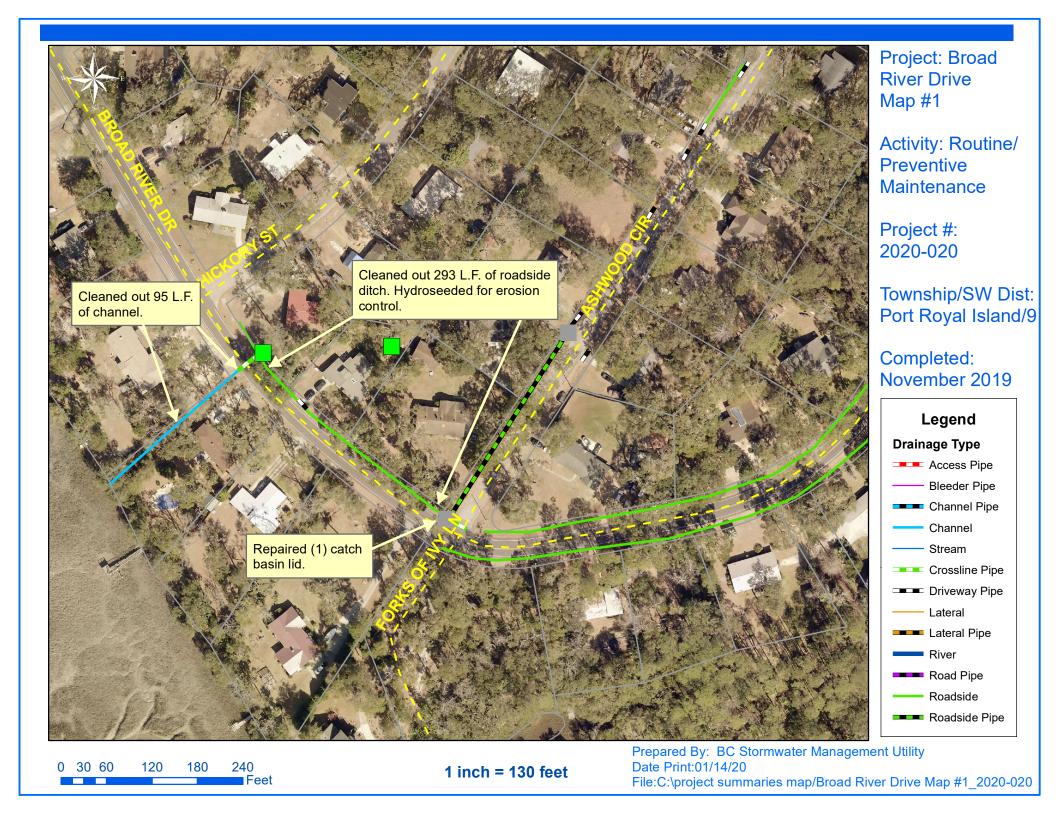

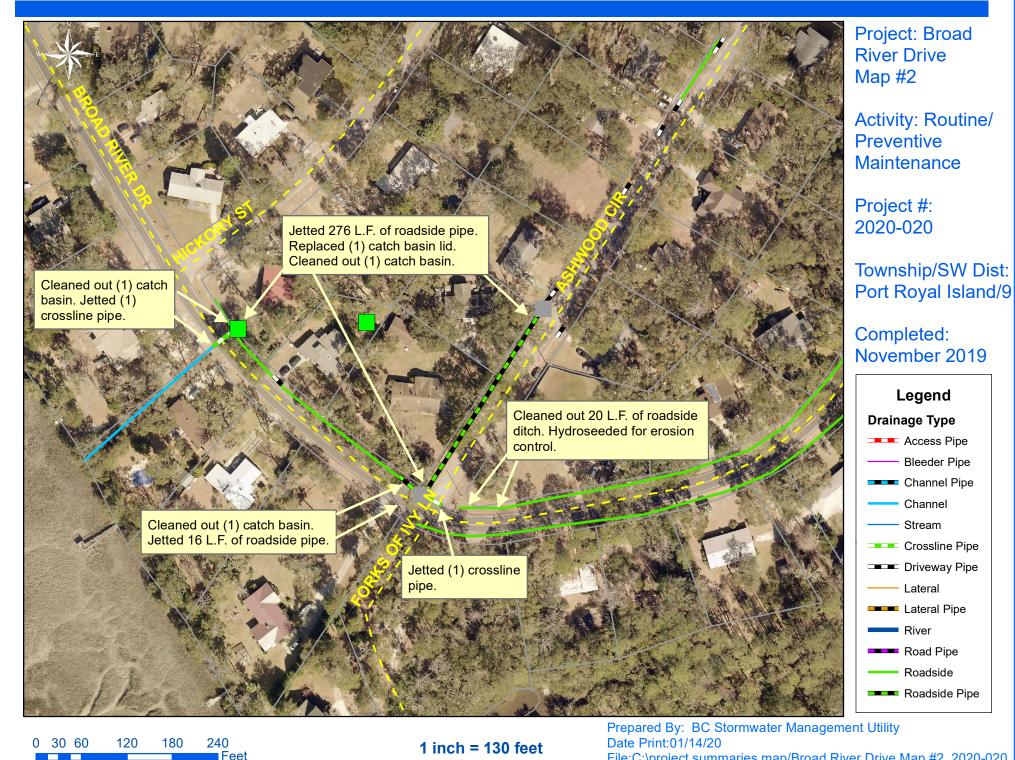

File:C:\project summaries map/Broad River Drive Map #2 2020-020
