



**Beaufort County Public Works**  
**Stormwater Infrastructure**  
*Project Summary*

**Project Summary:** Chisholm Road

**Activity:** Routine/Preventive Maintenance


Duration: 11/16/2020-11/24/2020

**Narrative Description of Project:**

Project improved 498 L.F. of drainage system. Cleaned out (7) catch basins and 356 L.F. of roadside ditch. Jetted (4) crossline pipes, (3) driveway pipes and 142 L.F. of roadside pipe.

<b>2021-513 / Chisholm Road</b>	<b>Labor Hours</b>	<b>Labor Cost</b>	<b>Equipment Cost</b>	<b>Material Cost</b>	<b>Contractor Cost</b>	<b>Indirect Labor</b>	<b>Total Cost</b>
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
CBCO / Catch basin - clean out	32.0	\$707.04	\$613.12	\$115.90	\$0.00	\$263.52	\$1,699.58
CLPJT / Crossline Pipe - Jetted	16.0	\$366.00	\$306.56	\$70.20	\$0.00	\$0.00	\$742.76
DPJT / Driveway Pipe - Jetted	8.0	\$176.76	\$153.28	\$22.60	\$0.00	\$65.88	\$418.52
HAUL / Hauling	8.0	\$178.16	\$152.48	\$25.60	\$0.00	\$115.36	\$471.60
RSDCL / Roadside Ditch - Cleanout	32.0	\$657.60	\$99.21	\$18.72	\$0.00	\$203.52	\$979.05
UTLOC / Utility locates	0.5	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
2021-513 / Chisholm Road Project Sub Total	98.0	\$2,130.60	\$1,324.65	\$253.02	\$0.00	\$654.90	\$4,363.16
<b>Grand Total</b>	<b>98.0</b>	<b>\$2,130.60</b>	<b>\$1,324.65</b>	<b>\$253.02</b>	<b>\$0.00</b>	<b>\$654.90</b>	<b>\$4,363.16</b>

(No Picture Available)

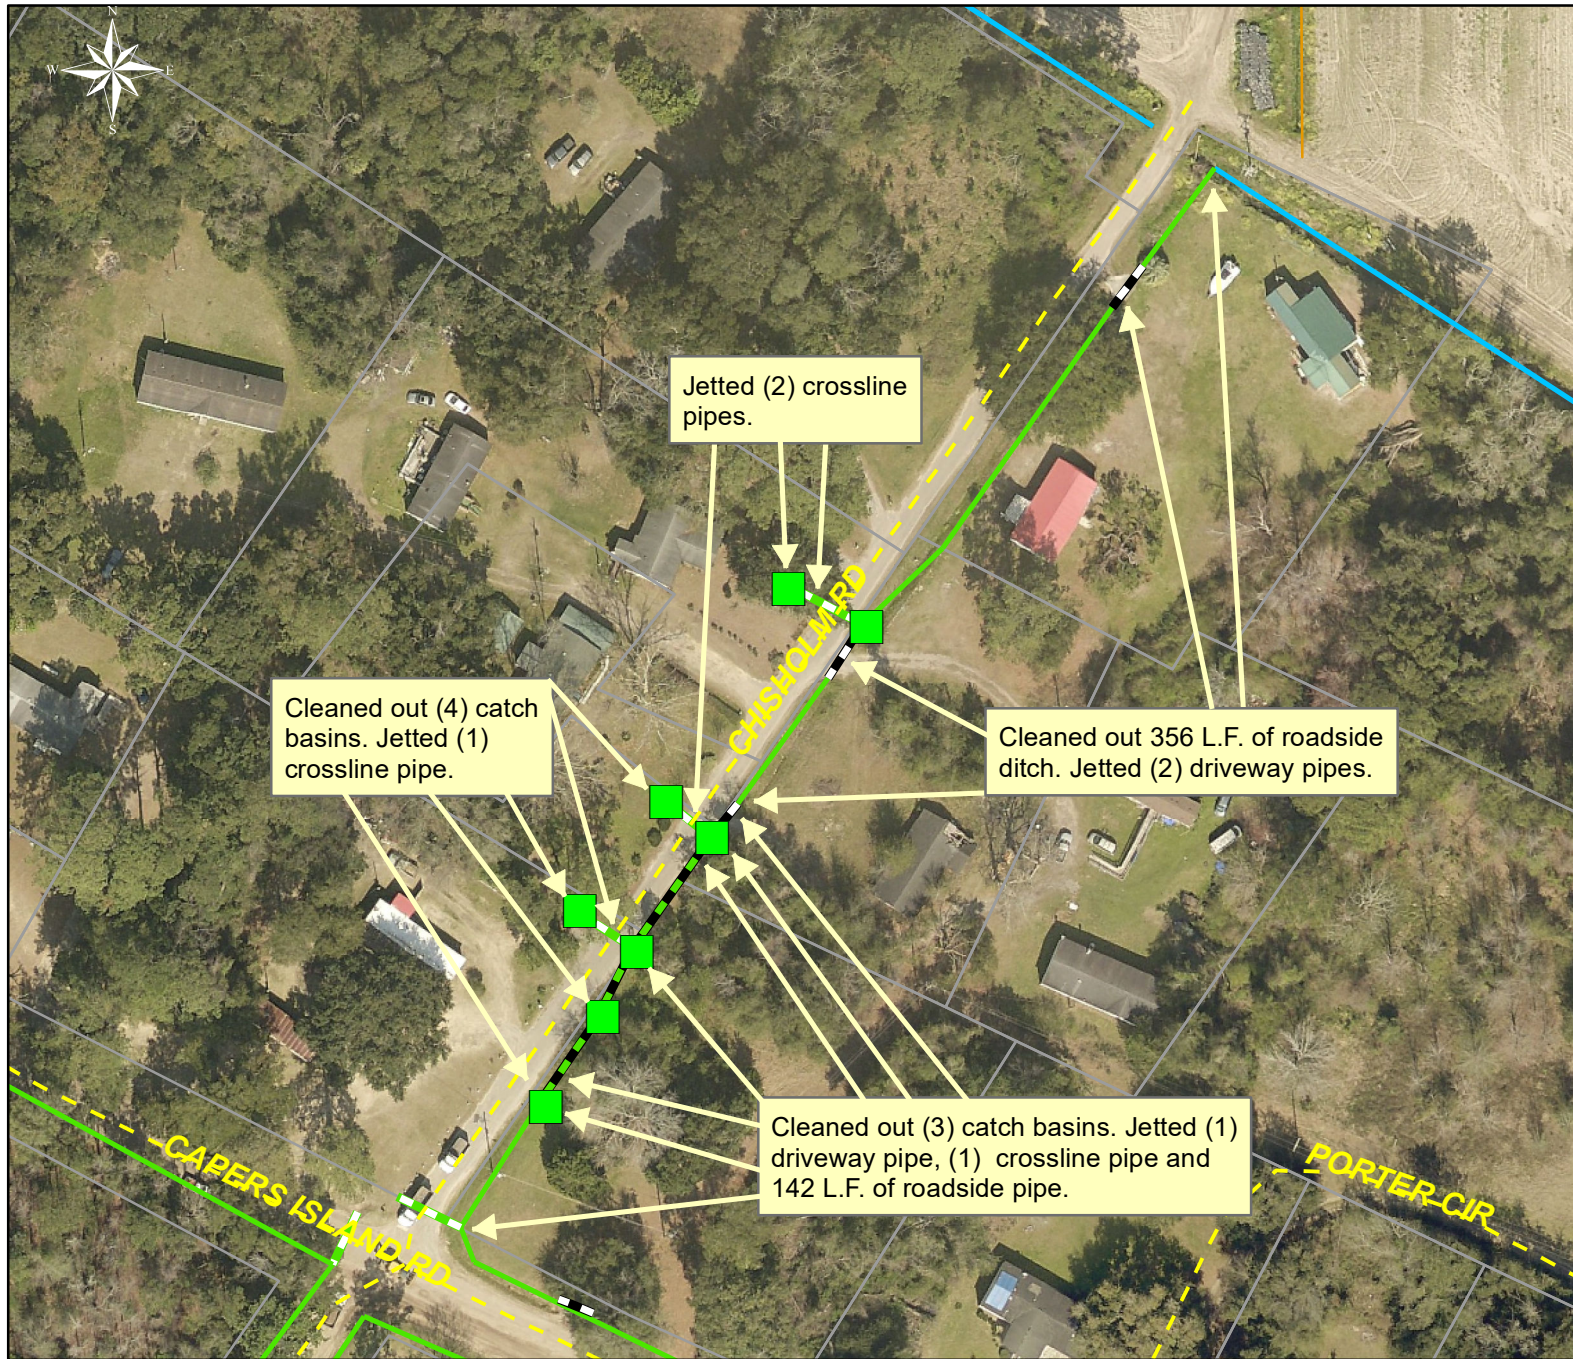

Project: Chisholm Road

Activity: Routine/  
Preventive  
Maintenance

Project #:  
2021-513

Township/SW Dist:  
St. Helena Island/8

Completed:  
November 2020

### Legend

#### Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 25 50 100 150 200  
Feet

1 inch = 100 feet

Prepared By: BC Stormwater Management Utility  
Date Print: 11/25/20  
File: C:\project summaries map\Chisholm Road\_2021-513
