



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: View Point Circle

Activity: Routine/Preventive Maintenance

Duration: 10/08/2020-11/20/2020

Narrative Description of Project:

Project improved 574 L.F. of drainage system. Cleaned out 550 L.F. of roadside ditch. Jetted (13) driveway pipes, (2) crossline pipes, and 24 L.F. of channel pipe. Replaced (2) driveway pipes. Installed (1) driveway pipe and rip rap for erosion control.

2021-509 / View Point Circle	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
ASI / Asphalt Installation	20.0	\$418.85	\$135.88	\$56.39	\$0.00	\$193.35	\$804.47
AUDIT / Audit Project	1.5	\$32.69	\$0.00	\$0.00	\$0.00	\$0.00	\$32.69
CLPJT / Crossline Pipe - Jetted	16.0	\$368.97	\$306.56	\$56.60	\$0.00	\$97.68	\$829.81
DPINS / Driveway Pipe - Installed	92.0	\$1904.52	\$302.82	\$2331.01	\$0.00	\$614.64	\$5,152.99
DPJT / Driveway Pipe - Jetted	14.0	\$309.33	\$268.24	\$62.20	\$0.00	\$115.29	\$755.06
HAUL / Hauling	56.0	\$1,244.64	\$1,008.56	\$5,328.49	\$0.00	\$259.56	\$7,841.25
PP / Project Preparation	76.0	\$1,568.00	\$254.82	\$118.96	\$0.00	\$565.80	\$2,507.58
RRI / Rip Rap - Installed	16.0	\$328.20	\$77.74	\$103.60	\$0.00	\$154.68	\$664.22
RSDCL / Roadside Ditch - Cleanout	96.0	\$1,956.20	\$284.94	\$214.00	\$0.00	\$663.48	\$3,118.62
UTLOC / Utility locates	2.0	\$49.40	\$0.00	\$0.00	\$0.00	\$26.46	\$75.86
2021-509 / View Point Circle Project Sub Total	389.5	\$8,180.79	\$2,639.56	\$8,271.26	\$0.00	\$2,690.94	\$21,782.55
Grand Total	389.5	\$8,180.79	\$2,639.56	\$8,271.26	\$0.00	\$2,690.94	\$21,782.55

(Before)


(During)

(Ending)

(No Picture Available)



(No Picture Available)

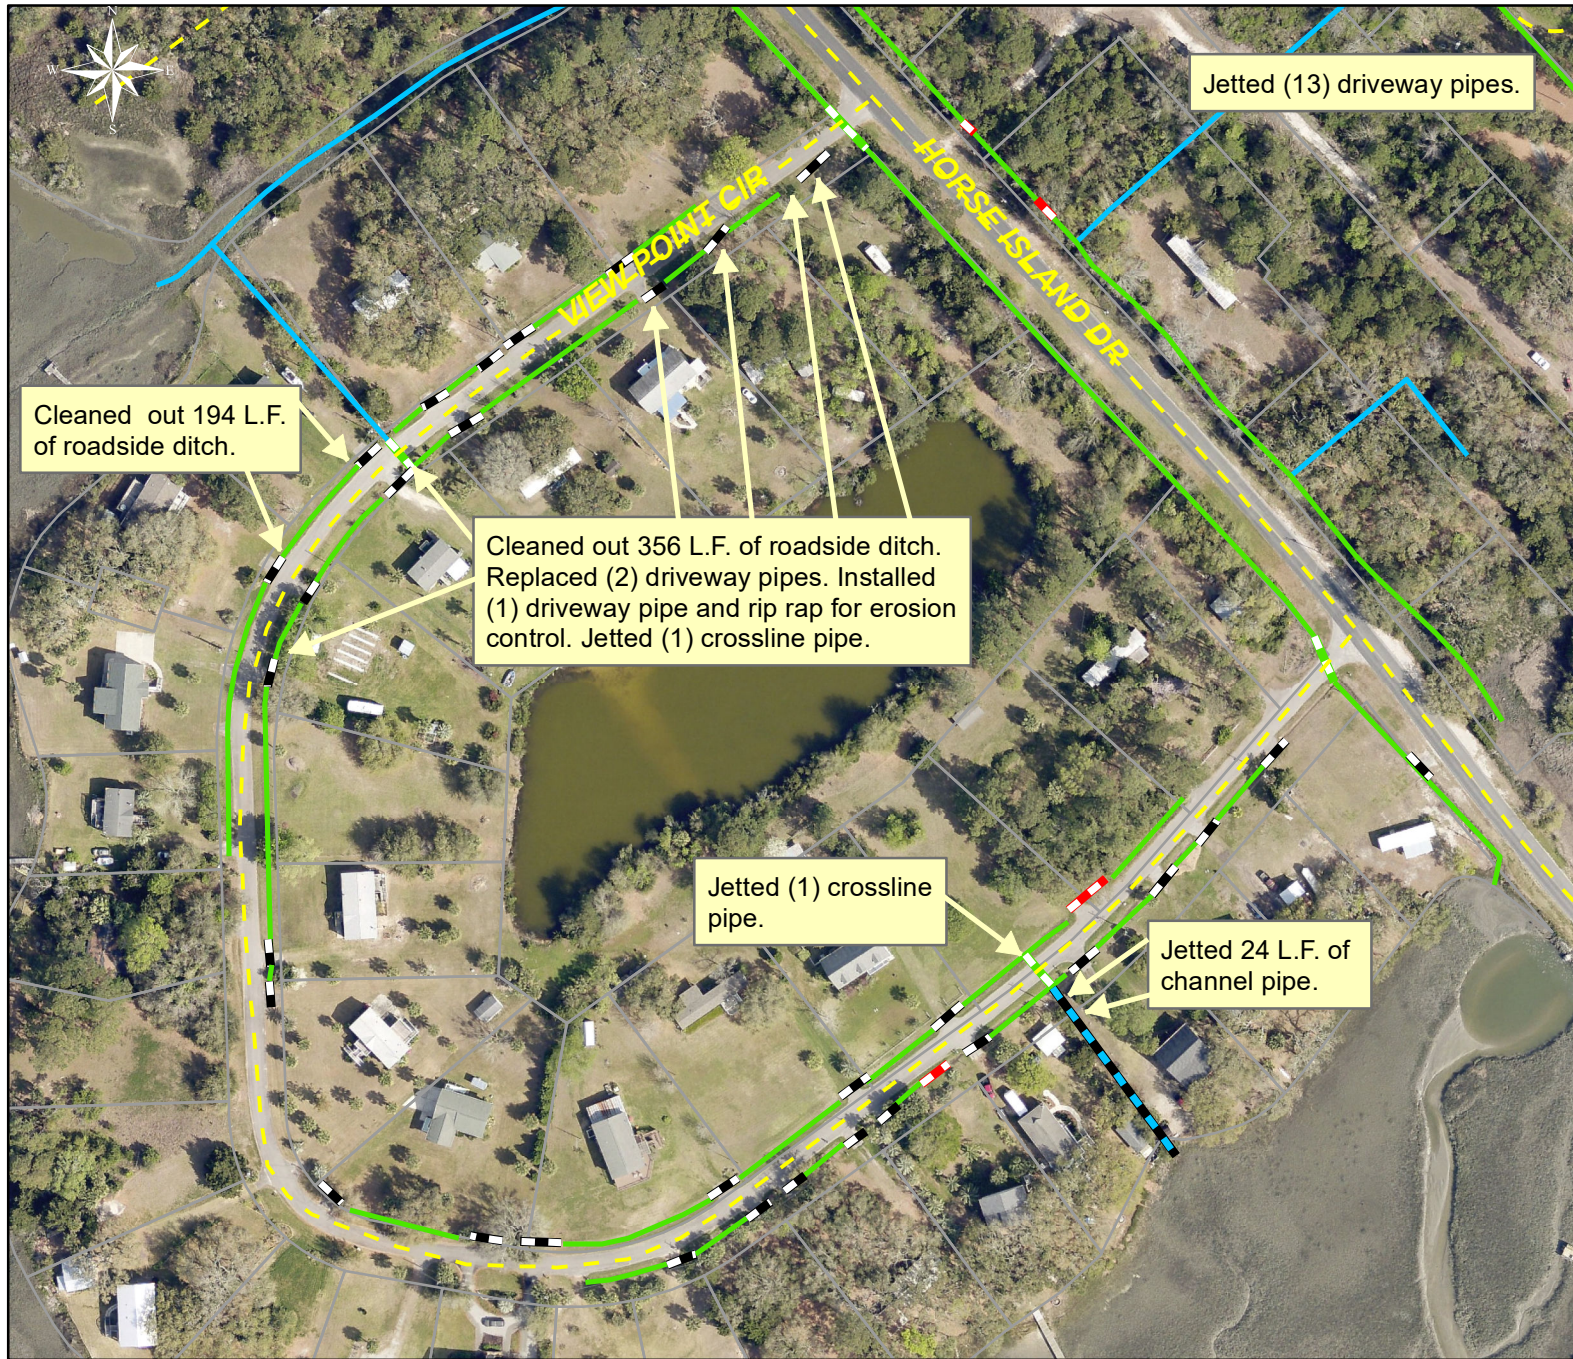

Project: View Point Circle

Activity: Routine/
Preventive
Maintenance

Project #:
2021-509

Township/SW Dist:
St. Helena Island/8

Completed:
November 2020

Legend

Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- - - Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 40 80 160 240 320
Feet

1 inch = 170 feet

Prepared By: BC Stormwater Management Utility
Date Print: 12/18/20
File: C:\project summaries map\View Point Circle_2021-509
