



Beaufort County
Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Oakmont Subdivision

Activity: Routine/Preventive Maintenance

Narrative Description of Project:

Project improved 2,182 L.F. of drainage system. Cleaned out 1,781 L.F. of roadside ditch and 175 L.F. of channel. Installed (1) access pipe. Replaced (1) crossline pipe. Handseeded and hydroseeded for erosion control. Jetted (4) crossline pipes, (16) driveway pipes and 226 L.F. channel pipe.

Duration: 7/27/17 - 8/21/17

2018-511 / Oakmont Subdivision	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
APINS / Access pipe - installed	60.0	\$1,251.00	\$72.00	\$508.18	\$0.00	\$521.10	\$2,352.28
APJT / Access pipe - jetted	14.0	\$311.92	\$60.76	\$60.20	\$0.00	\$200.76	\$633.64
AUDIT / Audit Project	1.5	\$35.24	\$0.00	\$0.00	\$0.00	\$19.85	\$55.08
CCO / Channel - cleaned out	62.0	\$1,291.72	\$351.27	\$50.04	\$0.00	\$663.54	\$2,356.57
CPJ / Channel Pipe - Jetted	10.0	\$222.80	\$43.40	\$42.30	\$0.00	\$143.40	\$451.90
ERCON / Erosion control	15.0	\$342.20	\$37.63	\$50.40	\$0.00	\$132.30	\$562.53
HAUL / Hauling	115.0	\$2,516.10	\$908.36	\$1,076.36	\$0.00	\$676.14	\$5,176.96
HYDR / Hydroseeding	40.0	\$895.00	\$63.60	\$122.47	\$0.00	\$396.90	\$1,477.97
PP / Project Preparation	38.1	\$866.05	\$72.00	\$40.26	\$0.00	\$398.43	\$1,376.74
RSDCL / Roadside Ditch - Cleanout	198.0	\$4,453.52	\$932.26	\$145.19	\$0.00	\$2,167.92	\$7,698.89
UTLOC / Utility locates	2.0	\$49.40	\$4.02	\$3.66	\$0.00	\$26.46	\$83.54
2018-511 / Oakmont Subdivision Sub Total	555.6	\$12,234.95	\$2,545.30	\$2,099.04	\$0.00	\$5,346.79	\$22,226.08
Grand Total	555.6	\$12,234.95	\$2,545.30	\$2,099.04	\$0.00	\$5,346.79	\$22,226.08

Before




During



After



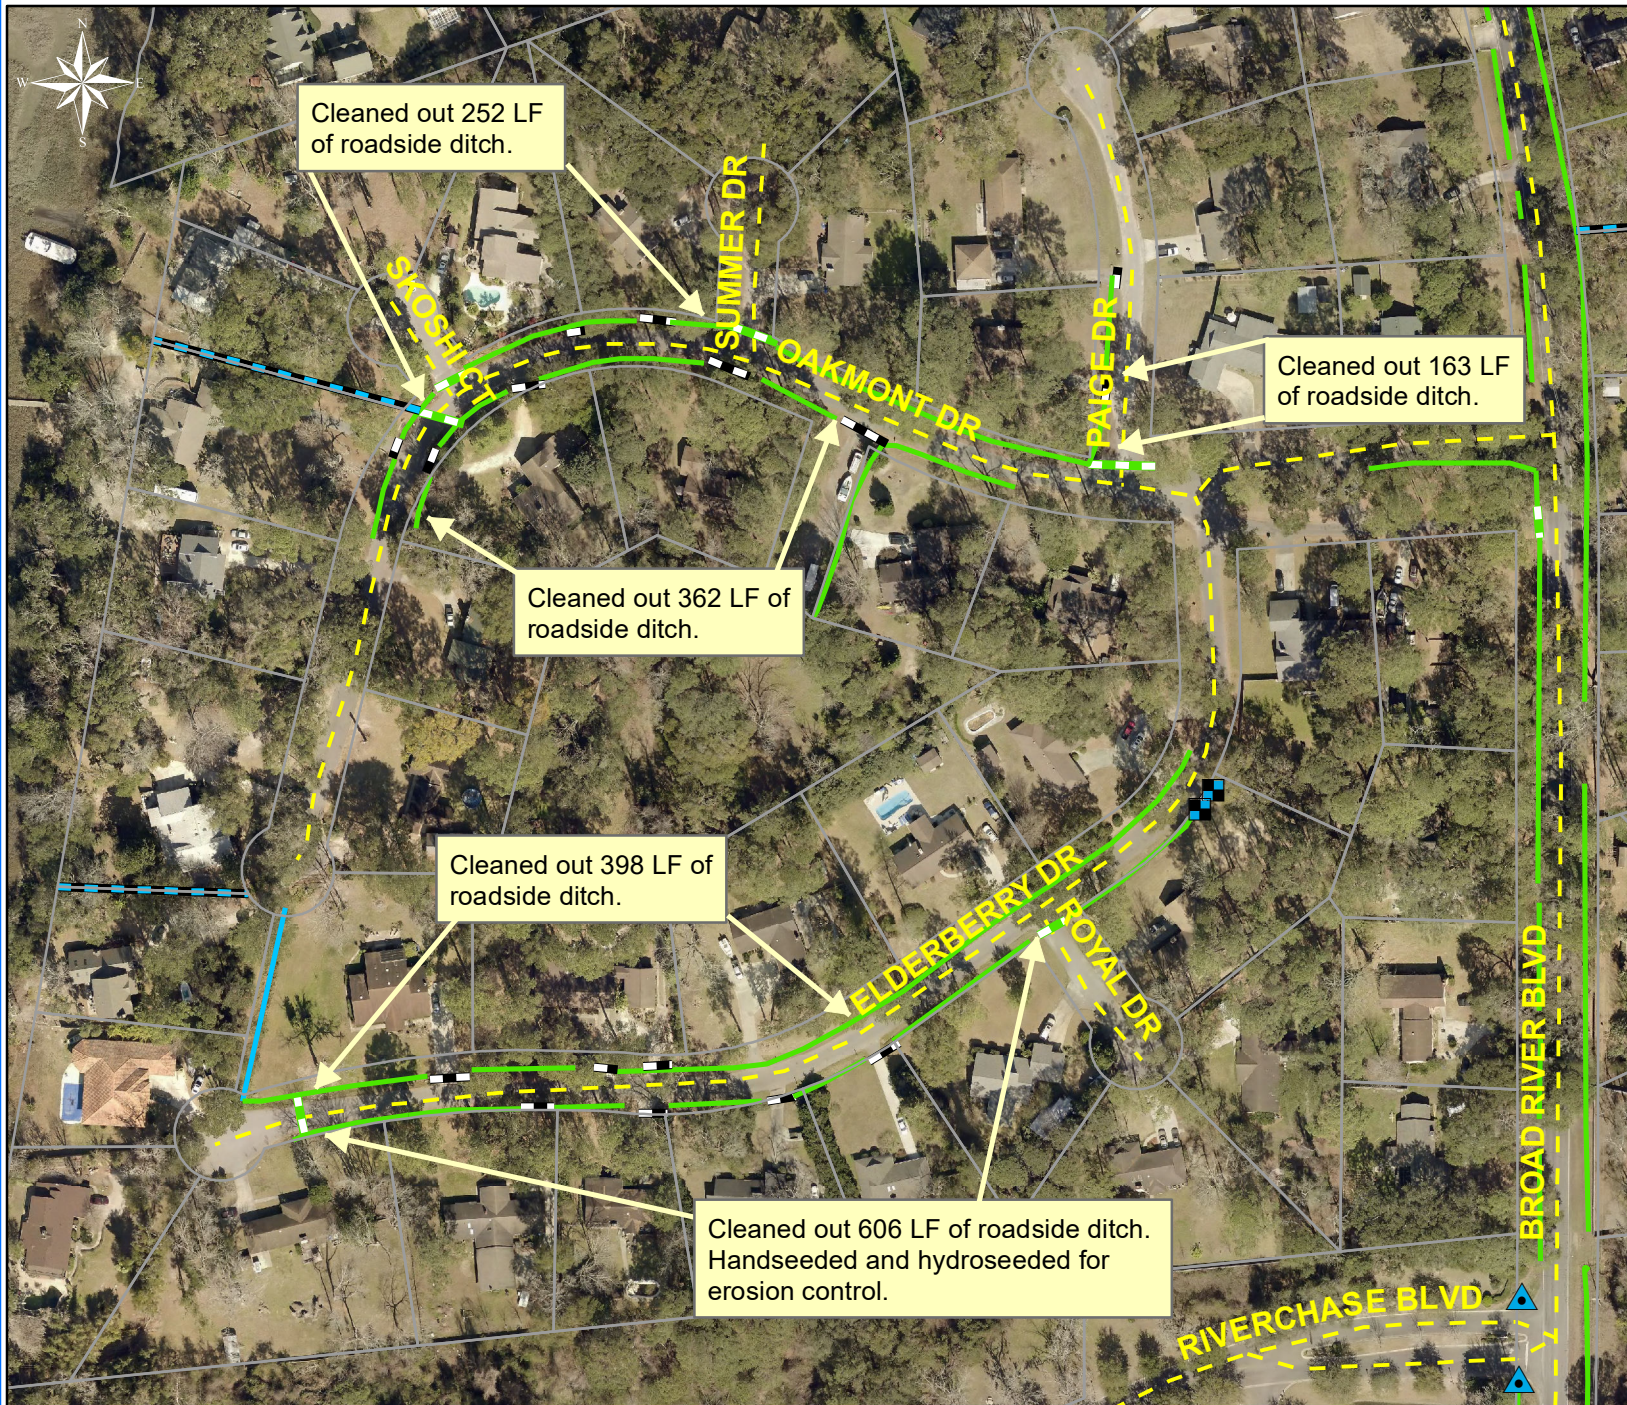

Project: Oakmont
Subdivision
Map #1

Activity: Routine/
Preventive
Maintenance

Project #:
2018-511

Township/SW Dist:
Port Royal Island/6

Completed:
August 2017

Legend

Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 40 80 160 240 320
Feet

1 inch = 170 feet

Prepared By: BC Stormwater Management Utility

Date Print: 01/16/18

File: C:\project summaries map\Oakmont Subdivision Map #1_2018-511



Project: Oakmont
Subdivision
Map #2

Activity: Routine/
Preventive
Maintenance

Project #:
2018-511

Township/SW Dist:
Port Royal Island/6

Completed:
August 2017

Legend

Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 30 60 120 180 240
Feet

1 inch = 130 feet

Prepared By: BC Stormwater Management Utility

Date Print: 01/16/18

File: C:\project summaries map\Oakmont Subdivision Map #2_2018-511
