

Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: Bay Pines Drive

Activity: Routine/Preventive Maintenance Duration: 01/14/20-02/28/20

Narrative Description of Project:

Project improved 987 L.F. of drainage system. Cleaned out 759 L.F. of roadside ditch. Jetted 10 driveway pipes and 228 L.F. of roadside pipe. Hydroseeded for erosion control.

2020-019A / Bay Pines Drive	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	2.0	\$43.58	\$0.00	\$0.00	\$0.00	\$0.00	\$43.58
DLO / Ditch Layout	24.0	\$500.40	\$23.34	\$29.97	\$0.00	\$158.76	\$712.47
DPJT / Driveway Pipe - Jetted	22.0	\$490.16	\$421.52	\$105.70	\$0.00	\$315.48	\$1,332.86
HAUL / Hauling	35.0	\$791.60	\$495.60	\$151.23	\$0.00	\$514.95	\$1,953.38
HYDR / Hydroseeding	16.0	\$334.88	\$51.53	\$849.99	\$0.00	\$0.00	\$1,236.40
LP / Locate Pipe	40.0	\$834.00	\$38.90	\$21.30	\$0.00	\$264.60	\$1,158.80
RSDCL / Roadside Ditch - Cleanout	136.0	\$2,842.44	\$505.03	\$137.76	\$0.00	\$830.43	\$4,315.66
RSPJ / Roadside Pipe - Jetted	14.0	\$311.92	\$268.24	\$61.12	\$0.00	\$200.76	\$842.04
UC / Utility Coordination	2.0	\$49.40	\$0.00	\$0.00	\$0.00	\$26.46	\$75.86
UTLOC / Utility locates	2.0	\$49.40	\$0.00	\$0.00	\$0.00	\$26.46	\$75.86
2020-019A / Bay Pines Drive Sub Total	293.0	\$6,247.78	\$1,804.16	\$1,357.07	\$0.00	\$2,337.90	\$11,746.91
Grand Total	293.0	\$6,247.78	\$1,804.16	\$1,357.07	\$0.00	\$2,337.90	\$11,746.91

Before








After




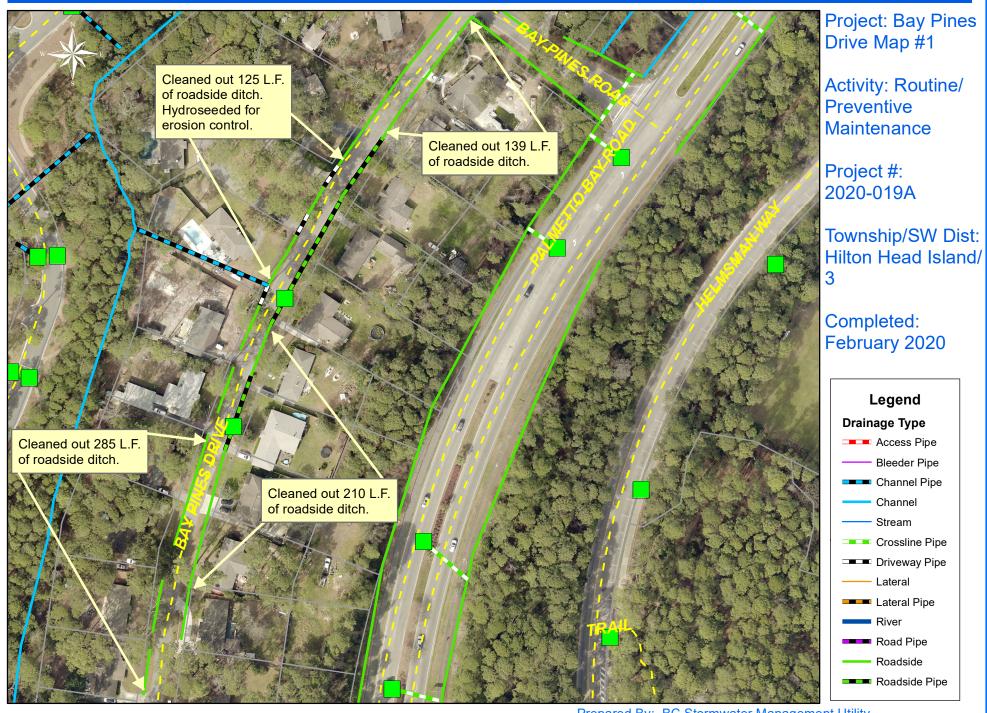

0 30 60 120 180 240

1 inch = 130 feet

Prepared By: BC Stormwater Management Utility Date Print:03/30/20 File:C:\project summaries map/Bay Pines Drive Map #1_2020-019A

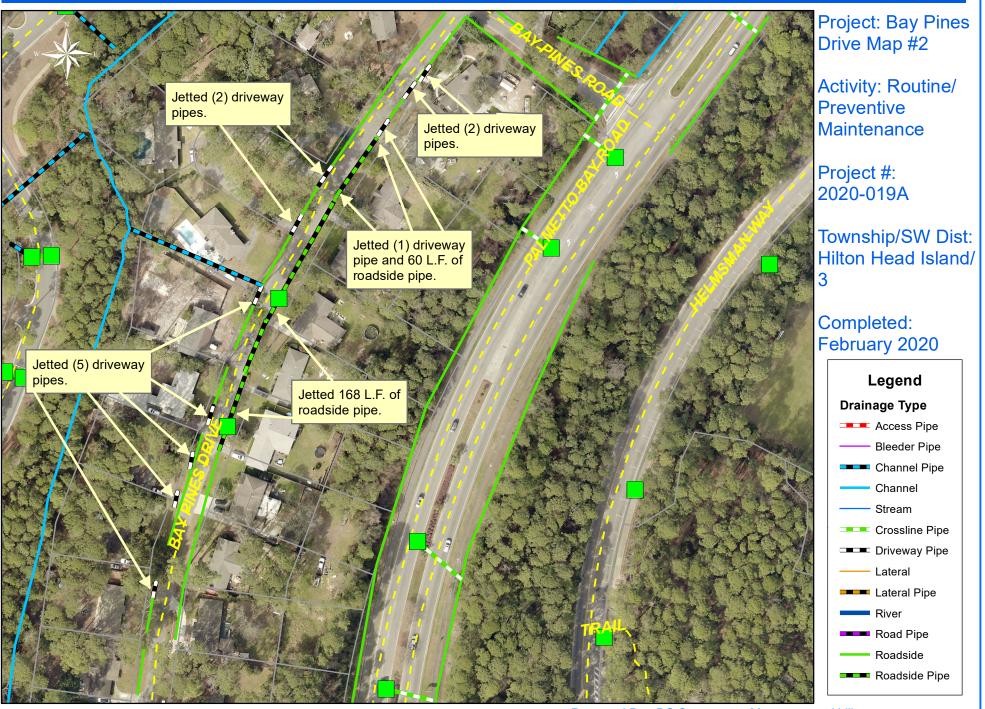

0 30 60 120 180 240 Feet

1 inch = 130 feet

Prepared By: BC Stormwater Management Utility Date Print:03/30/20 File:C:\project summaries map/Bay Pines Drive Map #2_2020-019A
