



Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: St. Helena Island Vacuum Truck - Fairfield Road and Capers Island Circle

Project #: 2010-018

Completed: Aug-09

Narrative Description of Project:

Cleaned out (2) catch basins. Jetted (2) crossline pipes and 16 L.F. of outfall pipe.

Material Cost, Rental Equipment Summary, and Labor

Material	Unit	Cost/Unit	Qty	Cost
Water	gallon	\$0.01	2,100	\$21.00
Diesel	gallon	\$2.37	25.0	\$59.25
Labor	hours		16.0	\$510.58
Total Cost of Materials, Rental Equip., and Labor				\$590.83

Note: Labor cost includes the employee's salary plus fringe benefits.

Equipment Cost

Item	Asset No.	Cost/Hour	Hrs.	Cost
Vacuum Truck	22812	\$20.30	7.0	\$142.10
Total Equipment Cost				\$142.10

Cost/hour excludes fuel cost.

Total Cost: \$732.93

Site Photographs

Before




During



After



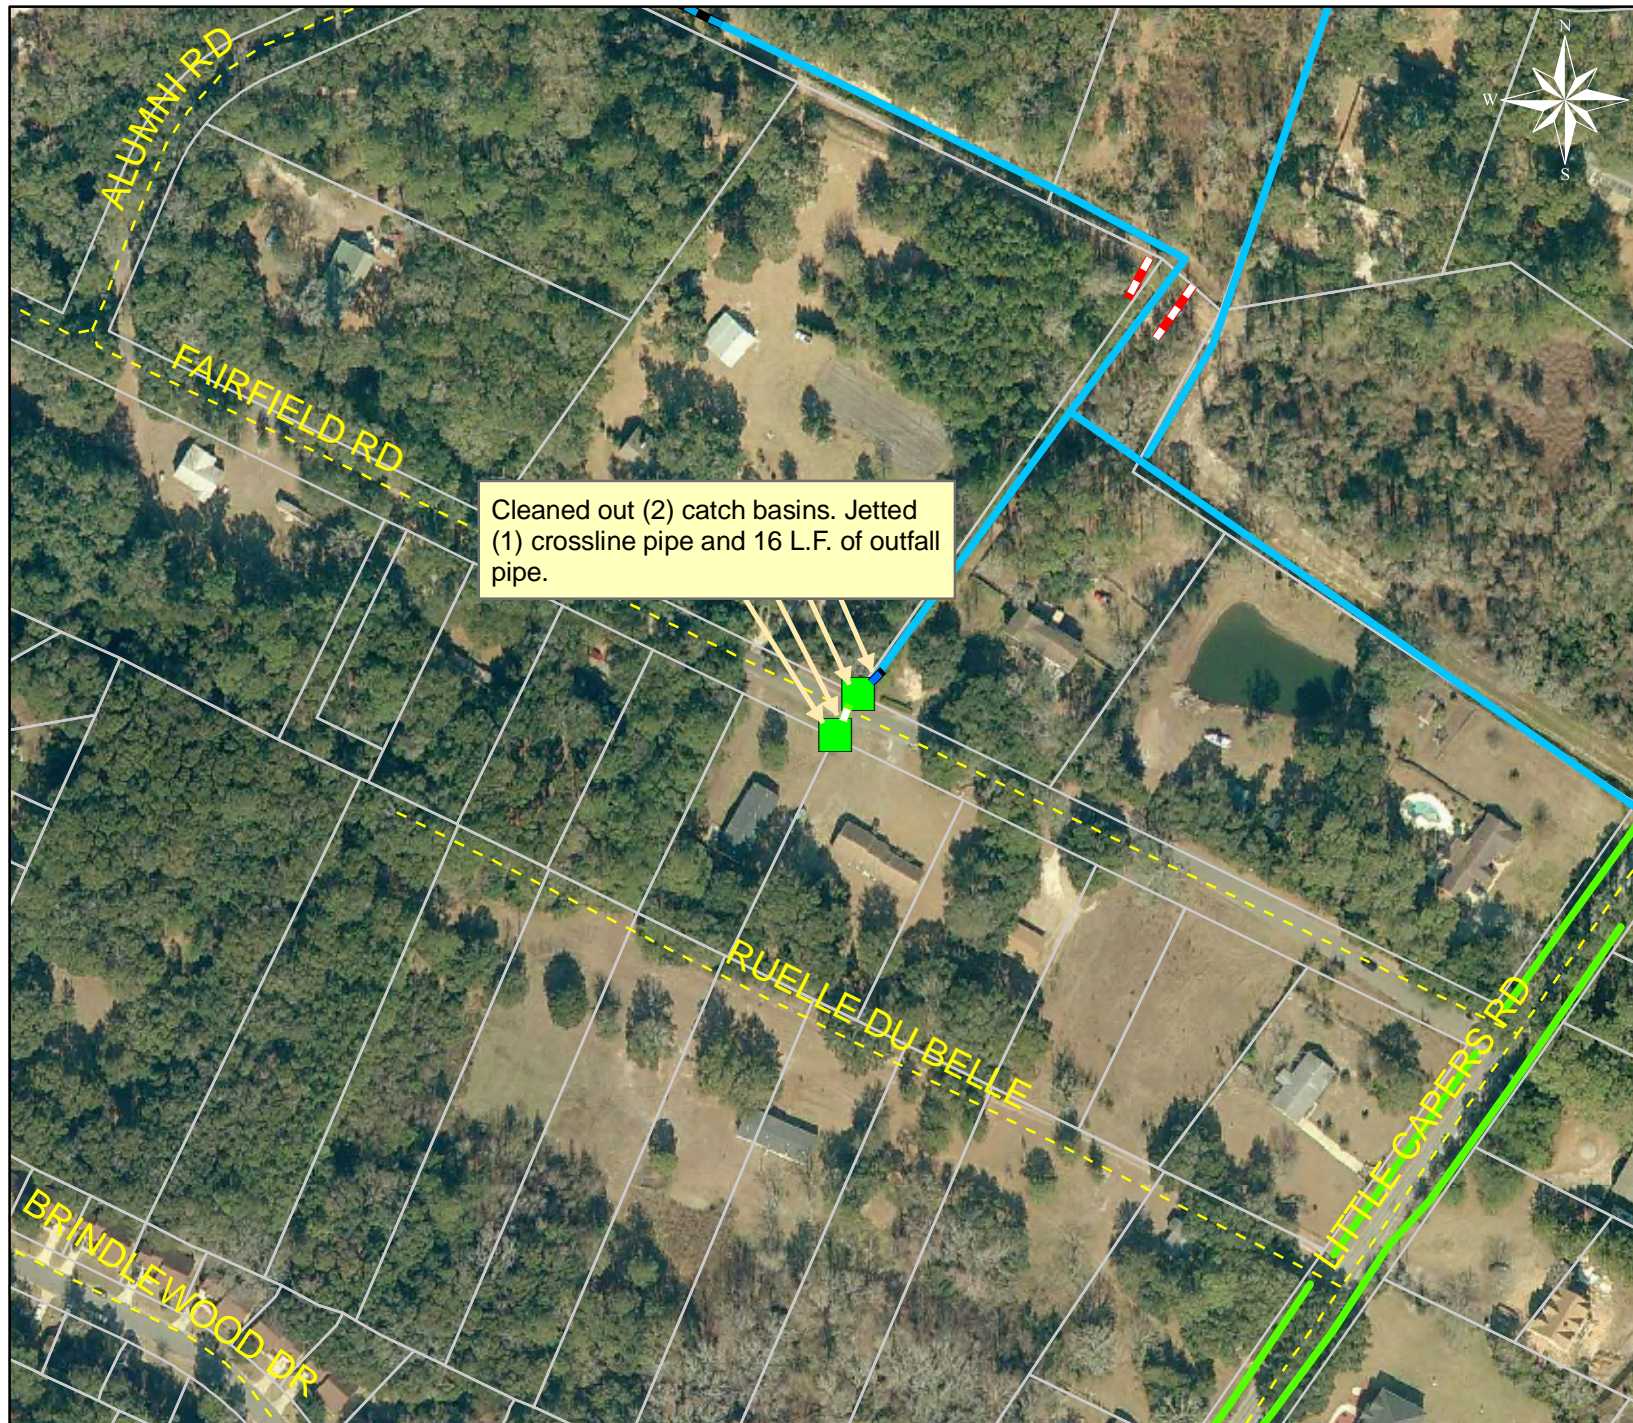

Project: Fairfield Road

Activity: Vacuum Truck












Project #:
2010-018

Township:
St. Helena Island

Completed:
August 2009

Legend

Drainage Type

-  River
-  Stream
-  Outfall
-  Lateral
-  Roadside
-  Crossline
-  D/W
-  Access
-  Piped
-  Bleeder
-  Parcels

0 55 110 220 330 440
Feet

1 inch equals 193.7 feet

Prepared By: BC Stormwater Management Utility

Date Print: 09/08/09

File: C:\project summaries map\St Helena Island Vacuum Truck-Fairfield Road_2010_018



Project: St.Helena
Island Vacuum
Truck - Capers
Island Circle

Activity: Vacuum
Truck

Project #:
2010-054

Township:
St. Helena Island

Completed:
August 2009

Legend

Drainage Type

- River
- Stream
- Outfall
- Lateral
- Roadside
- - - Crossline
- - - D/W
- - - Access
- - - Piped
- Bleeder
- Parcels

0 25 50 100 150 200
Feet

1 inch equals 86.366155 feet

Prepared By: BC Stormwater Management Utility

Date Print:10/12/09

File:C:\project summaries map\Capers Island Circle_2010_054
